Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID		Task Name	Duration	Start	Finish
1		**CIP Concrete**	**10 days**	**Mon 8/24/15**	**Fri 9/4/15**
2		F&P NW Placing Boom Blockouts	10 days	Mon 8/24/15	Fri 9/4/15
3		Shotcrete Southwest	1 day	Mon 8/24/15	Mon 8/24/15
4					
5		**Level 3 PT SW**	**8 days**	**Mon 8/24/15**	**Wed 9/2/15**
6		Stress/Strip	8 days	Mon 8/24/15	Wed 9/2/15
7					
8		**Level 3 SE PT**	**19 days**	**Mon 8/24/15**	**Thu 9/17/15**
9		Layout/Sleeves	2 days	Mon 8/24/15	Tue 8/25/15
10		Rebar/PT	3 days	Wed 8/26/15	Fri 8/28/15
11		Edgeform/Misc	2 days	Mon 8/31/15	Tue 9/1/15
12		Raised Slab edge	2 days	Wed 9/2/15	Thu 9/3/15
13		Inspections	1 day	Thu 9/3/15	Thu 9/3/15
14		Pour	1 day	Fri 9/4/15	Fri 9/4/15
15		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
16					
17		**Wood Framing L3**	**13 days**	**Mon 8/24/15**	**Wed 9/9/15**
18		**North**	**3 days**	**Mon 8/24/15**	**Wed 8/26/15**
19		TJI Joists	3 days	Mon 8/24/15	Wed 8/26/15
20		Deck	2 days	Tue 8/25/15	Wed 8/26/15
21		**Southwest**	**13 days**	**Mon 8/24/15**	**Wed 9/9/15**
22		Frame	6 days	Mon 8/24/15	Mon 8/31/15
23		TJI/Joist	5 days	Tue 9/1/15	Mon 9/7/15
24		Deck	4 days	Fri 9/4/15	Wed 9/9/15
25					
26		**Level 4 North**	**10 days**	**Tue 9/1/15**	**Mon 9/14/15**
27		Frame	10 days	Tue 9/1/15	Mon 9/14/15
28					
29		**Fire Sprinkler**	**10 days**	**Mon 8/24/15**	**Fri 9/4/15**
30		Mains North Garage	10 days	Mon 8/24/15	Fri 9/4/15
31					
32		**Garage**	**15 days**	**Mon 8/24/15**	**Fri 9/11/15**
33		MEP RI LP/ 1	15 days	Mon 8/24/15	Fri 9/11/15
34					

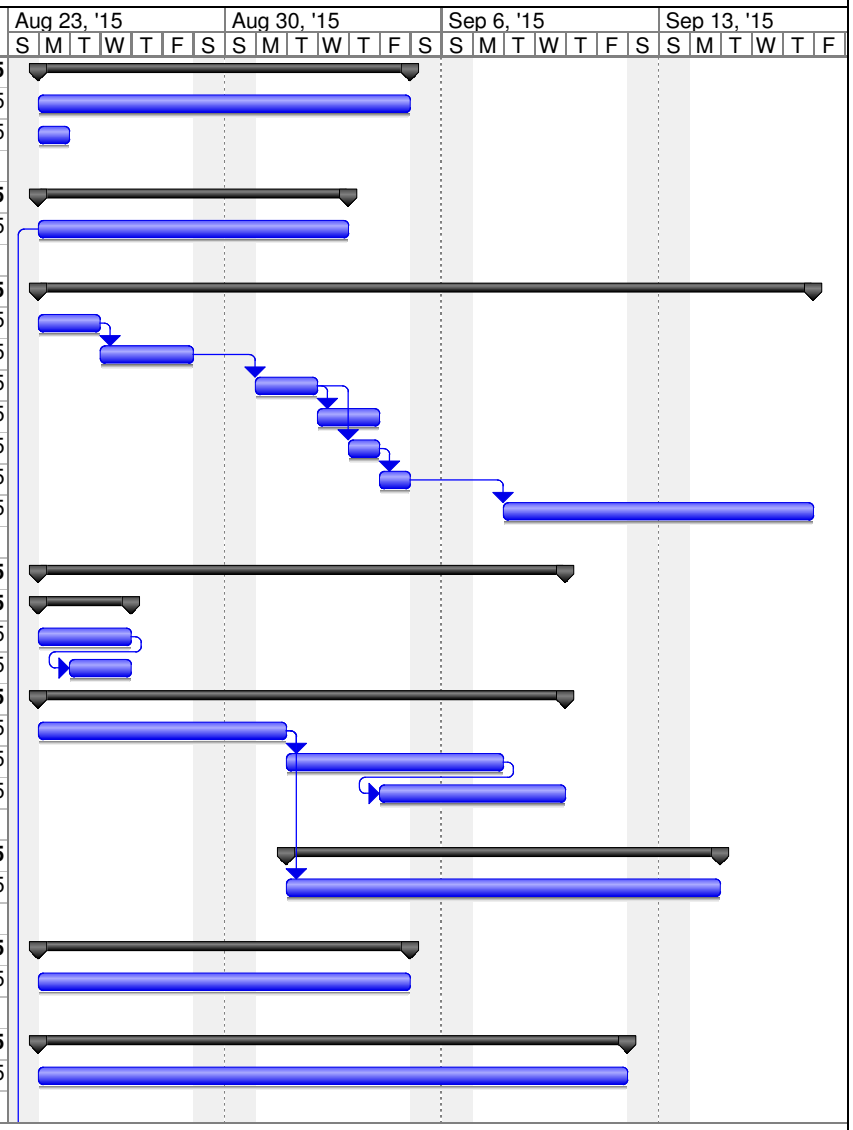

Project: 3wk look ahead 8-24-15
Date: Fri 8/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-17-2015

ID		Task Name	Duration	Start	Finish
35		**Mtl Stud Framing**	**14 days**	**Mon 8/24/15**	**Thu 9/10/15**
36		Level P	3 days	Mon 8/24/15	Wed 8/26/15
37		Stair 1 Exterior	4 days	Mon 8/24/15	Thu 8/27/15
38		Level 2 Units Etc. North	10 days	Fri 8/28/15	Thu 9/10/15
39					
40		**Waterproofing**	**4 days**	**Mon 8/24/15**	**Thu 8/27/15**
41		West wall	1 day	Mon 8/24/15	Mon 8/24/15
42		Blockouts/Tiebacks	3 days	Tue 8/25/15	Thu 8/27/15
43					
44		**Subgrade**	**4 days**	**Tue 8/25/15**	**Fri 8/28/15**
45		Shoring Support	4 days	Tue 8/25/15	Fri 8/28/15
46					
47		**Shoring**	**8 days**	**Mon 8/24/15**	**Wed 9/2/15**
48		Drill/Set Additional Piles	4 days	Wed 8/26/15	Mon 8/31/15
49		Lagging @ Corner	2 days	Mon 8/24/15	Tue 8/25/15
50		Additional Shoring Lagging	4 days	Fri 8/28/15	Wed 9/2/15
51					
52		**West Shoring walls**	**4 days**	**Tue 9/1/15**	**Fri 9/4/15**
53		Weld Nelson studs	1 day	Tue 9/1/15	Tue 9/1/15
54		Reinforcing	2 days	Wed 9/2/15	Thu 9/3/15
55		Shotcrete	1 day	Fri 9/4/15	Fri 9/4/15

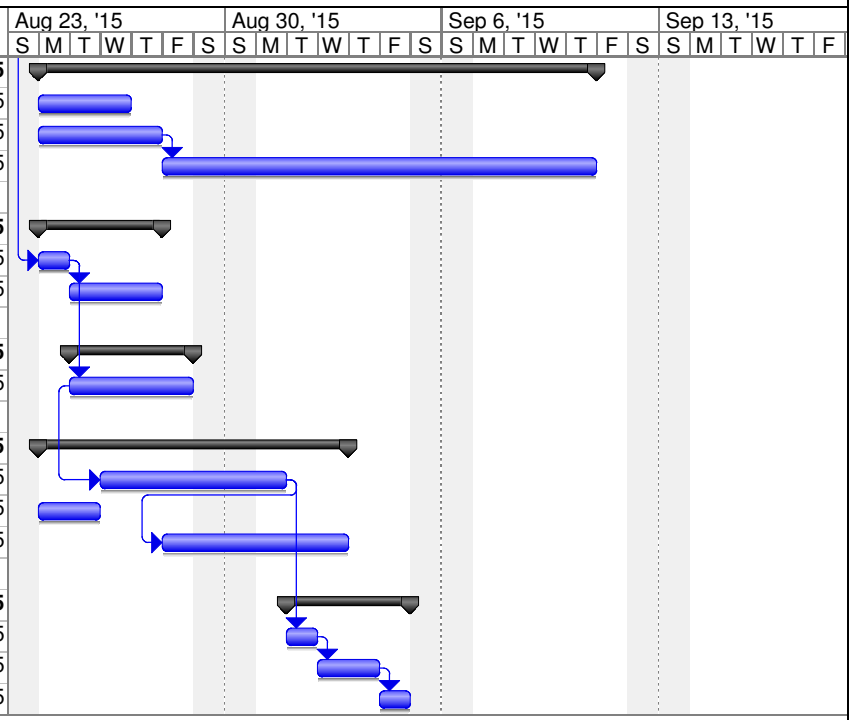

Project: 3wk look ahead 8-24-15
Date: Fri 8/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
