Hadley Mixed use
Legacy
3 wk Look ahead
8-3-2015

ID		Task Name	Duration	Start	Finish
1		**Instreet Utilities**	**5 days**	**Mon 8/3/15**	**Fri 8/7/15**
2		Sanitary South	1 day	Mon 8/3/15	Mon 8/3/15
3		PSE In Street Conduit	5 days	Mon 8/3/15	Fri 8/7/15
4					
5		**CIP Concrete**	**7 days**	**Mon 8/3/15**	**Tue 8/11/15**
6		F&P Remaining L1 South Col's Retail	2 days	Mon 8/3/15	Tue 8/4/15
7		F&P NW Placing Boom Blockouts	5 days	Wed 8/5/15	Tue 8/11/15
8					
9		**Level 2 PT Southeast**	**5 days**	**Mon 8/3/15**	**Fri 8/7/15**
10		Strip	5 days	Mon 8/3/15	Fri 8/7/15
11					
12		**Level 3 PT NE**	**5 days**	**Mon 8/3/15**	**Fri 8/7/15**
13		Strip	5 days	Mon 8/3/15	Fri 8/7/15
14		Remove Reshores North	2 days	Mon 8/3/15	Tue 8/4/15
15					
16		**Level 3 PT SW**	**18 days**	**Mon 8/3/15**	**Wed 8/26/15**
17		Shore/Deck	2 days	Mon 8/3/15	Tue 8/4/15
18		Layout/Sleeves	2 days	Wed 8/5/15	Thu 8/6/15
19		Bottom Mat/Sleeves	2 days	Fri 8/7/15	Mon 8/10/15
20		Edgeform/Misc	2 days	Tue 8/11/15	Wed 8/12/15
21		Raised Slab Edge	2 days	Thu 8/13/15	Fri 8/14/15
22		Inspections	1 day	Thu 8/13/15	Thu 8/13/15
23		Pour	1 day	Fri 8/14/15	Fri 8/14/15
24		Stress/Strip	6 days	Wed 8/19/15	Wed 8/26/15
25					
26		**Level 3 SE PT**	**28 days**	**Mon 8/3/15**	**Wed 9/9/15**
27		Shore/Deck	8 days	Mon 8/3/15	Wed 8/12/15
28		Layout/Sleeves	2 days	Thu 8/13/15	Fri 8/14/15
29		Bottom Mat/Sleeves	2 days	Mon 8/17/15	Tue 8/18/15
30		Edgeform/Misc	2 days	Wed 8/19/15	Thu 8/20/15
31		Raised Slab edge	2 days	Fri 8/21/15	Mon 8/24/15
32		Inspections	1 day	Tue 8/25/15	Tue 8/25/15
33		Pour	1 day	Thu 8/27/15	Thu 8/27/15
34		Stress/Strip	8 days	Mon 8/31/15	Wed 9/9/15

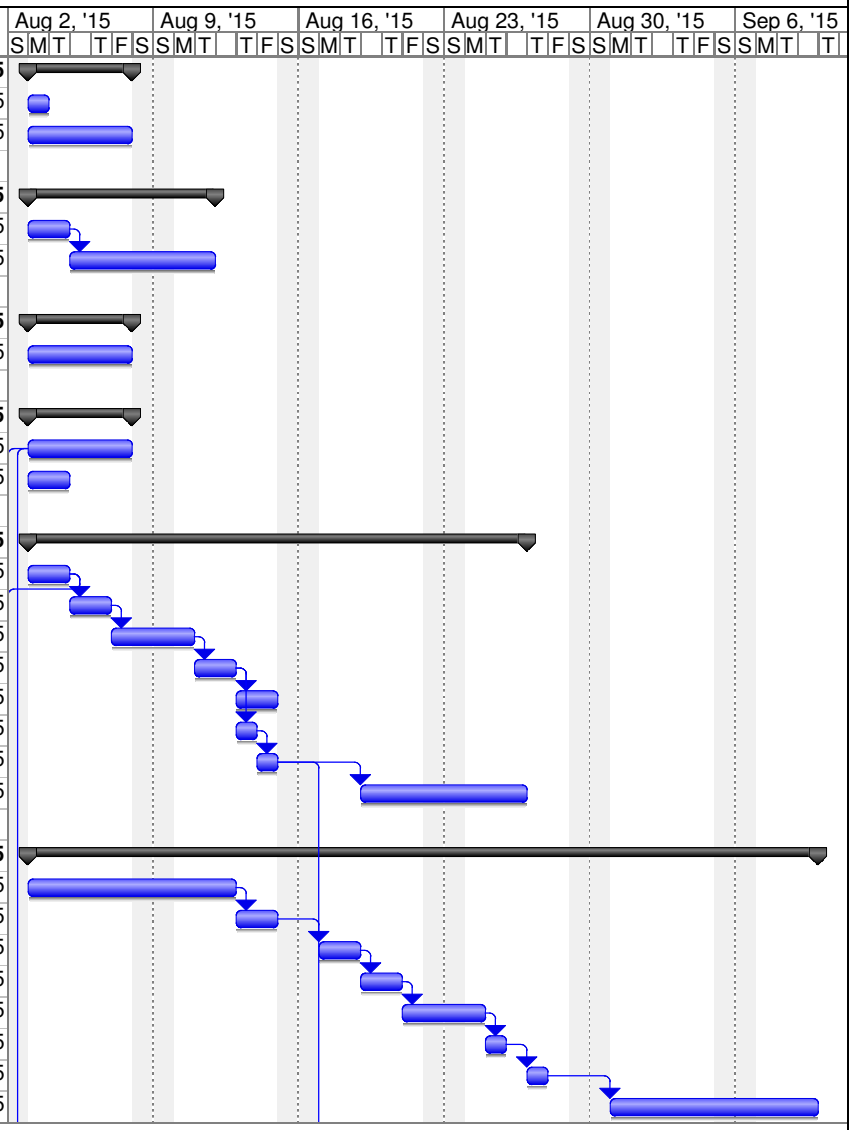

Project: 3wk look ahead 8-3-15
Date: Fri 7/31/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-3-2015

ID		Task Name	Duration	Start	Finish
35					
36		**Wood Framing NW**	**14 days**	**Mon 8/3/15**	**Thu 8/20/15**
37		Layout Walls	1 day	Mon 8/3/15	Mon 8/3/15
38		Frame	5 days	Tue 8/4/15	Mon 8/10/15
39		TJI Joists	4 days	Tue 8/11/15	Fri 8/14/15
40		Deck	4 days	Mon 8/17/15	Thu 8/20/15
41					
42		**Struct Steel**	**3 days**	**Mon 8/3/15**	**Wed 8/5/15**
43		Set Stair 1 LP to L3	3 days	Mon 8/3/15	Wed 8/5/15
44					
45		**Fire Sprinkler**	**2 days**	**Tue 8/4/15**	**Wed 8/5/15**
46		FDC Standpipe to L3	2 days	Tue 8/4/15	Wed 8/5/15
47					
48		**Level P**	**10 days**	**Mon 8/3/15**	**Fri 8/14/15**
49		MEP RI LP	10 days	Mon 8/3/15	Fri 8/14/15
50					
51		**Subgrade**	**4 days**	**Mon 8/17/15**	**Thu 8/20/15**
52		West exterior	4 days	Mon 8/17/15	Thu 8/20/15
53					
54		**Shoring**	**4 days**	**Fri 8/21/15**	**Wed 8/26/15**
55		Drill/Set Addl. Piles	4 days	Fri 8/21/15	Wed 8/26/15

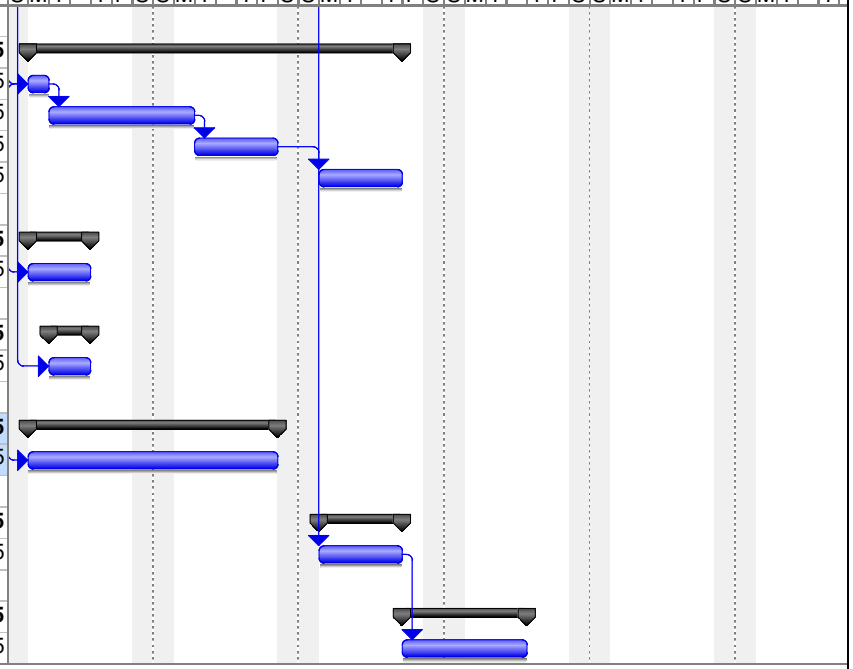

Project: 3wk look ahead 8-3-15
Date: Fri 7/31/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
