Hadley Mixed use
Legacy
3 wk Look ahead
8-31-2015

ID		Task Name	Duration	Start	Finish
1		**CIP Concrete**	**1 day**	**Mon 8/31/15**	**Mon 8/31/15**
2		Shotcrete Southwest	1 day	Mon 8/31/15	Mon 8/31/15
3					
4		**Level 3 PT SW**	**5 days**	**Mon 8/31/15**	**Fri 9/4/15**
5		Strip	5 days	Mon 8/31/15	Fri 9/4/15
6					
7		**Level 3 SE PT**	**14 days**	**Mon 8/31/15**	**Thu 9/17/15**
8		Rebar/PT	1 day	Mon 8/31/15	Mon 8/31/15
9		Edgeform/Misc	1 day	Tue 9/1/15	Tue 9/1/15
10		Raised Slab edge	1 day	Wed 9/2/15	Wed 9/2/15
11		Inspections	1 day	Thu 9/3/15	Thu 9/3/15
12		Pour	1 day	Fri 9/4/15	Fri 9/4/15
13		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
14					
15		**Wood Framing L3**	**18 days**	**Mon 8/31/15**	**Wed 9/23/15**
16		**Southwest**	**5 days**	**Mon 8/31/15**	**Fri 9/4/15**
17		Frame	2 days	Mon 8/31/15	Tue 9/1/15
18		TJI/Joist	3 days	Wed 9/2/15	Fri 9/4/15
19		Deck	2 days	Thu 9/3/15	Fri 9/4/15
20		**Southeast**	**13 days**	**Mon 9/7/15**	**Wed 9/23/15**
21		Frame	9 days	Mon 9/7/15	Thu 9/17/15
22		TJI/Joist	6 days	Fri 9/11/15	Fri 9/18/15
23		Deck	5 days	Thu 9/17/15	Wed 9/23/15
24					
25		**Level 4 North**	**11 days**	**Mon 8/31/15**	**Mon 9/14/15**
26		Frame	10 days	Mon 8/31/15	Fri 9/11/15
27		TJI/Joist	5 days	Mon 9/7/15	Fri 9/11/15
28		Deck	4 days	Wed 9/9/15	Mon 9/14/15
29					
30		**Fire Sprinkler**	**10 days**	**Mon 8/31/15**	**Fri 9/11/15**
31		Mains North Garage	10 days	Mon 8/31/15	Fri 9/11/15
32					
33		**Garage**	**15 days**	**Mon 8/31/15**	**Fri 9/18/15**
34		MEP RI LP/ 1	15 days	Mon 8/31/15	Fri 9/18/15

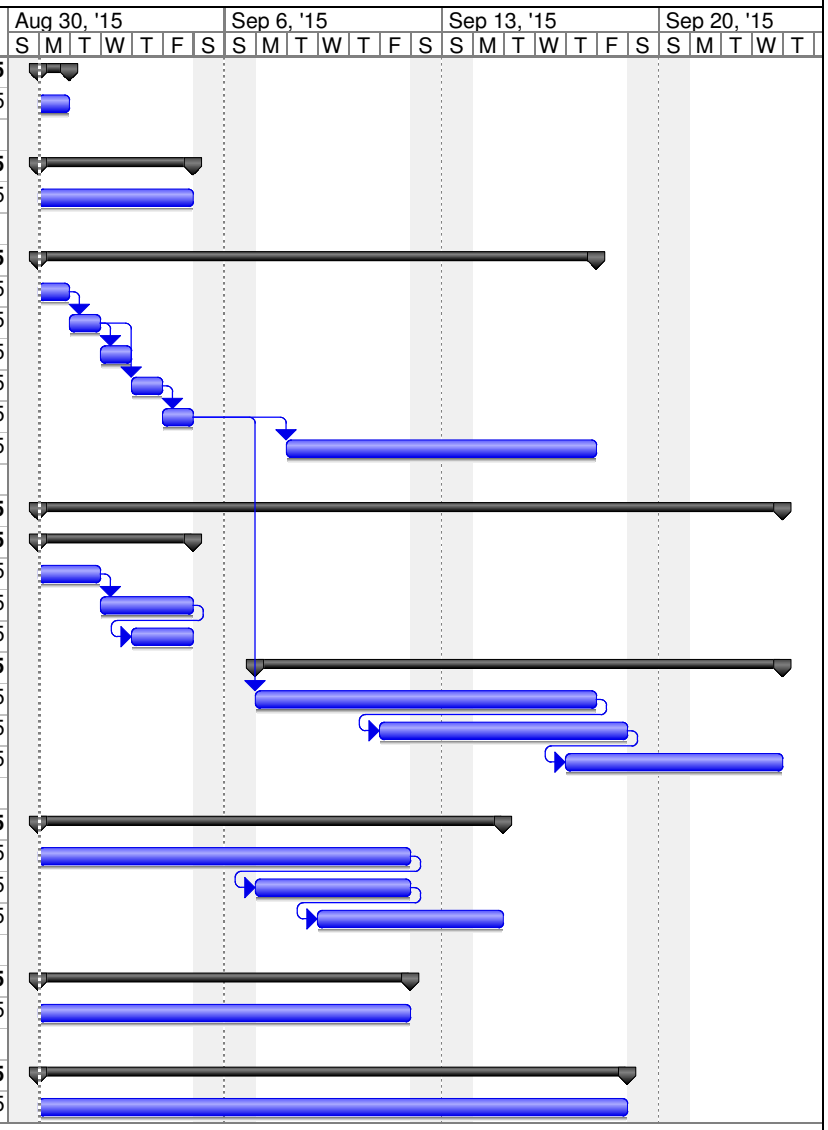

Project: 3wk look ahead 8-31-15
Date: Mon 8/31/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
8-31-2015

ID		Task Name	Duration	Start	Finish
35					
36		**Mtl Stud Framing**	**14 days**	**Mon 8/31/15**	**Thu 9/17/15**
37		Level P	3 days	Mon 8/31/15	Wed 9/2/15
38		Stair 1 Exterior	4 days	Mon 8/31/15	Thu 9/3/15
39		Level 2 Units Etc. North	10 days	Fri 9/4/15	Thu 9/17/15
40					
41		**Waterproofing**	**3 days**	**Mon 8/31/15**	**Wed 9/2/15**
42		Blockouts/Tiebacks	3 days	Mon 8/31/15	Wed 9/2/15
43					
44		**Subgrade**	**8 days**	**Mon 8/31/15**	**Wed 9/9/15**
45		Grade West	4 days	Mon 8/31/15	Thu 9/3/15
46		West Drainage	4 days	Wed 9/2/15	Mon 9/7/15
47		Exc Wall Ftgs	2 days	Tue 9/8/15	Wed 9/9/15
48					
49		**Shoring**	**2 days**	**Mon 8/31/15**	**Tue 9/1/15**
50		Drill/Set Additional Piles	1 day	Mon 8/31/15	Mon 8/31/15
51		Lagging @ Corner	1 day	Tue 9/1/15	Tue 9/1/15
52					
53		**West Shoring walls**	**4 days**	**Wed 9/2/15**	**Mon 9/7/15**
54		Weld Nelson studs	1 day	Wed 9/2/15	Wed 9/2/15
55		Reinforcing	2 days	Thu 9/3/15	Fri 9/4/15
56		Shotcrete	1 day	Mon 9/7/15	Mon 9/7/15

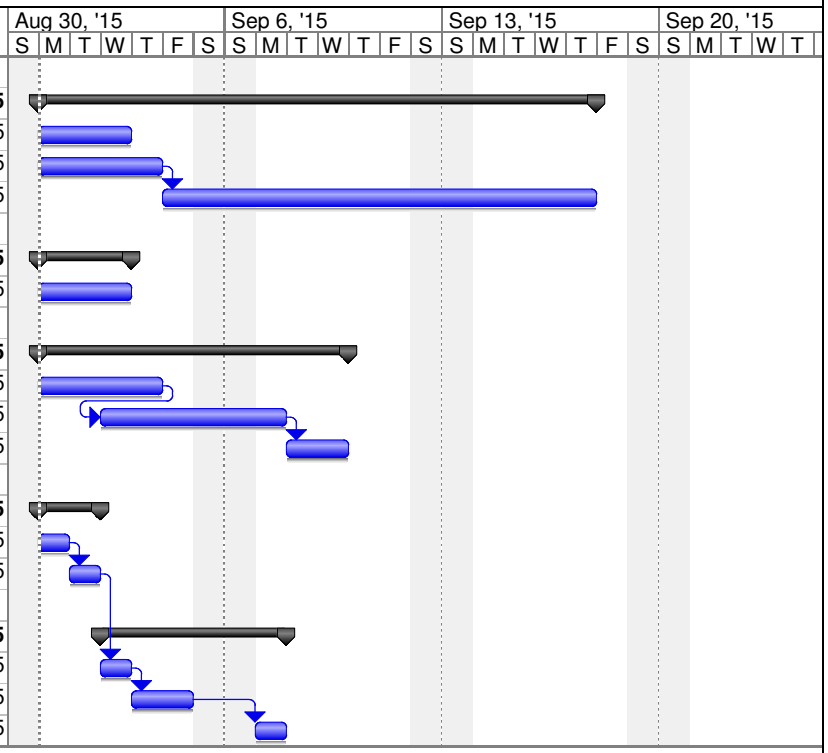

Project: 3wk look ahead 8-31-15
Date: Mon 8/31/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
