Hadley Mixed use
Legacy
3 wk Look ahead
9-14-2015

ID		Task Name	Duration	Start	Finish
1		**Concrete**	**16 days**	**Mon 9/14/15**	**Mon 10/5/15**
2		**Site/Structure**	**16 days**	**Mon 9/14/15**	**Mon 10/5/15**
3		Shotcrete West	4 days	Fri 9/18/15	Wed 9/23/15
4		West Retaing walls	8 days	Thu 9/24/15	Mon 10/5/15
5		Grind/Sack Exterior	15 days	Mon 9/14/15	Fri 10/2/15
6		Pourback Closure	1 day	Thu 9/24/15	Thu 9/24/15
7					
8		**Level 3 SE PT**	**8 days**	**Mon 9/14/15**	**Wed 9/23/15**
9		Strip/Haulout	8 days	Mon 9/14/15	Wed 9/23/15
10					
11		**Wood Framing L3**	**13 days**	**Mon 9/14/15**	**Wed 9/30/15**
12		**Southwest**	**3 days**	**Mon 9/14/15**	**Wed 9/16/15**
13		Roll Joist	3 days	Mon 9/14/15	Wed 9/16/15
14		Sheath	2 days	Tue 9/15/15	Wed 9/16/15
15		**Southeast**	**13 days**	**Mon 9/14/15**	**Wed 9/30/15**
16		Frame	7 days	Mon 9/14/15	Tue 9/22/15
17		Roll Joist	6 days	Fri 9/18/15	Fri 9/25/15
18		Sheath	6 days	Wed 9/23/15	Wed 9/30/15
19					
20		**Level 4 North**	**3 days**	**Mon 9/14/15**	**Wed 9/16/15**
21		Roll Joist	2 days	Mon 9/14/15	Tue 9/15/15
22		Sheath	2 days	Tue 9/15/15	Wed 9/16/15
23					
24		**Level 5 North**	**16 days**	**Wed 9/23/15**	**Wed 10/14/15**
25		Frame	12 days	Wed 9/23/15	Thu 10/8/15
26		Roll Joist	6 days	Fri 10/2/15	Fri 10/9/15
27		Sheath	6 days	Wed 10/7/15	Wed 10/14/15
28					
29		**Fire Sprinkler**	**10 days**	**Mon 9/14/15**	**Fri 9/25/15**
30		Mains North Garage	10 days	Mon 9/14/15	Fri 9/25/15
31					
32		**MEP**	**15 days**	**Mon 9/14/15**	**Fri 10/2/15**
33		MEP RI LP- 1-2	15 days	Mon 9/14/15	Fri 10/2/15
34		L2 South	10 days	Mon 9/21/15	Fri 10/2/15

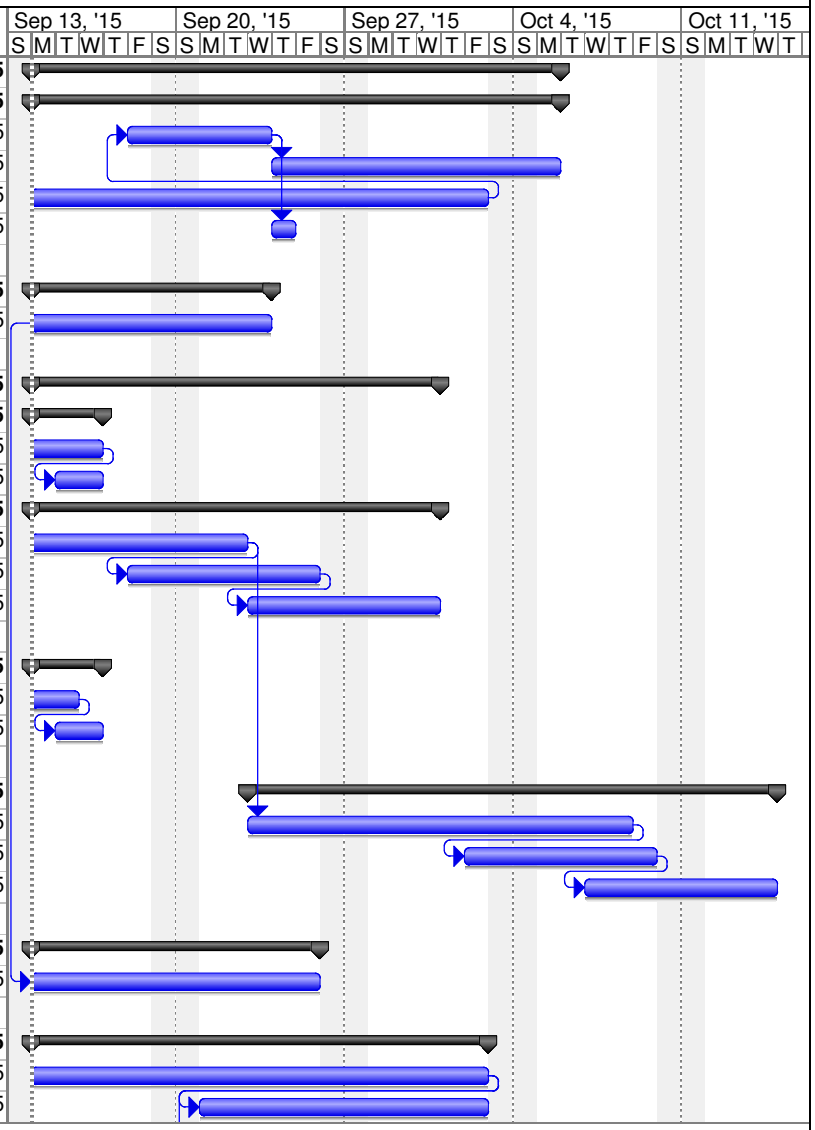

Project: 3wk look ahead 9-14-31 Rev
Date: Mon 9/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-14-2015

ID		Task Name	Duration	Start	Finish
35		Level 3 North	10 days	Mon 9/21/15	Fri 10/2/15
36					
37		**Mtl Stud Framing**	**12 days**	**Mon 9/14/15**	**Tue 9/29/15**
38		Level 2 Units Etc. North	4 days	Mon 9/14/15	Thu 9/17/15
39		Rock Ext walls	8 days	Fri 9/18/15	Tue 9/29/15
40		Level 1-2 South walls	6 days	Fri 9/18/15	Fri 9/25/15
41					
42		**Hollow metal**	**3 days**	**Tue 9/22/15**	**Thu 9/24/15**
43		Deliver	1 day	Tue 9/22/15	Tue 9/22/15
44		Set Frames	2 days	Wed 9/23/15	Thu 9/24/15
45					
46		**Waterproofing**	**4 days**	**Mon 9/14/15**	**Thu 9/17/15**
47		Blockouts/Tiebacks	4 days	Mon 9/14/15	Thu 9/17/15
48					
49		**Subgrade**	**10 days**	**Mon 9/14/15**	**Fri 9/25/15**
50		Grade West	3 days	Mon 9/14/15	Wed 9/16/15
51		West Drainage	2 days	Tue 9/15/15	Wed 9/16/15
52		Exc Wall Ftgs	4 days	Thu 9/17/15	Tue 9/22/15
53		Set Structures/Tie-in	3 days	Wed 9/23/15	Fri 9/25/15

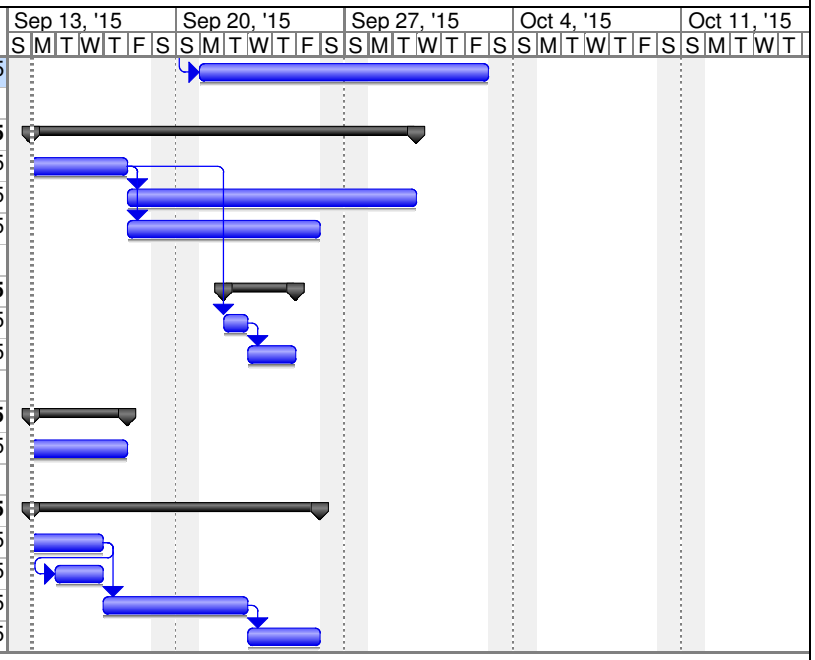

Project: 3wk look ahead 9-14-31 Rev
Date: Mon 9/14/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
