Hadley Mixed use
Legacy
3 wk Look ahead
9-21-2015

ID		Task Name	Duration	Start	Finish
1		**Concrete**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
2		**Site/Structure**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
3		Shotcrete West	3 days	Mon 9/21/15	Wed 9/23/15
4		West Retaing walls	8 days	Mon 9/28/15	Wed 10/7/15
5		Grind/Sack Exterior	15 days	Mon 9/21/15	Fri 10/9/15
6		Pourback Closure	1 day	Mon 9/21/15	Mon 9/21/15
7					
8		**Level 3 SE PT**	**3 days**	**Mon 9/21/15**	**Wed 9/23/15**
9		Strip/Haulout	3 days	Mon 9/21/15	Wed 9/23/15
10					
11		**Wood Framing**	**21 days**	**Mon 9/21/15**	**Mon 10/19/15**
12		**Level 4 SW**	**6 days**	**Mon 9/21/15**	**Mon 9/28/15**
13		Joist	2 days	Mon 9/21/15	Tue 9/22/15
14		Sheath	1 day	Wed 9/23/15	Wed 9/23/15
15					
16		**Level 3 SE**	**6 days**	**Mon 9/21/15**	**Mon 9/28/15**
17		Roll Joist	5 days	Mon 9/21/15	Fri 9/25/15
18		Sheath	4 days	Wed 9/23/15	Mon 9/28/15
19					
20		**Level 5 North**	**16 days**	**Mon 9/21/15**	**Mon 10/12/15**
21		Frame	10 days	Mon 9/21/15	Fri 10/2/15
22		Roll Joist	8 days	Mon 9/28/15	Wed 10/7/15
23		Sheath	6 days	Mon 10/5/15	Mon 10/12/15
24					
25		**Level 5 SW**	**14 days**	**Thu 9/24/15**	**Tue 10/13/15**
26		Frame	8 days	Thu 9/24/15	Mon 10/5/15
27		Roll Joist	6 days	Thu 10/1/15	Thu 10/8/15
28		Sheath	5 days	Wed 10/7/15	Tue 10/13/15
29					
30		**Level 4 SE**	**15 days**	**Tue 9/29/15**	**Mon 10/19/15**
31		Frame	8 days	Tue 9/29/15	Thu 10/8/15
32		Roll Joist	7 days	Tue 10/6/15	Wed 10/14/15
33		Sheath	5 days	Tue 10/13/15	Mon 10/19/15
34					

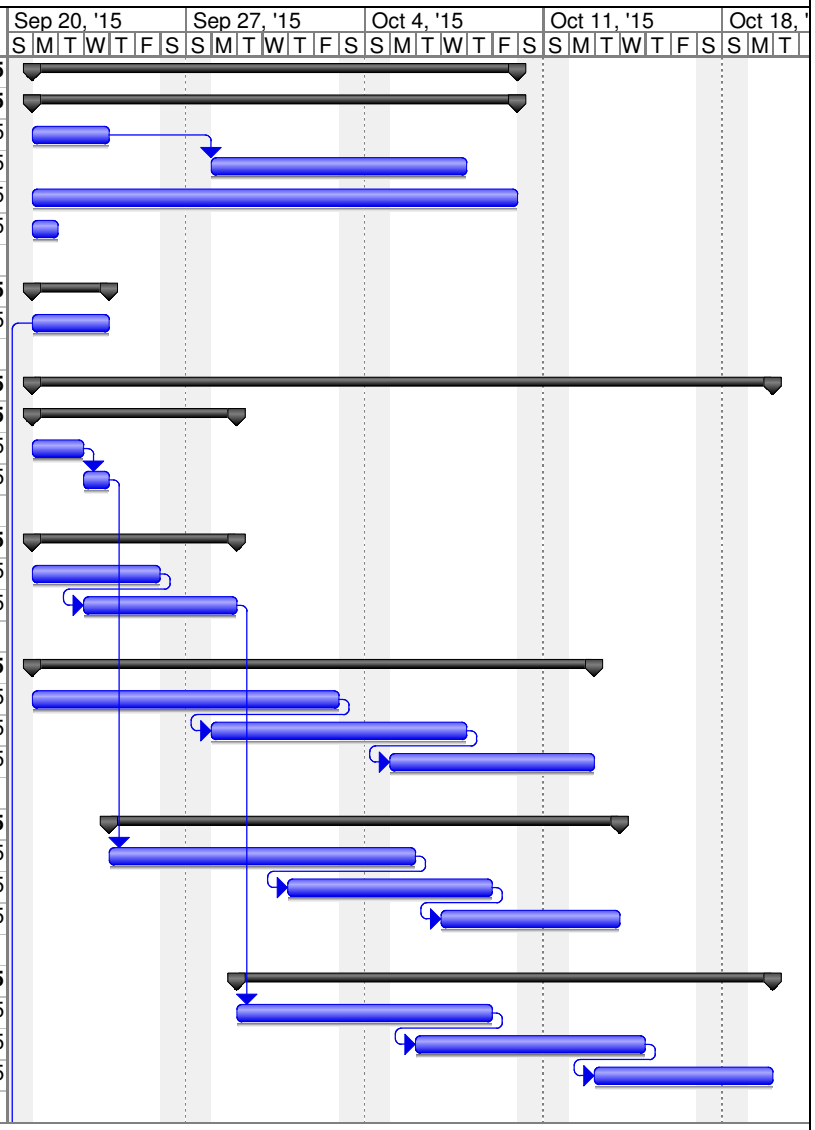

Project: 3wk look ahead 9-21-31 Rev
Date: Fri 9/18/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-21-2015

ID	Task Name	Duration	Start	Finish
35	**Fire Sprinkler**	**10 days**	**Mon 9/21/15**	**Fri 10/2/15**
36	Mains North Garage	10 days	Mon 9/21/15	Fri 10/2/15
37				
38	**MEP**	**15 days**	**Mon 9/21/15**	**Fri 10/9/15**
39	MEP RI LP- 1-2	15 days	Mon 9/21/15	Fri 10/9/15
40	L2 South	10 days	Mon 9/28/15	Fri 10/9/15
41	Level 3 North	10 days	Mon 9/28/15	Fri 10/9/15
42				
43	**Mtl Stud Framing**	**12 days**	**Mon 9/21/15**	**Tue 10/6/15**
44	Level 2 Units Ext. North	4 days	Mon 9/21/15	Thu 9/24/15
45	Rock Ext walls	8 days	Fri 9/25/15	Tue 10/6/15
46	Level 1-2 South walls	6 days	Fri 9/25/15	Fri 10/2/15
47				
48	**Hollow metal**	**3 days**	**Tue 9/29/15**	**Thu 10/1/15**
49	Deliver	1 day	Tue 9/29/15	Tue 9/29/15
50	Set Frames	2 days	Wed 9/30/15	Thu 10/1/15
51				
52	**Waterproofing**	**4 days**	**Mon 9/21/15**	**Thu 9/24/15**
53	Blockouts/Tiebacks	4 days	Mon 9/21/15	Thu 9/24/15
54				
55	**Subgrade**	**8 days**	**Mon 9/21/15**	**Wed 9/30/15**
56	Grade West	3 days	Mon 9/21/15	Wed 9/23/15
57	West Drainage	4 days	Tue 9/22/15	Fri 9/25/15
58	Exc Wall Ftgs	4 days	Thu 9/24/15	Tue 9/29/15
59	Set Structures/Tie-in	3 days	Mon 9/28/15	Wed 9/30/15

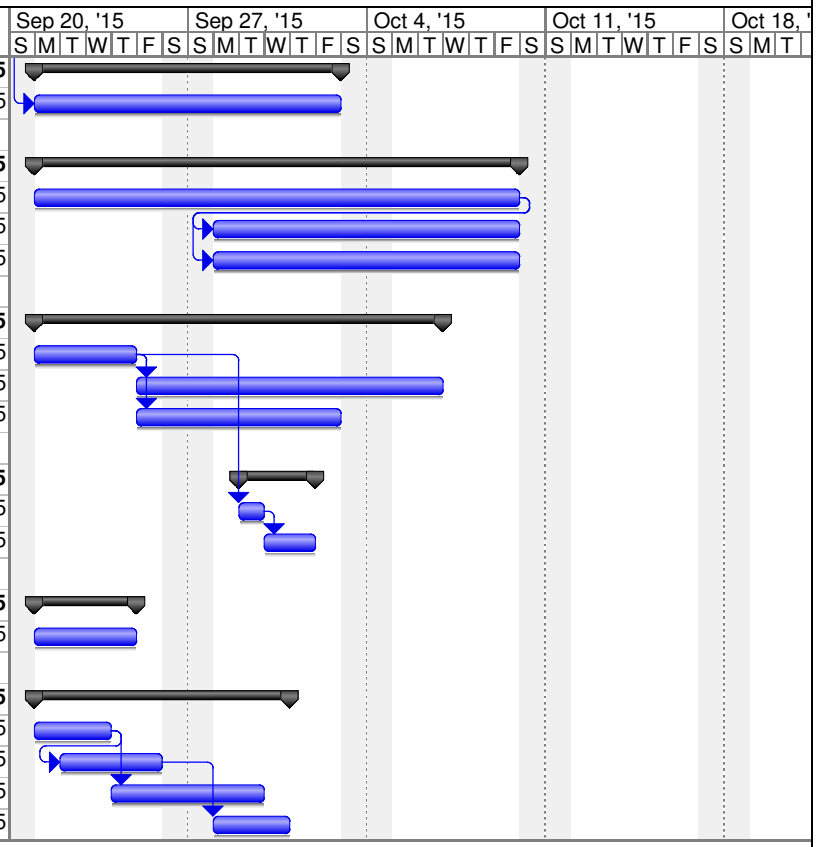

Project: 3wk look ahead 9-21-31 Rev
Date: Fri 9/18/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
