Hadley Mixed use
Legacy
3 wk Look ahead
9-28-2015

ID		Task Name	Duration	Start	Finish
1		**Site/Structure**	**18 days**	**Mon 9/28/15**	**Wed 10/21/15**
2		**West**	**8 days**	**Mon 9/28/15**	**Wed 10/7/15**
3		F&P Retaing walls	8 days	Mon 9/28/15	Wed 10/7/15
4		**North**	**10 days**	**Thu 10/8/15**	**Wed 10/21/15**
5		Retaining Walls	10 days	Thu 10/8/15	Wed 10/21/15
6		Mech Shaft	5 days	Thu 10/15/15	Wed 10/21/15
7		**South**	**5 days**	**Wed 9/30/15**	**Tue 10/6/15**
8		F&P Planters	5 days	Wed 9/30/15	Tue 10/6/15
9					
10		**Wood Framing**	**15 days**	**Mon 9/28/15**	**Fri 10/16/15**
11		**Level 4 SW**	**2 days**	**Mon 9/28/15**	**Tue 9/29/15**
12		Joist	2 days	Mon 9/28/15	Tue 9/29/15
13		Sheath	1 day	Mon 9/28/15	Mon 9/28/15
14					
15		**Level 5 North**	**6 days**	**Mon 9/28/15**	**Mon 10/5/15**
16		Roll Joist	5 days	Mon 9/28/15	Fri 10/2/15
17		Sheath	6 days	Mon 9/28/15	Mon 10/5/15
18					
19		**Level 5 SW**	**12 days**	**Tue 9/29/15**	**Wed 10/14/15**
20		Frame	6 days	Tue 9/29/15	Tue 10/6/15
21		Roll Joist	6 days	Fri 10/2/15	Fri 10/9/15
22		Sheath	5 days	Thu 10/8/15	Wed 10/14/15
23					
24		**Level 4 SE**	**15 days**	**Mon 9/28/15**	**Fri 10/16/15**
25		Frame	8 days	Mon 9/28/15	Wed 10/7/15
26		Roll Joist	7 days	Mon 10/5/15	Tue 10/13/15
27		Sheath	5 days	Mon 10/12/15	Fri 10/16/15
28					
29		**Fire Sprinkler**	**10 days**	**Wed 9/30/15**	**Tue 10/13/15**
30		Mains North Garage Level 1	10 days	Wed 9/30/15	Tue 10/13/15
31					
32		**MEP**	**15 days**	**Mon 9/28/15**	**Fri 10/16/15**
33		MEP RI LP- 1-2	15 days	Mon 9/28/15	Fri 10/16/15
34		L2 South	10 days	Mon 10/5/15	Fri 10/16/15

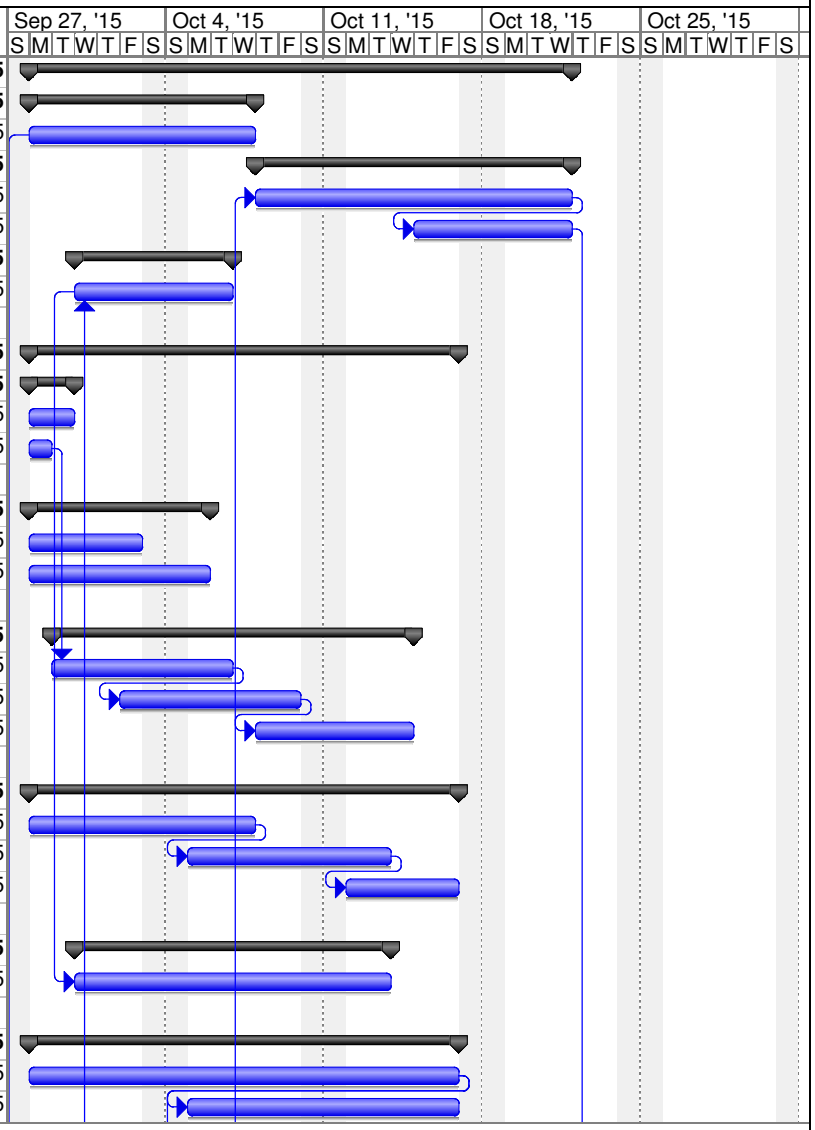

Project: 3wk look ahead 9-28-15
Date: Fri 9/25/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-28-2015

ID	Task Name	Duration	Start	Finish
35	Level 3 Risers	10 days	Mon 10/5/15	Fri 10/16/15
36				
37	**Mtl Stud Framing**	**10 days**	**Mon 9/28/15**	**Fri 10/9/15**
38	Rock Ext walls	8 days	Mon 9/28/15	Wed 10/7/15
39	Level 1-2 South walls	6 days	Fri 10/2/15	Fri 10/9/15
40				
41	**Hollow metal**	**6 days**	**Thu 10/1/15**	**Thu 10/8/15**
42	Deliver	1 day	Thu 10/1/15	Thu 10/1/15
43	Set Frames	5 days	Fri 10/2/15	Thu 10/8/15
44				
45	**Waterproofing**	**2 days**	**Mon 9/28/15**	**Tue 9/29/15**
46	Blockouts/Tiebacks	2 days	Mon 9/28/15	Tue 9/29/15
47				
48	**Sitework Subgrade**	**25 days**	**Mon 9/28/15**	**Fri 10/30/15**
49	**West**	**9 days**	**Mon 9/28/15**	**Thu 10/8/15**
50	Grade	2 days	Mon 9/28/15	Tue 9/29/15
51	West Drainage	4 days	Mon 9/28/15	Thu 10/1/15
52	Exc Wall Ftgs	1 day	Mon 9/28/15	Mon 9/28/15
53	Backfill Walls	2 days	Fri 10/2/15	Mon 10/5/15
54	Cap Break @ Patio's/Sidewalks	3 days	Tue 10/6/15	Thu 10/8/15
55				
56	**South**	**15 days**	**Mon 9/28/15**	**Fri 10/16/15**
57	Patial Backfill	2 days	Mon 9/28/15	Tue 9/29/15
58	Cut/Cap Mains	4 days	Tue 10/13/15	Fri 10/16/15
59				
60	**North**	**19 days**	**Tue 10/6/15**	**Fri 10/30/15**
61	Subgrade	3 days	Tue 10/6/15	Thu 10/8/15
62	Exc Wall Ftgs	2 days	Fri 10/9/15	Mon 10/12/15
63	Set Manhole/Piping	4 days	Tue 10/13/15	Fri 10/16/15
64	Backfill Walls	3 days	Thu 10/22/15	Mon 10/26/15
65	Cap Break Sidewalks/Stairs	4 days	Tue 10/27/15	Fri 10/30/15

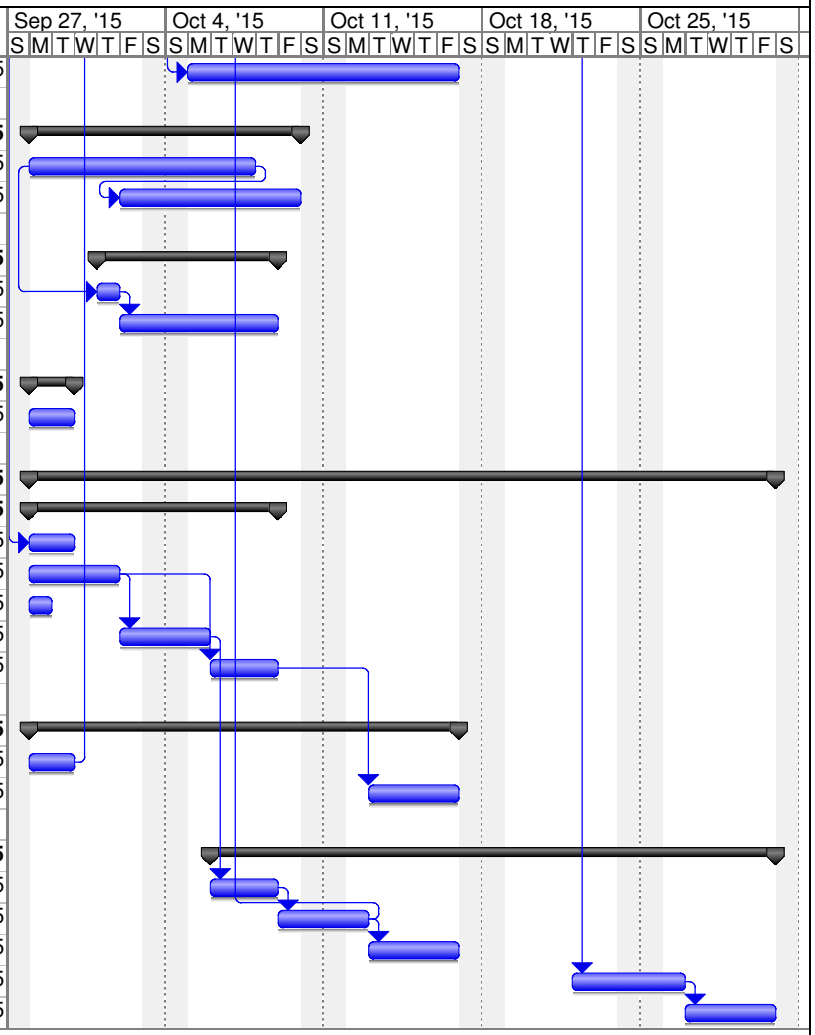

Project: 3wk look ahead 9-28-15
Date: Fri 9/25/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
