Hadley Mixed use
Legacy
3 wk Look ahead
9-8-2015

ID		Task Name	Duration	Start	Finish
1		**Level 3 SE PT**	**8 days**	**Tue 9/8/15**	**Thu 9/17/15**
2		Stress/Strip	8 days	Tue 9/8/15	Thu 9/17/15
3					
4		**Wood Framing L3**	**15 days**	**Tue 9/8/15**	**Mon 9/28/15**
5		**Southwest**	**5 days**	**Tue 9/8/15**	**Mon 9/14/15**
6		Frame	2 days	Tue 9/8/15	Wed 9/9/15
7		Roll Joist	3 days	Thu 9/10/15	Mon 9/14/15
8		Sheath	2 days	Fri 9/11/15	Mon 9/14/15
9		**Southeast**	**13 days**	**Thu 9/10/15**	**Mon 9/28/15**
10		Frame	9 days	Thu 9/10/15	Tue 9/22/15
11		Roll Joist	6 days	Wed 9/16/15	Wed 9/23/15
12		Sheath	5 days	Tue 9/22/15	Mon 9/28/15
13					
14		**Level 4 North**	**8 days**	**Tue 9/8/15**	**Thu 9/17/15**
15		Frame	4 days	Tue 9/8/15	Fri 9/11/15
16		Roll Joist	3 days	Fri 9/11/15	Tue 9/15/15
17		Sheath	4 days	Mon 9/14/15	Thu 9/17/15
18					
19		**Fire Sprinkler**	**10 days**	**Tue 9/8/15**	**Mon 9/21/15**
20		Mains North Garage	10 days	Tue 9/8/15	Mon 9/21/15
21					
22		**Garage**	**15 days**	**Tue 9/8/15**	**Mon 9/28/15**
23		MEP RI LP/ 1	15 days	Tue 9/8/15	Mon 9/28/15
24					
25		**Mtl Stud Framing**	**14 days?**	**Tue 9/8/15**	**Fri 9/25/15**
26		Level P	3 days	Tue 9/8/15	Thu 9/10/15
27		Stair 1 Exterior	4 days	Tue 9/8/15	Fri 9/11/15
28		Level 2 Units Etc. North	10 days	Mon 9/14/15	Fri 9/25/15
29		Rock Ext walls	1 day?	Tue 9/8/15	Tue 9/8/15
30					
31		**Hollow metal**	**3 days**	**Tue 9/22/15**	**Thu 9/24/15**
32		Deliver	1 day	Tue 9/22/15	Tue 9/22/15
33		Set Frames	2 days	Wed 9/23/15	Thu 9/24/15
34					

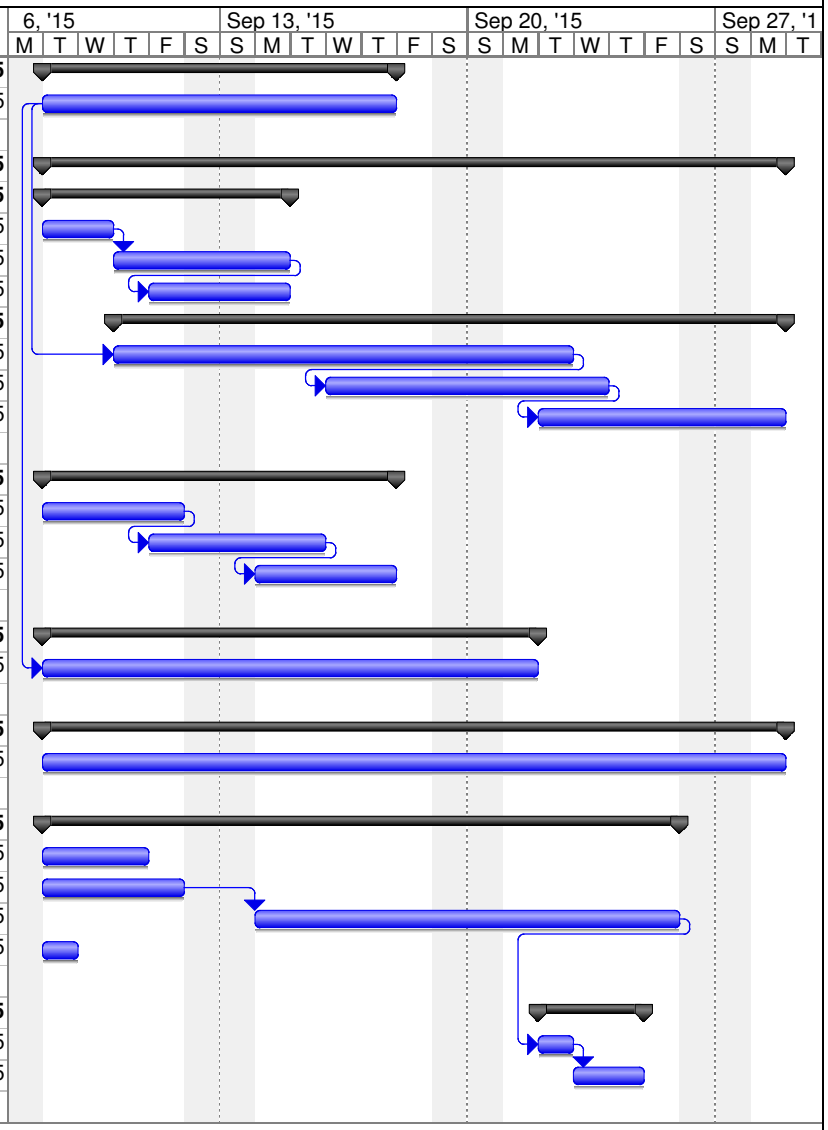

Project: 3wk look ahead 9-8-31 Rev 1
Date: Wed 9/2/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
9-8-2015

ID		Task Name	Duration	Start	Finish
35		**Waterproofing**	**4 days**	**Tue 9/8/15**	**Fri 9/11/15**
36		Blockouts/Tiebacks	4 days	Tue 9/8/15	Fri 9/11/15
37					
38		**Subgrade**	**6 days**	**Tue 9/8/15**	**Tue 9/15/15**
39		Grade West	4 days	Tue 9/8/15	Fri 9/11/15
40		West Drainage	4 days	Thu 9/10/15	Tue 9/15/15
41		Exc Wall Ftgs	2 days	Mon 9/14/15	Tue 9/15/15
42					
43		**West Shoring walls**	**4 days**	**Mon 9/14/15**	**Thu 9/17/15**
44		Weld Nelson studs	1 day	Mon 9/14/15	Mon 9/14/15
45		Reinforcing	2 days	Tue 9/15/15	Wed 9/16/15
46		Shotcrete	1 day	Thu 9/17/15	Thu 9/17/15

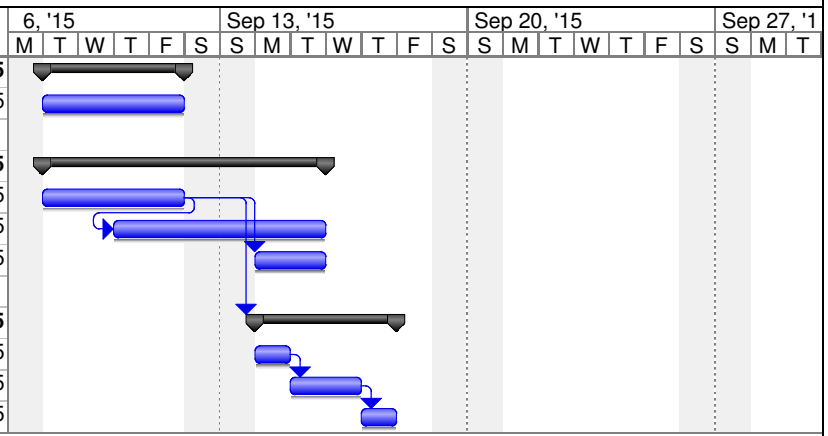

Project: 3wk look ahead 9-8-31 Rev 1
Date: Wed 9/2/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
