CHINN CONSTRUCTION, LLC

CONSTRUCTION MEETING MINUTES

PROJECT: **Hadley Project / Legacy Mercer Island – Mixed Use**

LOCATION: **Legacy Office**

MEETING #: **16**

MEETING DATE: **03/03/15**

ATTENDEES:
~~Steffenie Evans – Legacy~~
~~Kerry Nicholson Legacy~~
~~Parker Nicholson – Legacy~~
Roger Sawicki –Legacy
Darcy Perrault – VIA
~~Kevin Chinn – CHINN~~
Mike Kalvelage – CHINN
Mark Pesanti - CHINN
Charlie Poggemann – CHINN
Lauren Bjorndahl – CHINN
Richard Donelson – One Way Plumbing
Brett Mortimore – One Way Plumbing

SAFETY: LNI will be onsite on 03/04/15 for a consultation

SCHEDULE:

04.02 **3 Week Look Ahead:**

- 03/02-03/06 – Excavate footings M line/entry; 03/02-03/04 backfill/grade NW; 03/03 export contaminated soil South; 03/02-03/06 Pipe trenching NW; 03/05-03/12 Vapor Barrier/Cap Break NW; 03/13-03/0319 backfill/grade NE; 03/18-03/24 Pipe Trenching NE; 03/23-03/26 Vapor Barrier/Cap Break NE
- 03/06-03/10 clean and prep walls for EPRO; 03/11 Apply EPRO system
- 03/09-03/10 Domestic/Fire Roughin to FC Room
- 03/02-03/19 Underslab piping, NWand NE Storm/Slab Drainage, Entry Trance Drain
- 03/02-03/30 CIP Concrete; F&P Footings NE Level P, F&P B Line Wall, F&P walls /Columns Level P NE, 03/12 Pour SOG West/Ramp, Sawcut, Form for perimeter for SOG Elev 98, 03/27 Pour SOG NE, Sawcut, L1 Deck Shoring NW

OLD BUSINESS:

01.14 **Contaminated Soils:** Coordination meetings with Farallon, Legacy, CHINN, Earthwork, Geopier and Shoring Subcontractors to review soil protocols.

- 02/24/15: CHINN to sort through Republic and Waste Management Log for final pricing
- 03/02/15: CHINN pulling back up. RS to get updated Waste Management Log

01.15 **CD Drawings:** CD set will have all comments from the city. One set of CD drawings will be issued with the clouds showing for costing purposes. One set of non-clouded drawings will be issued for construction purposes.

- 10/28/2014: Drawings downloaded and being distributed by CHINN to construction team.

- 12/02/14: Pricing for Waterproofing, Fire Sprinklers, Roofing needed so that revisions to City of MI may be submitted. After revisions are submitted VIA will release construction drawings. Target date for pricing is 12/12/14.
- 12/09/14: CHINN will try to have a ROM for the changes to the plans by 12/12/14.
- 12/16/14: CP provided ROM for waterproofing which was much higher than anticipated. CP to define scope changes for Legacy to review w/ A/E team.
- 12/23/14: CHINN to finish pricing revisions the 15th of January.
- 01/06/15: DP requested target dates to submit to the city and produce CD's.
- 01/13/15 Waterproofing pricing was submitted. CHINN needs Waterproofing sign off. Roofing pricing with framing and sprinkler contractor. This week review joists above Amenity with RSIC's.
- 01/20/15 Sprinkler ROM is $125k, Tapered TJIs $59k, LB to schedule meeting for Roof Design Exercise for 1/23 at 10:00 am.
- 01/27/15: CHINN expects revised roofing number 1/27; wood framed crickets are not shown on base bid documents; CHINN to get pricing on flat TJIs (not tapered)
- 02/03/15: Pending pricing
- 02/10/15: Estimated credit for going to flat TJIs is approx. $92k. CHINN to review if credit offsets the tapered insulation cost. R-value of the roof insulation is 32.5, R-value of Roof assembly G2000 is 33.89.
- 02/17/15: Price pending
- 02/24/15: WRB spec has changed, CHINN to do research and bring findings to next meeting.
- 03/03/15: REV12 specs call for a 10 year Tyvek warranty. CHINN to price per CD specs and an add for the REV12 specs. RP Ownership would like this to be wrapped up, so VIA can submit to the COMI formally. CHINN Changes are not clouded in the specfications.

01.20 **Vista Switch and Permanent Power:** PSE needs to decide a location for the Vista Switch.

- 10/28/2014: Chinn to coordinate pre-con for permanent power with IEC and PSE.
- 11/11/14: IEC is coordinating with PSE/ Poetelco.
- 12/02/2014: CHINN to schedule an onsite meeting to coordinate temp power, vista switch and permanent power.
- 12/09/14: Roger to arrange a meeting with PSE for 12/19/14. CHINN to coordinate electrician.
- 12/23/14: PSE to decide Vista Switch location base. RS will follow up with PSE
- 01/13/15: RS to schedule meeting with PSE for 1/16/15.
- 01/20/15: Per meeting with PSE and RS, power needs to run under sidewalk along 76th Ave to NE corner of property. Additionally, the street crossing will need to be opened up at NE corner. Not resolved.
- 01/27/15: RS has reached out to PSE
- 02/03/15: RS, CHINN, and Electrical subcontractor continue to reach out. Requesting routing and transformer power model number.
- 02/10/15: Received preliminary plan from PSE. Key information is missing. Legacy Partners to coordinate meeting with utilities and players.
- 02/17/15: Coordination is ongoing.
- 02/24/15: Team went to City this morning. Vaults and Vista will not be in the ROW. Landscaping will be displaced.
- 03/03/15; RS to contact PSE (Infrasource) regarding gas. OWP will be installing approx.. 6 pipes adjacent to loading dock bay for future tenants.

02.06 **MEP Coordination:** DP requested that Chinn coordinate an electrical coordination meetings as soon as we have HVAC signed on.

- 12/02/14: CP hopes to have HVAC on board by 12/05/14. Target date for MEP coordination meeting before Christmas.

- 12/09/14: CFM was chosen for HVAC. C & R was chosen for low volt. CHINN will have a MEP coordination meeting before Christmas.
- 12/16/14: CHINN to schedule coordination meeting this week for the 1st week of January.
- 12/23/14: MEP coordination meeting to be on 01/13/15
- 01/06/15: CHINN to coordinate MEP meeting for Tuesday 1/13/15 at 1pm.
- 01/13/15: Preliminary MEP coord meeting held today. Review overlays in 2 ½ weeks
- 01/20/15: Legacy received feedback regarding Commercial space power. Legacy to email comments to CHINN for Electrical subcontractor response.
- 01/27/15: CHINN to schedule coordination meeting for Low Voltage and Electrical unit layout
- 02/03/15: CHINN brought a preliminary set of low voltage shop drawings for mark ups. CHINN to provide quantities for card readers.
- 02/17/15: MEP coordination held today. Issue with 2x6 staggered stud shear walls that are also plumbing walls.
- 02/24/15: DP Strapping was going to be added to the 2x6 walls and the sill plate was the conern.
- 03/03/15: DP to check with Acoustical Engineer regarding adding hat channel on 2x6 wall (no stagger). CHINN to price furnish and install of stud shoe. (Per unit cost). Review mag hold opens and doors if wall changes.

02.07 **AC Units:** SE would like some options and pricing to add AC units. She would like pricing for installed units vs. a price for just venting and electrical hook up.

- 12/02/14: CP provided ROM of $500 a unit including vent, hood and dedicate 120v/ 20 amp circuits. Legacy is reviewing.
- 12/16/14: Legacy requested CHINN to provide a formal proposal.
- 01/13/15: CHINN working with a siding contractor
- 01/20/15: Unit G, x46 stack of apartments will not have hoods and option for AC.
- 02/03/15: Electrical subcontractor quoted $60 per unit for a 20 amp circuit and breaker.

02.08 **Buyout:** RS would like Chinn to focus on buy out for roofing, framing and waterproofing. These were the major revisions to the CD set.

- 12/02/14: CP hopes to have pricing by 12/12/14.
- 01/13/15: Close to releasing Framing, Siding, and Deck subcontracts.
- 02/17/15: Scaffolding
- 02/24/15: Scaffolding and siding in the same package
- 03/03/15: Window install, Storefronts, Hardi Siding and Metal panels

04.07 **Neighbors Work:** Chinn to get samples, and pricing of fencing from McFabco. Chinn to get pricing for soldier pile extension at SW corner. Legacy to Grant about design, i.e. whether or not we remove the Jersey barriers and fence options. Per Owner Agreement with neighbor, all work must be completed by end of January.

- 12/09/14: CHINN to get fencing samples by 12/16/14.
- 12/16/14: CHINN to provide pricing based on design idea present by Mark.
- 01/06/14: CHINN is awarding PO to McFabco. They are pricing the metal, and making a mockup drawing. CHINN has purchased the wood.
- 01/13/15: SE waiting for a response if the neighbor wants the fence back up.
- 01/13/15: SE to help CHINN coordinate Jersey Barrier Removal
- 01/20/15: Legacy requested pricing to continue fence to the corner
- 01/27/15: Legacy do not remove jersey barrier; RS build fence and step it to meet 42" height at south end only.
- 02/03/15: Steel supplier working on options.
- 02/10/15: LB delivered perforated steel and expanded steel options.

- 02/17/15: Pile extensions have been ordered and a ROM is $1,600.00. CHINN to check with deck subcontractor for metal screen samples going on the decks.
- 02/24/15: Pile extensions have been delivered to the site. LB getting a welder on board.
- 03/03/15: Welder is on board. CHINN to schedule work. LB to receive a sample of screen this week. LP requested that pile extensions occur without delay.

05.02 **Comcast:** Comcast asked for drawings. They are performing offsite work soon in preparation for this project. Legacy to reach out to Comcast.

- 01/13/15: SE to reach out again.
- 02/03/15: Comcast wants fiber all of the way to the units. DAS system will need backbone up to roof. After coordination meeting with C&R, may require (4) – 2" conduits to roof.
- 02/10/15: Legacy Partners requested pricing to run fiber to the units from MDF. Closets may need to be bigger.

06.02 **SW Corner Stability:** At the South West corner of the site, the grade from the lagging pile to the existing rockery is very steep. Richard from Terrecon looked at it today and suggested it could be unsafe. Confirming RFI to be written by CHINN. Terrecon will respond with direction.

- 12/23/14: RFI answer to extend four piles; - Closed
- 01/06/15: RS requested CO
- 01/13/15: MP noted drawings and actual slope need to be coordinated before this item can be closed out.
- 01/20/15: RS/SE to schedule a coordinate meeting for 1/23.
- 02/10/15: It is going to be more difficult to remove and work around items surrounded by bracing.
- 02/24/15: CHINN to respond to email from Shannon Wilson (Geotech) peer review.
- 03/03/15: CHINN responded, risk of damage to waterline from movement of the adjacent excavation is low.

08:05 **West Property Line Design Coordination:** RS suggested holding a design coordination meeting to clarify and define the scope of work along the west property line. RS noted that a portion of the budget was earmarked for this work. CP asked why it was not an allowance.

- 02/03/15: Meeting scheduled for 2/10.
- 02/10/15: Revised drawings to be issued 02/27/15
- 02/17/15: LP to check in with Landscape Architect and address
- 02/24/15: New Sheets L2.5 and L2.6 were distributed for review.
- 03/03/15: L2.7 and L2.8 were received later. VIA to send proposal to LP for walls. Drainage at the North, South, and West walls needs to be addressed by CPL.

09.06 **Grease Shaft/lining and Grease Trap for future tenant:** Provide Power and grease shaft for future

- 01/27/15: Need power or raceway requirements; price for shaft wall assembly
- 03/03/15: Electrician has included (2) ¾" conduit for future; CHINN to submit pricing.

09.07 **Grease Trap for Future** Tenant: coordinate accessible location for grease trap maintenance.

- 01/20/15: Send Big Dipper and Trap Zilla information to SE
- 01/27/15: LB provided printed information of different models (hanging, in-ground, and floor mounted)
- 02/03/15: Legacy reviewed maintenance data, ok to put an in ground grease trap.

09.08 **Sheet EN 2.00 8" pipe up through Level P** – Need to coordinate route for 8" vent from Level P to Roof

- Plumbing subcontractor to propose a route to DP
- 02/24/15: The fan motor size needs to be specified on the blower for the depressurization system under ground.
- 03/03/15: One way plumbing proposed two routes. Route changed to closet, needs shaft enclosure.

13.04 **Monitoring Wells coordinating with Farallon as Required –** It is acceptable to place a Waste Management container for monitoring well spoils.

14.04 **LP Make efforts to demobilize Clearwater**

14.05 **Does LP want to install drains that come through the shotcrete walls to tie into garage in the storm system at North, West, and South Walls?**

- 03/03/15: RP It was discussed that another round of coordination is needed based on the content of new information provided by Brumbaugh and Associates. The need to accommodate for planter drains is still needed.

15.05 **Acoustical Engineer to review Room 106 since dwelling units are above**

15.06 **Value Engineering option for siding type CF-1 to go to stucco**

SUBCONTRACTOR BUYOUT STATUS:

16.01 Subcontractor buyout status is based on % of dollar value.

- 03/03/15: CP to provide update

RFIs:

16.02 Review of RFI Log

- 03/03/15: RFI 036, 037

SUBMITTALS:

16.03 **CRITICAL SUBMITTALS:**

- 03/03/15:
  - 03-3000.11 – Control Joints
  - 05-1200.01 – Embed shop drawings
  - 33-1000.04REV1 – Meter Vaults

NEW BUISNESS:

NEXT MEETING: 03/10/2015, time 2:30, at Legacy's office.

Meeting Adjourned: *The preceding minutes are CHINN Construction's interpretation of the items discussed and decisions reached at the above referenced meeting. Any persons desiring to add to, or otherwise change the minutes, are asked to correct the written statement or submit their comments in writing to CHINN Construction within two (2) days; otherwise the Minutes will stand as written.*

Hadley Mixed use
Legacy
3 wk Look ahead
3-02-2015

ID		Task Name	Duration	Start	Finish
1		**Mass Excavation**	**19 days**	**Mon 3/2/15**	**Thu 3/26/15**
2		Excavate Footings M Line/Entry	5 days	Mon 3/2/15	Fri 3/6/15
3		Backfill/Grade NW	3 days	Mon 3/2/15	Wed 3/4/15
4		Export Cont. South	1 day	Tue 3/3/15	Tue 3/3/15
5		Pipe Trenching NW	5 days	Mon 3/2/15	Fri 3/6/15
6		Vapor Barrier/Cap Break NW	6 days	Thu 3/5/15	Thu 3/12/15
7		Backfill/Grade NE	5 days	Fri 3/13/15	Thu 3/19/15
8		Pipe Trenching NE	5 days	Wed 3/18/15	Tue 3/24/15
9		Vapor Barrier/Cap Break NE	4 days	Mon 3/23/15	Thu 3/26/15
10					
11		**Waterproofing**	**4 days**	**Fri 3/6/15**	**Wed 3/11/15**
12		Clean/Prep Building Separation Walls	3 days	Fri 3/6/15	Tue 3/10/15
13		Apply Epro System	1 day	Wed 3/11/15	Wed 3/11/15
14					
15		**Utilities**	**2 days**	**Mon 3/9/15**	**Tue 3/10/15**
16		Domestic/Fire Roughin to FC Room	2 days	Mon 3/9/15	Tue 3/10/15
17					
18		**Underslab Piping**	**14 days**	**Mon 3/2/15**	**Thu 3/19/15**
19		North/West Storm/Slab Drainage	5 days	Mon 3/2/15	Fri 3/6/15
20		North/East Storm/Slab Drainage	8 days	Tue 3/10/15	Thu 3/19/15
21		Trench Drain NE Entry	1 day	Thu 3/19/15	Thu 3/19/15
22					
23		**CIP Concrete**	**21 days**	**Mon 3/2/15**	**Mon 3/30/15**
24		F&P Footings Northeast LP	5 days	Mon 3/2/15	Fri 3/6/15
25		F&P Remainder Concrete NW	2 days	Mon 3/2/15	Tue 3/3/15
26		F&P B Line Wall	3 days	Tue 3/3/15	Thu 3/5/15
27		F&P Walls/Columns Level P NE	7 days	Fri 3/6/15	Mon 3/16/15
28		PourSOG West/Ramp	1 day	Thu 3/12/15	Thu 3/12/15
29		Sawcut	1 day	Fri 3/13/15	Fri 3/13/15
30		Form Perimeter for SOG El 98	2 days	Fri 3/13/15	Mon 3/16/15
31		Pour SOG Elev 98	1 day	Tue 3/17/15	Tue 3/17/15
32		Pour SOG NE	1 day	Fri 3/27/15	Fri 3/27/15
33		Sawcut	1 day	Mon 3/30/15	Mon 3/30/15
34		L1 Deck Shoring NW	10 days	Fri 3/13/15	Thu 3/26/15

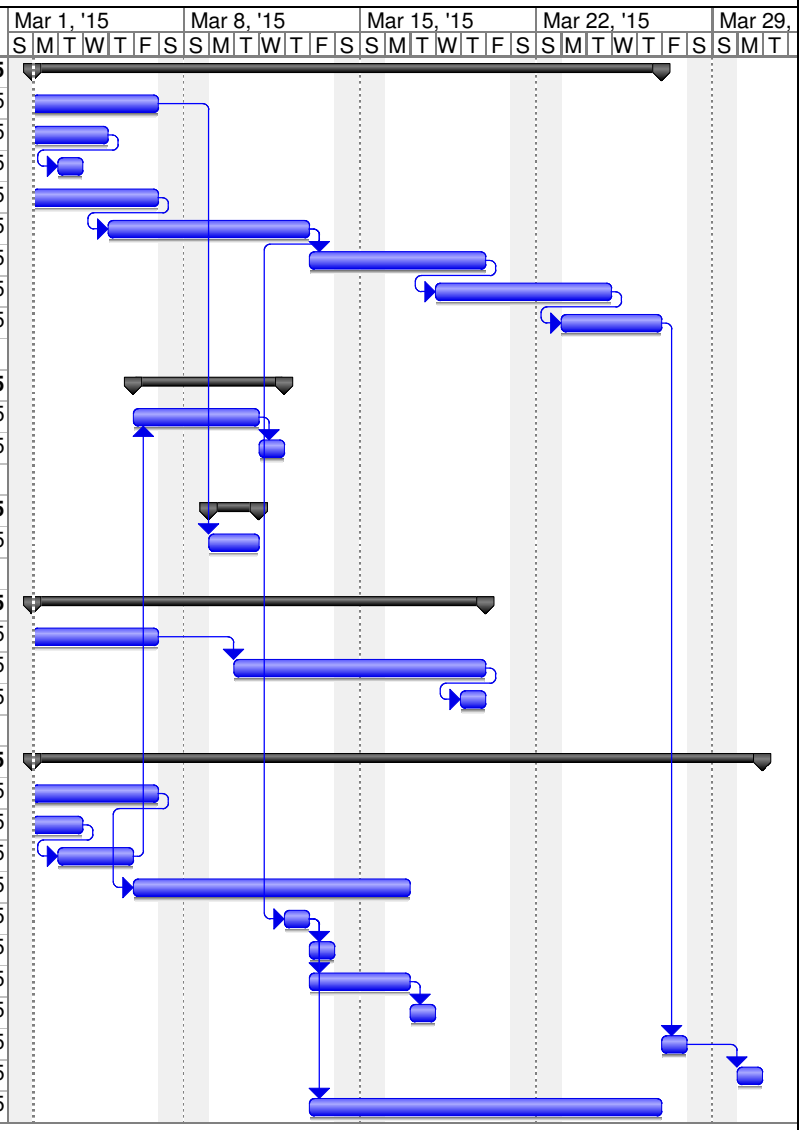

Project: 3wk look ahead 3-2-15
Date: Mon 3/2/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

CHINN CONSTRUCTION, LLC

RFI LOG

PRINT DATE: 3/2/2015

PROJECT: Hadley Project

PROJECT NUMBER: 14-0905

RFI	Description	Requested By	Date Initiated	Date Requested	Date Received	COP# / No Cost
036	Type A Decks From Outside Corners	Skyline	02/18/15	02/25/15		
037	Dimensions at SK1 and SK2	CC	02/18/15	02/20/15		
040	Concrete Rough Opening Dimensions at Stair 2 Level P	CC	02/23/15	02/23/15	*03/02/15*	*n/a*
041	Detail for Ledger	LAB	02/25/15	02/25/15	*03/02/15*	n/a
044	GL G Concrete Step in SOG	CC	03/02/15	03/04/15		
045						
046						
047						
048						
049						
050						
051						
052						
053						
054						
055						
056						
057						
058						
059						
060						
061						
062						
063						
064						
065						
066						
067						
068						
069						
070						

CHINN CONSTRUCTION, LLC

Hadley Mercer Island 14-0905

Reviewer: Submittal distribution as indicated to Owner, Architect and Consultants is subject to change by the Owner. Additional submittals may be added at the discretion of the Owner.

Code	Description	Subcontractor Vendor Supplier	Due to CHINN	Date Received from Sub	Date Reviewed	Reviewed By	Date Sent to Consultant	Due Date Requested	Date Returned by Consultant	Date Returned to Sub	Approved?	Remarks
	Concrete											
03-3000	**CIP Concrete**											
03-3000.11	Control Joints LP and L1 South	LAB		02/17/15	02/18/15	LB	02/18/15	03/02/15				
26-0000	**Electrical**	Independent Electric	01/30/15									
26-0000.01	Lighting - Level P North	Independent Electric	02/30/15	02/27/15	03/02/15	LB	03/02/15	03/16/15				
33-1000	**Water Distribution**	Northwest Construction										
33-1000.01	Water Distribution	Northwest Construction	01/07/15	11/20/14	11/24/14	SD	11/24/14	12/08/14	12/09/14	12/09/14		
33-1000.04REV1	Meter Vaults	Northwest Construction	02/20/15	02/20/15	02/23/15	LB	02/23/15	03/09/15				
