INVOICE

One Way Plumbing
127 10th St S,
Suite 200
Kirkland, WA 98033

Scan2Core, Inc.
31811 Pacific Hwy S, Ste B #345
Federal Way, Wa 98003

Phone: 206-518-1292
Email: dwight@scan2core.com
Web: scan2core.com

Payment Terms	Due upon receipt
Invoice #	070157
Date	09/21/2015

Posted
10/12/2015

Description	Quantity	Rate	Total
Scan2Core Special**	1.0	$600.00	$600.00

**$450 for Scanning & $150 for Core Drilling

GPR Scan AND Core any 2 locations to 10" Diameter

-------NOTES----------

Avoid PT cables by 3"
Avoid Conduits by 2.5"
Avoid Unlabeled items by 2.5"
Avoid Reinforcement Bar by 1.5"
Avoid Underground Utilities

Core, Cut, or Embed in "OK" areas only or to Depth noted for each area Imaged/Scanned

Coring and Anchoring inside existing walls where wall track or plates have not been completely removed will never designate an "OK" area by Scan2Core. Too many unknown variables can occur in those areas. However, Scan2Core GPR techs will provide clients with usable information for said areas.

Vendor:
Invoice:
Date:
Due:
PO:
Amount:
Disc:
Account:

Mobilization-Core Drilling	2.0	$150.00	$300.00

30 core locations required multiple days to complete scanning and core drilling. Initial request was for 15+ cores

Additional Core Drilling	1.0	$2,324.00	$2,324.00

Formula:
(2) X (Diameter) X (Depth) X (#Cores) = $Cost

Lev1:
(1-12"x4" deep 8" minimum charge, =$192 TRASH ROOM DRAIN (RFI 71)
1-5" thru 10" deep)=$100
3-4"x10"=$240
1-2"x10"=$40 } MISSED CANS FOR MAINS

BUT I THINK ITS 1-4"
2-3"
1-2"

WILL CONFIRM IN MORNING

2 - BAD PRE SNAP

Lev2:
4-1.5"x10"=$120 — 2 MISSED CANS
1-4"x10"=$80
1-3"x10"=$60
1-2"x10"=$40
} MISSED CANS FOR MAINS
1-6"x12"=$144 thru wall — THIS IS A 6" HOLE FOR OUTSIDE DRAIN

Lev3:
Unit 350:1-2"x14"=$56 — MISSED CAN IN POUR BACK
Unit 352:2-3"x16"=$192,1-4x16"=$128 ,1-5"x19"=$190
Unit 354:2-3"x14"=$168,1-4"x14"=$112, 1-5"x19"=$190
} BAD PRE SNAP
1-6"x18"=$216 thru wall — 5"
Outside unit 333: 1-4"x14"=$112, 2-2"x14"=$112 RELOCATE PER SIM (FIRE DOOR CONFLICT)
Unit 328: 2-3" need scanned first=$free with scan 2 core special. BAD PRE SNAP

Subtotal	$3,224.00
Total	**$3,224.00**
Summary	
Paid	$0.00
Amount Due	**$3,224.00**

Notes:

Job: Mercer Island

Site contact: Joe (206) 335-9762

9-21-15: scanned and drilled multiple areas

9-29-15: scanned and drilled remaining areas.

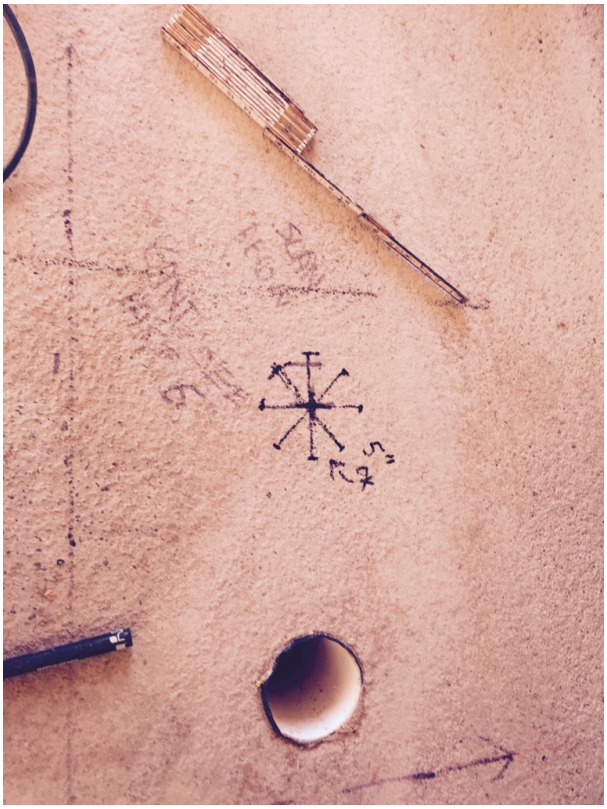

5"x19" location after scanning

2-3" locations scanned prior to drilling.

5"x19" core thru banded cable area after scanning and drilling b

2" alternative area after scanning and drilling. Note--cannot scan over metal wall plate.

Too congested to core 2-1.5" locations. Alternative area suggested.

4" core location over existing 3" sleeve with no scanning

2"x14" core location thru banded PT cable area prior to drilling location.

By signing this document, the customer agrees to the services and conditions outlined in this document.

One Way Plumbing
