EXXEL PACIFIC
GENERAL CONTRACTORS

Request For Information - 146

The Cora Apartments (19 W Harrison)

DATE: 05/15/2017

To:	**John Whitlow**	**From**	**Jola Bielecki**
	VIA Architecture 1809 7th Avenue, Suite 800 Seattle, WA 98101		The Cora Apartments (19 W Harrison) 19 W Harrison Seattle, WA 98109
Phone:	206-995-8872	**Phone:**	425-502-1573
Fax:		**Fax:**	360-671-7616
Email:	jwhitlow@via-architecture.com	**Email:**	jolab@exxelpacific.com
CC:			

Subject:	**Trench Drain and Wall Location at OH Door 209A**	**Status:**	**Open**
Drawing #:	4/A0412	**Spec Sect #:**	
Addendum:		**Submittal #:**	

Potential Schedule &/or Cost Impacts:

Schedule Impact (days):
Cost Impact:

Information Requested: **Date Required: 05/19/2017**

Please confirm if the metal framed wall at the OH door 209A & door 209B should be centered on the joint between concrete and sheetrock. Provide any waterproofing details if neccessay. Also, confirm the 5'-6" distance from the edge of the wall (grid F) to the the leading edge of the trench drain, per onsite review with John W., John L. and Tim C. is acceptable. Please note that any sprinkler pipes that impact the required clearance for the garage door have to be re-routed to allow for the 7'-3" tall door. See the attached sketches.

Suggestion:

Requesting Firm: Exxel Pacific, Inc.

Submitted By: *Jola Bielecki*

Response:

Date	Response
5-15-2017	Modification to the Ramp, Wall and Trench Drain location are acceptable as shown. Verify wall location as noted in Green notes on attached images. JXW

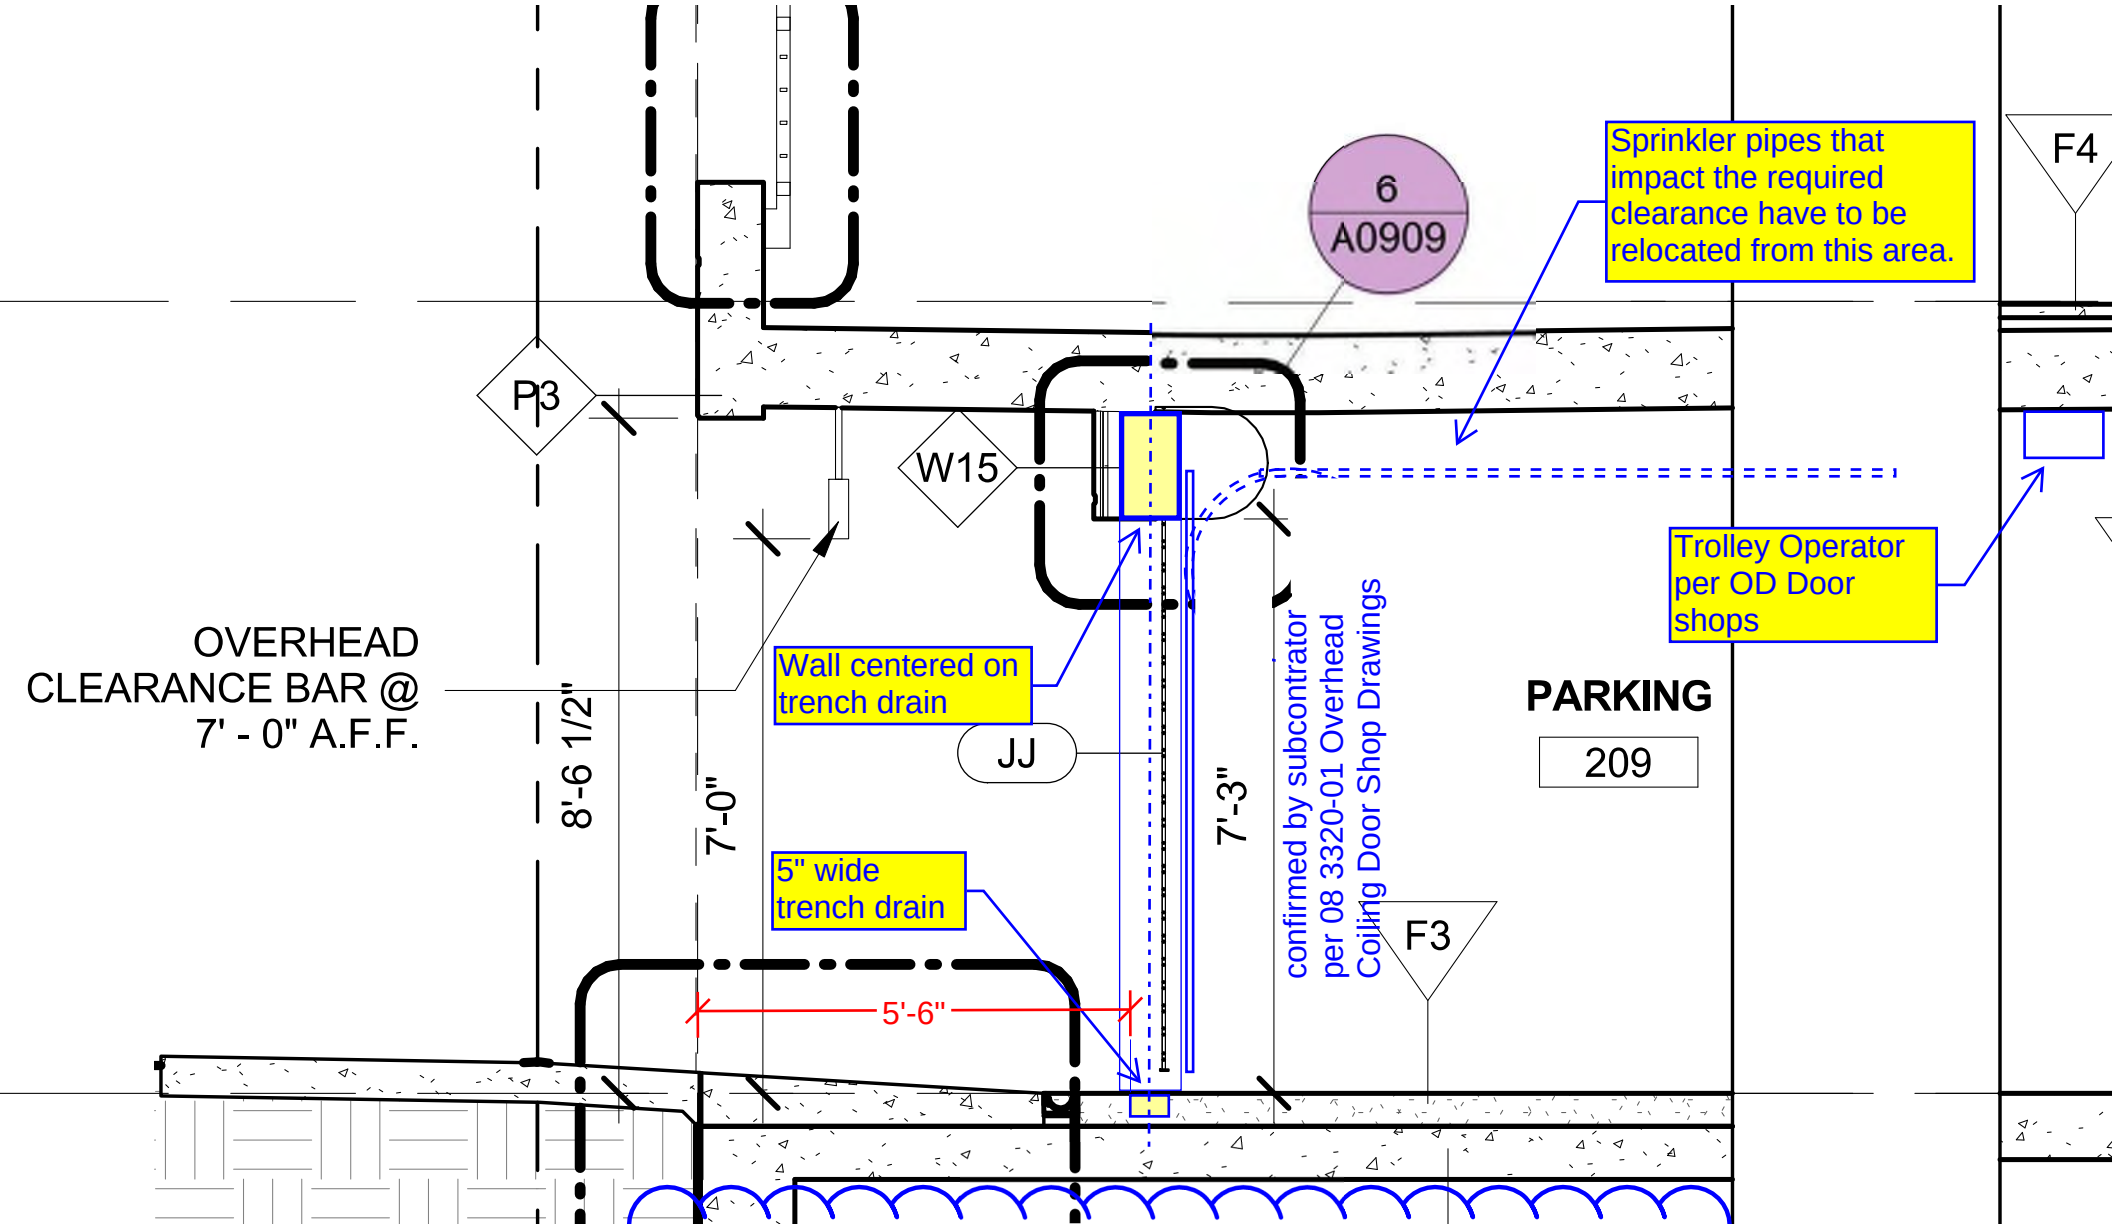
6
A0909
Sprinkler pipes that impact the required clearance have to be relocated from this area.
F4
P3
W15
Trolley Operator per OD Door shops
OVERHEAD CLEARANCE BAR @ 7' - 0" A.F.F.
Wall centered on trench drain
JJ
8'-6 1/2"
7'-0"
7'-3"
confirmed by subcontrator per 08 3320-01 Overhead Coiling Door Shop Drawings
PARKING
209
5" wide trench drain
F3
5'-6"

NO
TRESPASSING
1'-1"
6"
trench drain

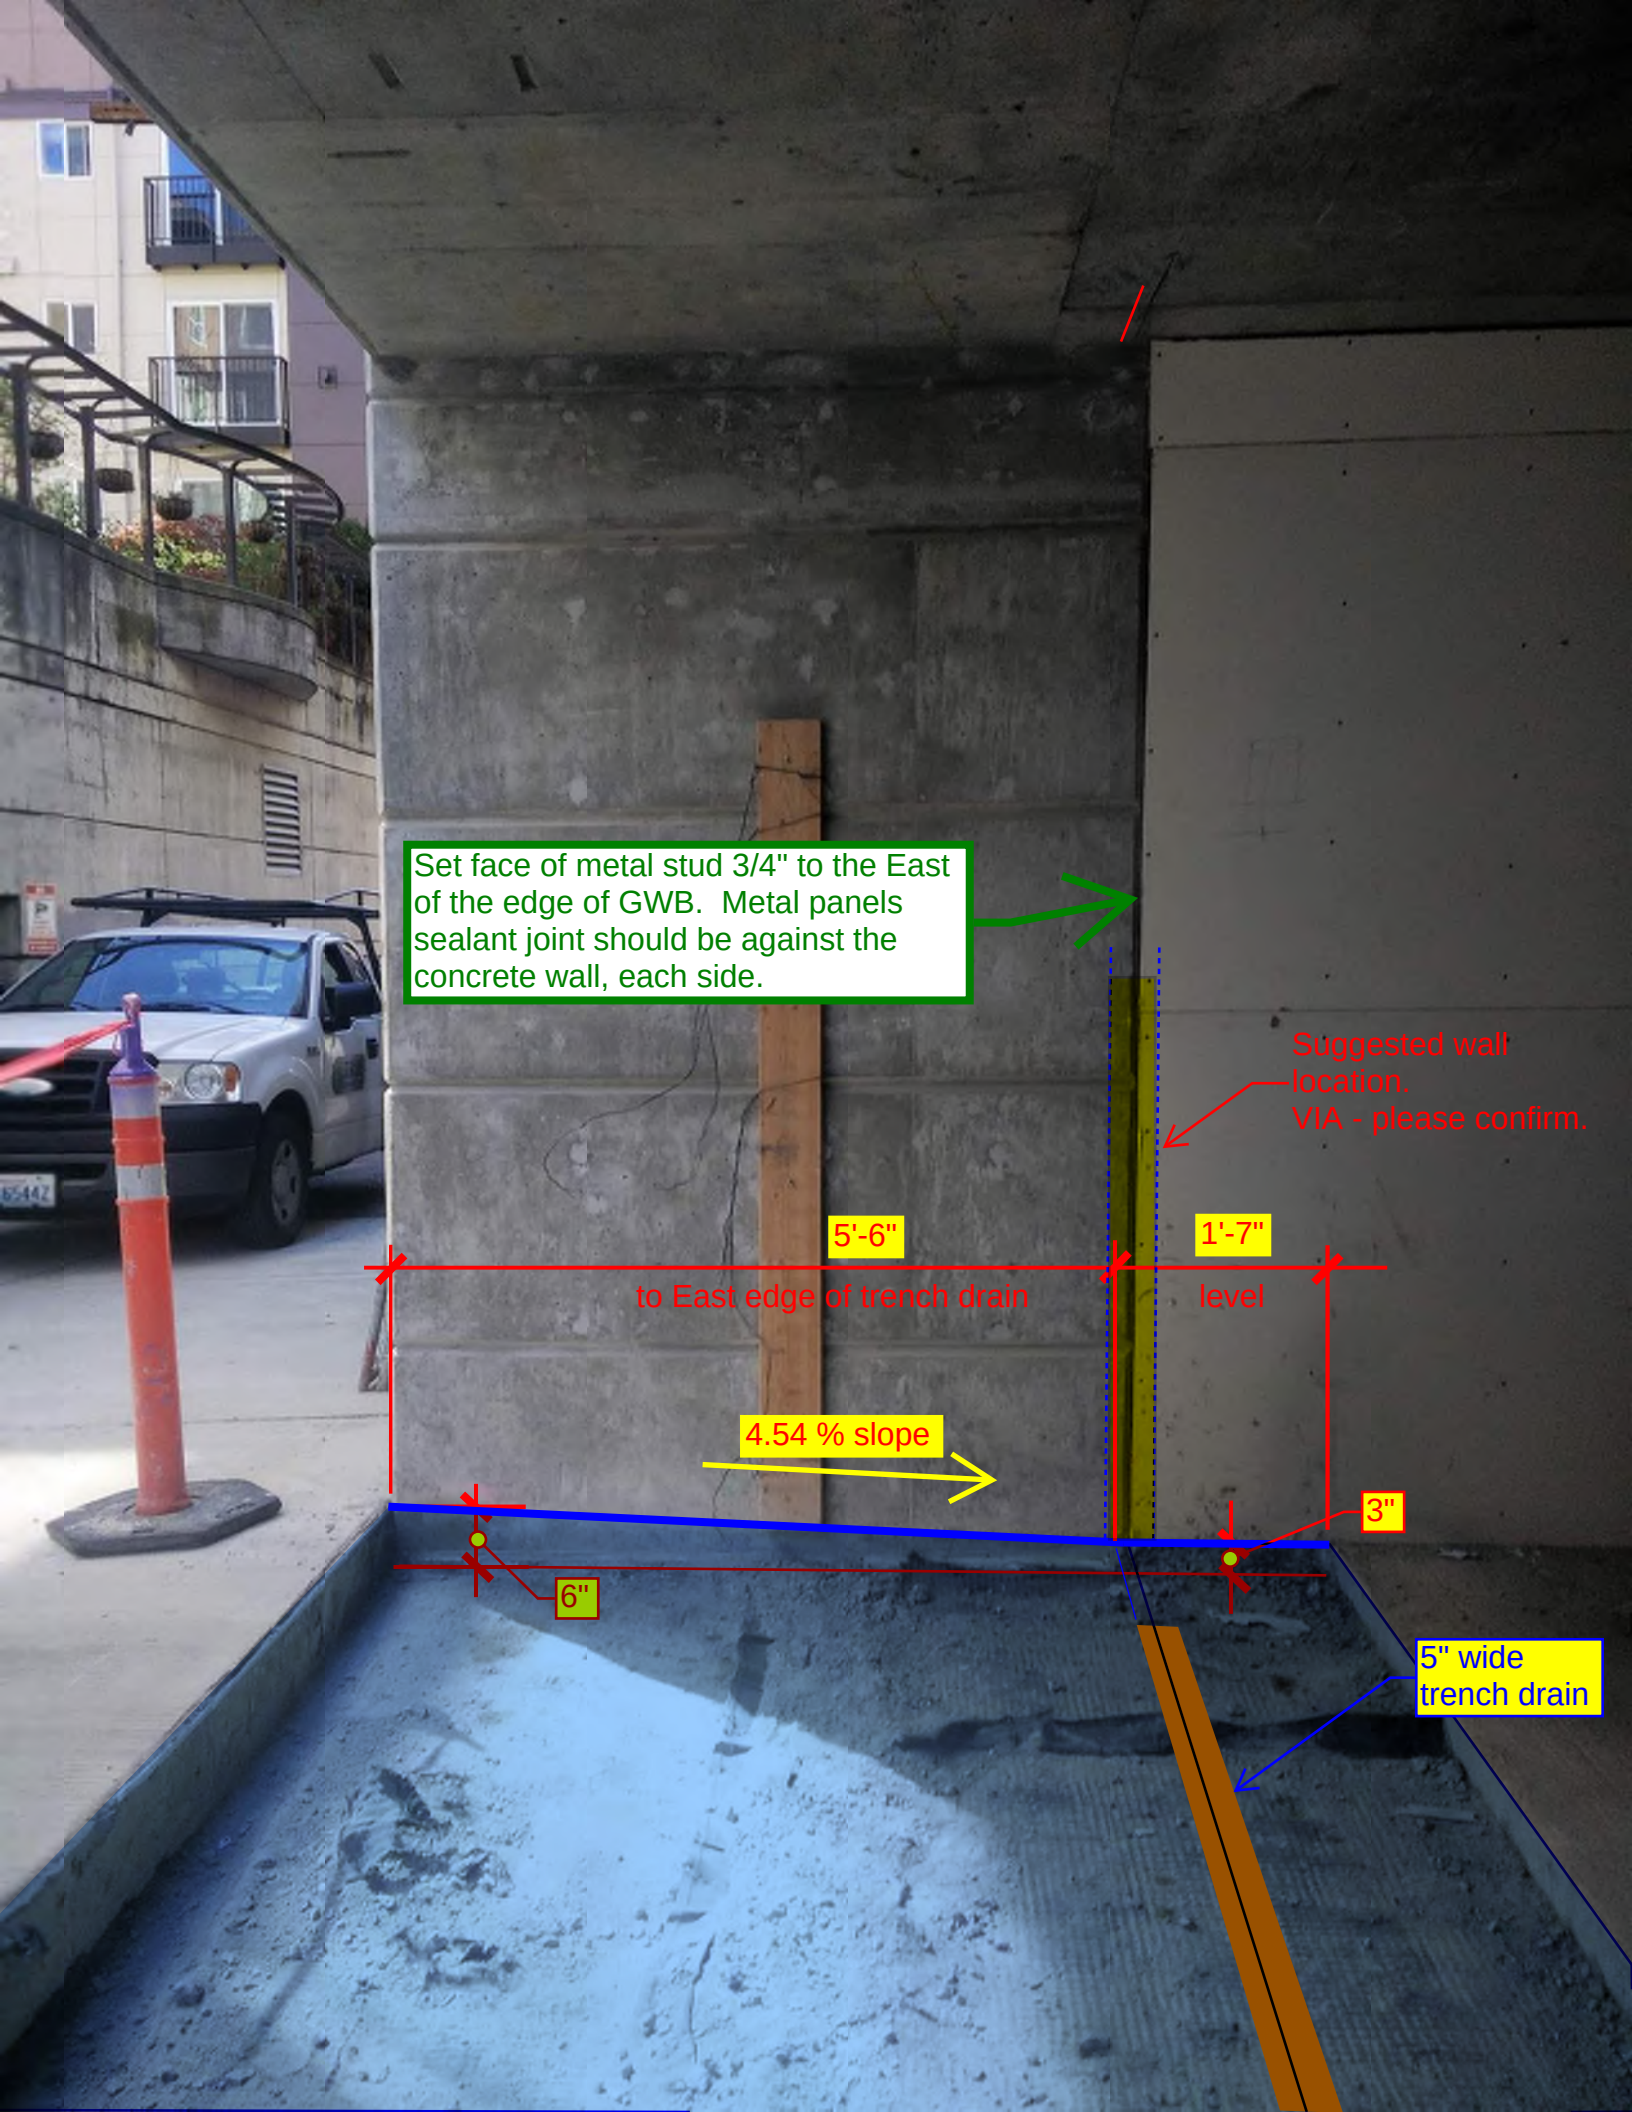
Set face of metal stud 3/4" to the East of the edge of GWB. Metal panels sealant joint should be against the concrete wall, each side.
Suggested wall location.
VIA - please confirm.
5'-6"
to East edge of trench drain
1'-7"
level
4.54 % slope
3"
6"
5" wide trench drain

Verify the wall location will engage the concrete wall on the North side, by min. of 2"
ROAD CLOSED
7'-1"
1'-7"
5'-6"
level
to East edge of trench drain
15.15 % slope
1'-1"
3"
5" wide trench drain
