BELOW GRADE WATERPROOFING PRE-CONSTRUCTION KICK-OFF MEETING

JOB NAME: Cora **JOB#** 201602
DATE: 5/11/2016 **TIME:** 10:00am

ATTENDEES	TITLE	COMPANY
Tim Connor	Superintendent	Exxel Pacific
Jola Bielecki	Project Engineer	Exxel Pacific
Matt VanderVeen	Building Envelope Manager	Exxel Pacific
Sean Lagers	Sr. Building Envelope Foreman	Exxel Pacific
Steven Thompson	Building Envelope Foreman	Exxel Pacific
Heath Merrigan	Site Formean	Exxel Pacific
Patrick McMahon	Envelope Consultant	BEE
John Whitlow	VIA Architecture	Architect
Peter Neilsen	VIA Architecture	Architect
John Links	Project Owner Representative	Barrientos LLC
Randy Dana	Below Grade Waterproofing Subcontractor	Sound Waterproofers
Dan Elliott	Product Representative	Cetco
Joe Browder	Concrete Contractor	Braycon
Jeff Gerard	Plumbing Contractor	One Way Plumbing
Scott Dinkelman	Geotech	Pangeo

MEETING OBJECTIVE:
The objective of this meeting is to become familiar with the exterior QA/QC program and the people responsible for the design, management, inspection and installation of the building envelope components. We will discuss scheduling, details, testing & inspections, and coordination items needed for a successful below grade waterproofing system.

PROJECT INFO & APPROVED DETAILS:

1. Current plans
   a) Current construction drawing set dated: 2/12/2016
   b) Current envelope details dated: 1/6/2016
   c) Drawings can be ordered via the Exxel FTP site and www.bxwa.com.
2. Pertaining building envelope-related ASIs and RFIs to date:
   a) RFI #001 – Foundation Wall Drainage Layout
3. All RFI's and ASI's will be distributed via email.
4. Submittals, material compatibility, installation responsibility review.
   a) Any deviation from approved details without written authorization from the architect, owner, and envelope consultant is STRICTLY PROHIBITED.
   b) Alternate materials will be considered only if submitted in a timely manner and in written RFI format including product data.
      - Substitution requests must be a complete packet, including all product data & MSDS
      - Below grade submittals – any follow-up items?

BELOW GRADE WATERPROOFING
PRE-CONSTRUCTION KICK-OFF MEETING

EXXEL PACIFIC
GENERAL CONTRACTORS

JOB NAME: Cora **JOB#** 201602
DATE: 5/11/2016 **TIME:** 10:00am

c) Any outstanding submittals?

5. Chain of communication on-site, who do you go to first: exchange phone #'s
   - First communication for Exxel: Steven Thompson: 425-772-4441.
   - Second communication for Exxel: Tim Connor 360-815-0766.
   - First communication for Sound Waterproofing: Jim Bates 206-510-4976
   - Second Communication for Sound Waterproofing: Randy Dana 206-419-3510
   - Primary contact for Braycon: Brian Sand 206-713-4615
   - Primary contact for BEE: Patrick McMahon 425-931-7409 (inspections)
     Jim Freeling 206-920-1090 (RFI's)
6. Forman meeting time: To be decided.
7. Safety meeting time: Mondays at 7am

ENVELOPE SCHEDULE:

1. Starting point and direction/flow of work. See below grade zone layout sheet.
   Work is to start in the NW corner and will move clockwise.
2. Review project schedule and starting dates:
   a) Elevator pit waterproofing: Mid-June
   b) 1st day of perimeter footing formwork: Mid-June
   c) Perimeter wall waterproofing: Mid-June
   d) Vapor barrier and first slab on grade concrete pour: Mid-July
   e) 1st level elevated deck pour: Mid-August
   f) Waterproofing at storm water detention vault: TBD
3. Sequence of work and schedule of trades involved
4. Any potential concerns with material availability, weather or manpower that should adversely affect schedule? NO

BELOW GRADE WATERPROOFING PRE-CONSTRUCTION KICK-OFF MEETING

JOB NAME: Cora **JOB#** 201602
DATE: 5/11/2016 **TIME:** 10:00am

PRODUCT SELECTION AND PLAN REVIEW:

1. Product selection for below grade horizontal and walls
   a) Vapor retarder below slab on grade at all slab on grade conditions: Viper II, 15 mil. Has been submitted and stamped by VIA. This submittal has not been reviewed by BEE.
   b) Waterstop RX101 and RX102. Installation by Braycon at all exterior cold joints and elevator pit cold joints. Sound Waterproofers will be installing the waterstop at block-outs and below grade penetrations.
   c) Voltex DS at select areas, with Aquadrain 15X drainage mat. Please refer to attached diagram for locations. This will be confirmed with an RFI.
   d) Stormwater Detention Tank: Polycoat Aquaseal 5000 and Polyprime 21.
   e) Note any other below grade waterproofing products that will be used.

2. Review below grade waterproofing plan.
   a) Elevator pit waterproofing per 103/BE100. This detail will be revised in an upcoming RFI to reflect Cetco detailing.
      i. Where is the water table in relation to the bottom of the elevator pit? Pangeo has determined that the height of the water table is not a concern on this project.
      ii. Clarify elevator pit pour sequencing. Exxel will not be installing a rat slab under the elevator pit.
      iii. Discuss concrete mix and stingers. Consolidation is key.

   b) Discuss waterproofing details at footing:
      i. Voltex DS to extend 12" past top of footing. Drain mat to stop at top of footing.
      ii. 2" PVC tight line with 2" wall drain connection every 8' O.C. (between piles).
      iii. Is there a thickened footing anywhere? Yes, Braycon to install water stop around drain grate pipes that run through thickened slabs.
      iv. Confirm we are using Aquadrain 15X in lieu of 100BD. See detail 108/BE10. Exxel to write an RFI to omit the 100BD from this detail.
      v. Confirm rebar layout doesn't interfere with the drain grates. It's too early to confirm at this point.

   c) Voltex DS and drain mat areas. See below grade waterproofing zone layout sheets:
      i. Cetco requires foam or grout in shoring voids prior to pressure treated plywood.
      ii. Mark top of grade on H-piles prior to Sound WP starting work. Keep drain mat and Voltex DS 2" below this line. Who will mark grade? Exxel to mark grade.
      iii. Clarify tie-back waterproofing details.
         1. Block out size and material at Voltex: Boxes will be framed around tie backs at Voltex DS areas. Tie backs should be centered and boxes should be framed

large enough to allow for Voltex DS tie in to material around tie back. 6" needed for tie in.

2. Block out size and material at drain mat only: Use heavy duty sonotube to prevent "squishing" of the tube. min. 18"
3. Clarify tie-back detentioning and pour-back method and timing. Shotcrete is fine, but full consolidation is critical.

iv. List locations where H-piles will be removed: _____Pre-cut?
v. Discuss termination of Voltex DS where concrete abuts. Terminate 1" in or just below? Grades set by Exxel.
vi. Discuss action plan to attach rebar mat. Cetco recommended using Hilti-clips to attach the rebar.

d) Confirm RX waterstop locations:
   i. RX Waterstop to be installed at all exterior cold joints, including above grade? Yes.
   ii. Around pipe penetrations & drain grate pipes (at thickened slab)
   iii. Around columns and against stairwell walls? No.

e) Clarify vapor barrier scope:
   i. 100 and 103/BE100. Detail to be revised per RFI to match Cetco standard detail showing Voltex extending 12" horizontally over vapor barrier.

f) Clarify below grade termination details at grade:
   i. Detail 101/BE100. Discuss addition of flashing at grade. See also detail 104. Clarify where this occurs. VIA and Barrientos have stated that they do not want to take on the additional cost of flashing to conceal the below grade water proofing termination along landscaped areas.
   ii. Terminate bentonite in the sidewalk in lieu of below? Review detail 113/BE101. Yes, Termination should match Cetco standard detail showing the Voltex terminating 1" into the sidewalk. Exxel to confirm with RFI.

g) Clarify where we have below grade rigid insulation. Review details 100 & 103/BE100 Elevator Pit and stairwells.

BELOW GRADE WATERPROOFING
PRE-CONSTRUCTION KICK-OFF MEETING

JOB NAME: Cora **JOB#** 201602
DATE: 5/11/2016 **TIME:** 10:00am

3. Surface prep requirements:
   a) For waterstop rope: Concrete substrates at cold joints must have a clean flat surface for bentonite rope to be installed. Braycon to inform Exxel who will be responsible for bentonite installation.
   b) For bentonite panels: Who will complete prep if there are voids in lagging, debris on lagging or other substrate concerns? Lagging appears to be free of voids.
   c) For hot-applied: light broom finish, no curing compounds or hard smooth finish
   d) Detention Vault: light broom finish is prefered. Cast in place is OK.
4. Clarify plan for protecting below grade waterproofing elements:
   a) Voltex DS Should not require any protection considering the time of year. Visqueen is on hand to cover any exposed Voltex if needed.
   b) RX waterstop Braycon will drape Visqueen over top of formwork if rain is expected.
5. Discuss below grade penetration details
   a) Below grade penetrations – identify which will be cored later, sleeved or installed prior to pour
      a. One sewer on 1st ave, cored later
      b. One storm on 1st ave, cored later Drain mat and Voltex DS
      c. One fire service on 1st ave, cored later. Drain mat and Voltex DS
      d. One domestic water service on 1st ave cored later. Drain mat and Voltex DS
      e. Primary power feed on alley side, stubbed in, 2 conduits. Drain mat and Voltex DS
      f. Comcast feed on alley side stubbed in, 1 conduit. Drain mat and Voltex DS
      g. Wave feed on alley side stubbed in, 1 conduit. Drain mat and Voltex DS
      h. C link feed on alley side stubbed in, 2 conduits. Drain mat and Voltex DS

QUALITY CONTROL, TESTING AND INSPECTIONS:

1. Quality control by Sound Waterproofers foreman. Forman is to review crew's work prior to moving on and confirm area is ready for next trade.
2. BEE to discuss site visit protocol & requirements…any required tests? NO required below grade testing.
   a) Any testing requirements re soil conditions? Any contaminants? No.
   b) Who will be conducting the site visits? Patrick McMahon
   c) Discuss open action item documentation and protocol. BEE to notify Exxel of open action items that will be on any report prior to leaving the site. Exxel to send affected subcontractors a copy of the BEE report if action items occur.
   d) Review warranty and requirements for final letters
3. Product rep site visits – input from Dan Elliot / Cetco rep. What is needed to obtain product warranties? Steven T. to coordinate with Cetco to inspect below grade waterproofing prior to shotcrete.

EXXEL PACIFIC
GENERAL CONTRACTORS

BELOW GRADE WATERPROOFING PRE-CONSTRUCTION KICK-OFF MEETING

JOB NAME: Cora **JOB#** 201602
DATE: 5/11/2016 **TIME:** 10:00am

OTHER DISCUSSION TOPICS / NEW BUSINESS:

VIA would like BEE to coordinate site visits with VIA so that the two can inspect the site together. BEE has a certain number of site visits per contract with Barrientos and schedules their site visits based on the progress of the water proofing. BEE to notify VIA when they expect to be making a site visit for inspection.

RFI's and submittals pertaining to the building envelope will go to through VIA who will forward on to BEE.

CETCO WATERPROOFING

FOUNDATION WALL

Termination at Grade

DETAIL

WP-7

NO SCALE - 03/17/09

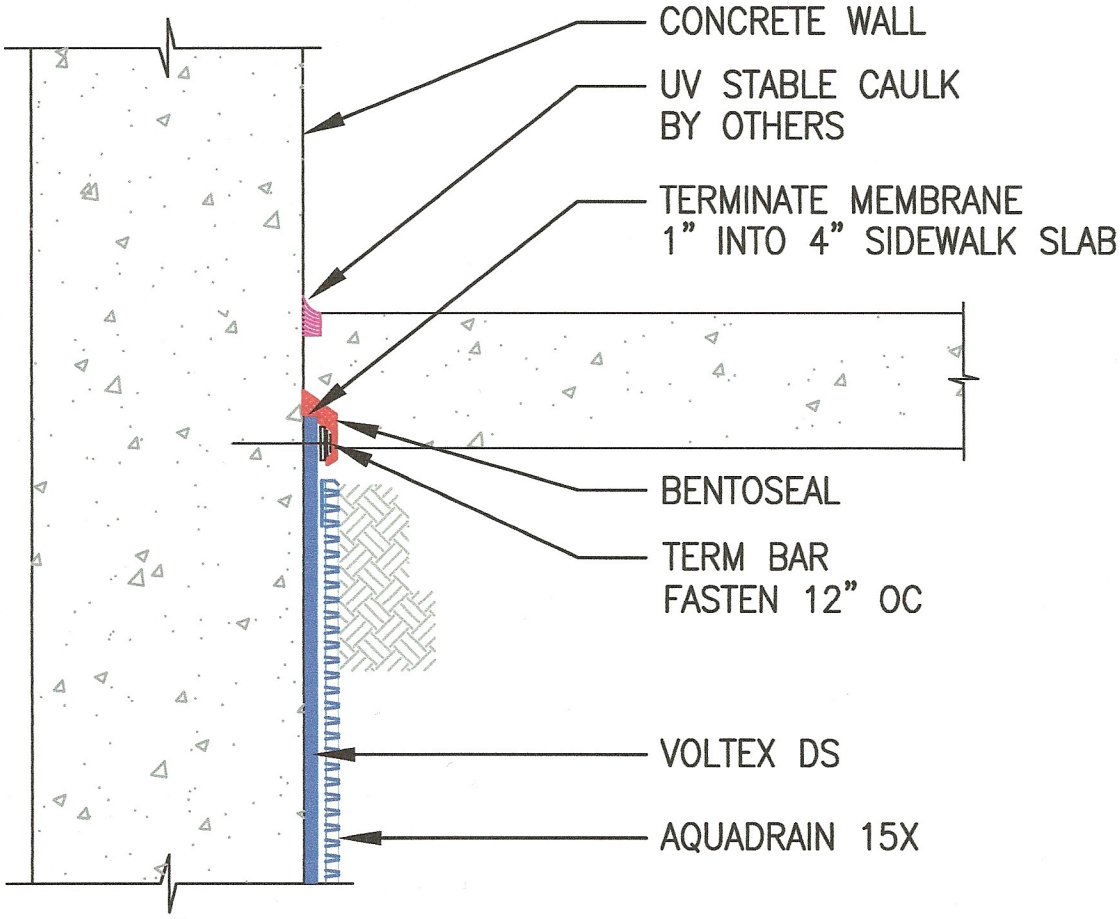

INSTALL VOLTEX DS WITH POLY LINER FACING INSTALLER

This information is based on data and knowledge considered to be true and accurate. The information is offered for the users' consideration, verification, and requires project designer's approval before installation. CETCO does not warrant the results obtained and assumes no liability for the use of the information. Please contact CETCO with any questions or deviations from this information. CETCO waterproofing products are not expansion joint materials. Expansion joints should be sealed with a proper expansion joint material by others. This information is subject to change.

CETCO®

BUILDING MATERIALS GROUP

tel (847) 392.5800 fax (847) 506.6195 http://www.cetco.com
(800) 527.9948 email: field.services@CETCO.com

VOLTEX DS WATERPROOFING

DS-01

FOUNDATION SLAB

Backfilled Elevator Pit (Non-Hydrostatic)

304-NH

SCALE: NTS 09/12

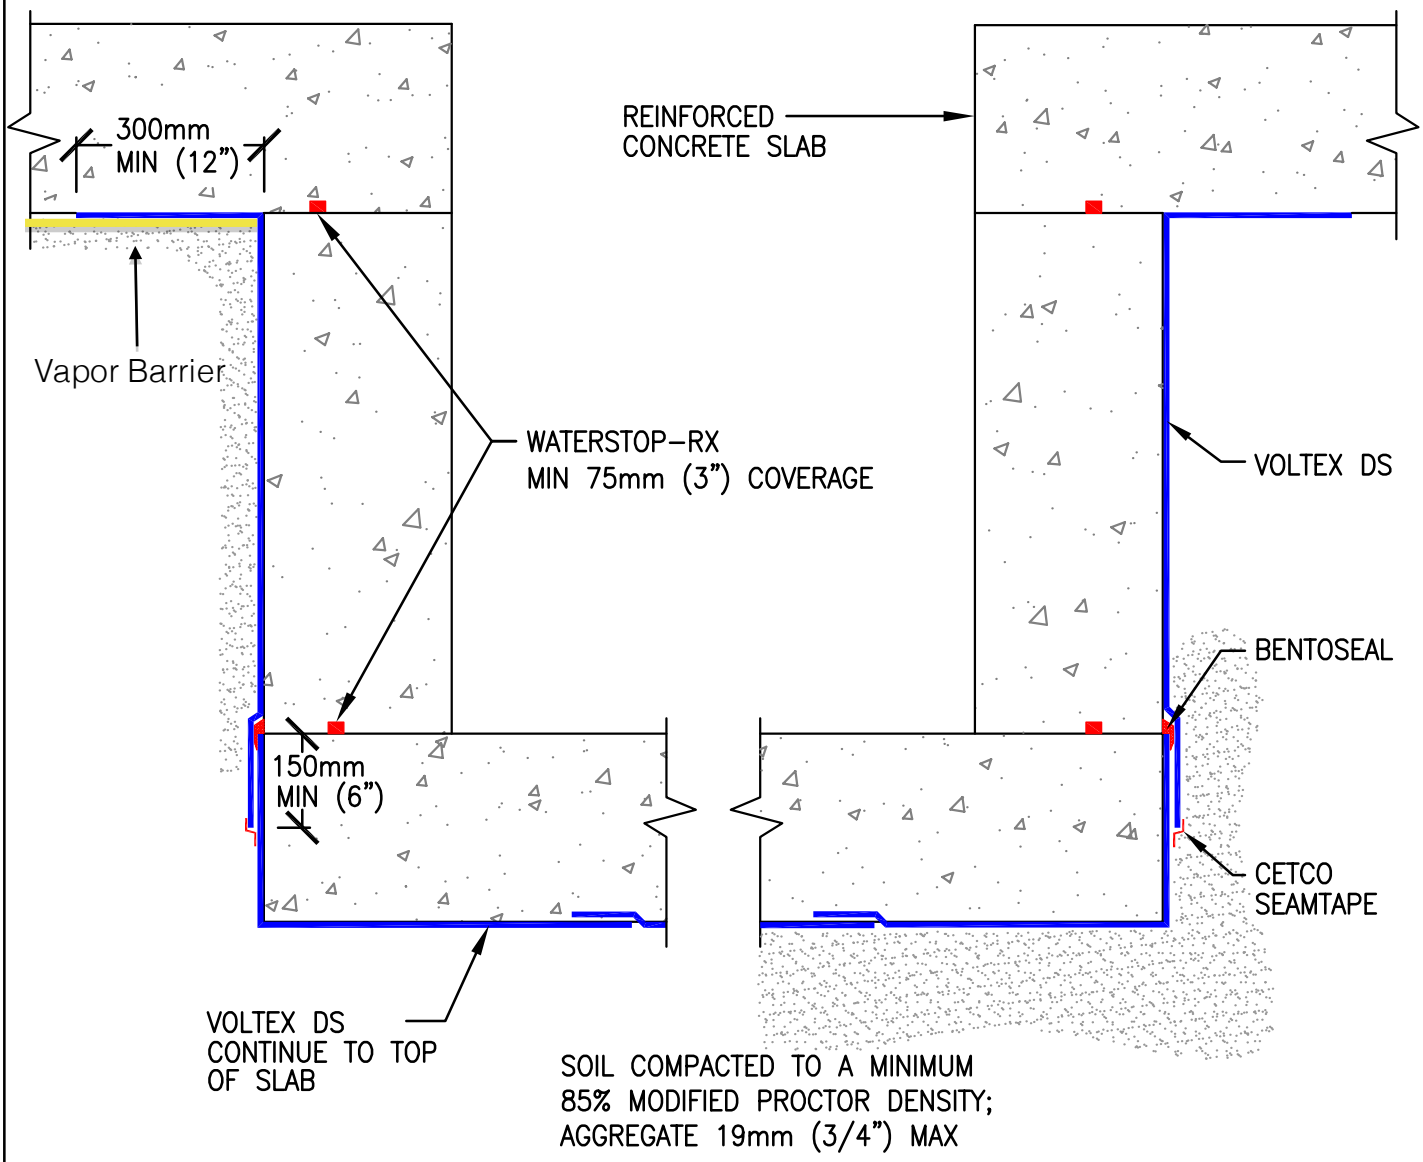

INSTALL CETCO SEAMTAPE ON BACKFILLED VOLTEX DS OVERLAP SEAMS
INSTALL UNDER SLAB VOLTEX DS WITH GRAY GEOTEXTILE FACING INSTALLER

This information is based on data and knowledge considered to be true and accurate. The information is offered for the users' consideration, verification, and requires project designer's approval before installation. CETCO does not warrant the results obtained and assumes no liability for the use of the information. Please contact CETCO with any questions or deviations from this information. CETCO waterproofing products are not expansion joint materials. Expansion joints should be sealed with a proper expansion joint material by others. This information is subject to change.

CETCO®
2870 Forbs Avenue, Hoffman Estates, IL 60192 USA
tel 847.851.1800 fax (847) 851.1371 http://www.cetco.com
800.527.9948 email: field.services@cetco.com

© 2012 Colloid Environmental Technologies Company

EXXEL PACIFIC
GENERAL CONTRACTORS

BELOW GRADE PRE-CONSTRUCTION COORDINATION MEETING

ATTENDANCE RECORD

PROJECT NAME: Cora PROJECT: # 201602

MEETING DATE: 5/11/2016

Representative Name:	Company:	E-mail:	Phone:
SEAN LAGERS	EXXEL PACIFIC	SEANL@EXXELPACIFIC.COM	(206) 409-1676
Joe Browder	Brayton	joeb@brayton.com	206.276.7440
Randy Dana	Sound	Randy@soundwaterproofers.com	206-419-3510
DAN ELLIOTT	Cetco Rep	desgcpro@msn.com	425-210-2779
PATRICK MCMAHON	BEE	PATRICK@BEE-ENGINEERS.COM	425 931 7409
JEFF GERARD	OWP	JEFFG@OWPLLC.NET	206-427-1578
JOLA BIELECKI	EXXEL PACIFIC	jolab@exxelpacific.com	425.502.1573
JOHN X WHITLOW	VIA ARCHITECTURE	JWHITLOW@VIA-ARCHITECTURE.COM	206.550.7591
PETER NEILSEN	VIA ARCHITECTURE	pneilsen@via-architecture.com	206.469 1401
John Links	Barrientos	John@mbarrientos.com	206-914-8130
Matt VanderVeen	Exxel Pacific	matt@exxelpacific.com	360-815-1872
Tim Conover	Exxel Pacific	tim@exxelpacific.com	360 815-0766
Heath Merrigan	Exxel	heathm@gmail.com	402-730-3985
SCOT DINKELMAN	PANGEO	sdinkelman@pangeoinc.com	425.233-0097
Steven Thompson	EXXEL	stevent@exxelpacific.com	425-772-4441

Copyright – Exxel Pacific Inc. This document is proprietary information and is not allowed to be duplicated or shared without prior authorization and consent from Exxel Pacific Inc.

VOLTEX DS

DRAIN MAT ONLY
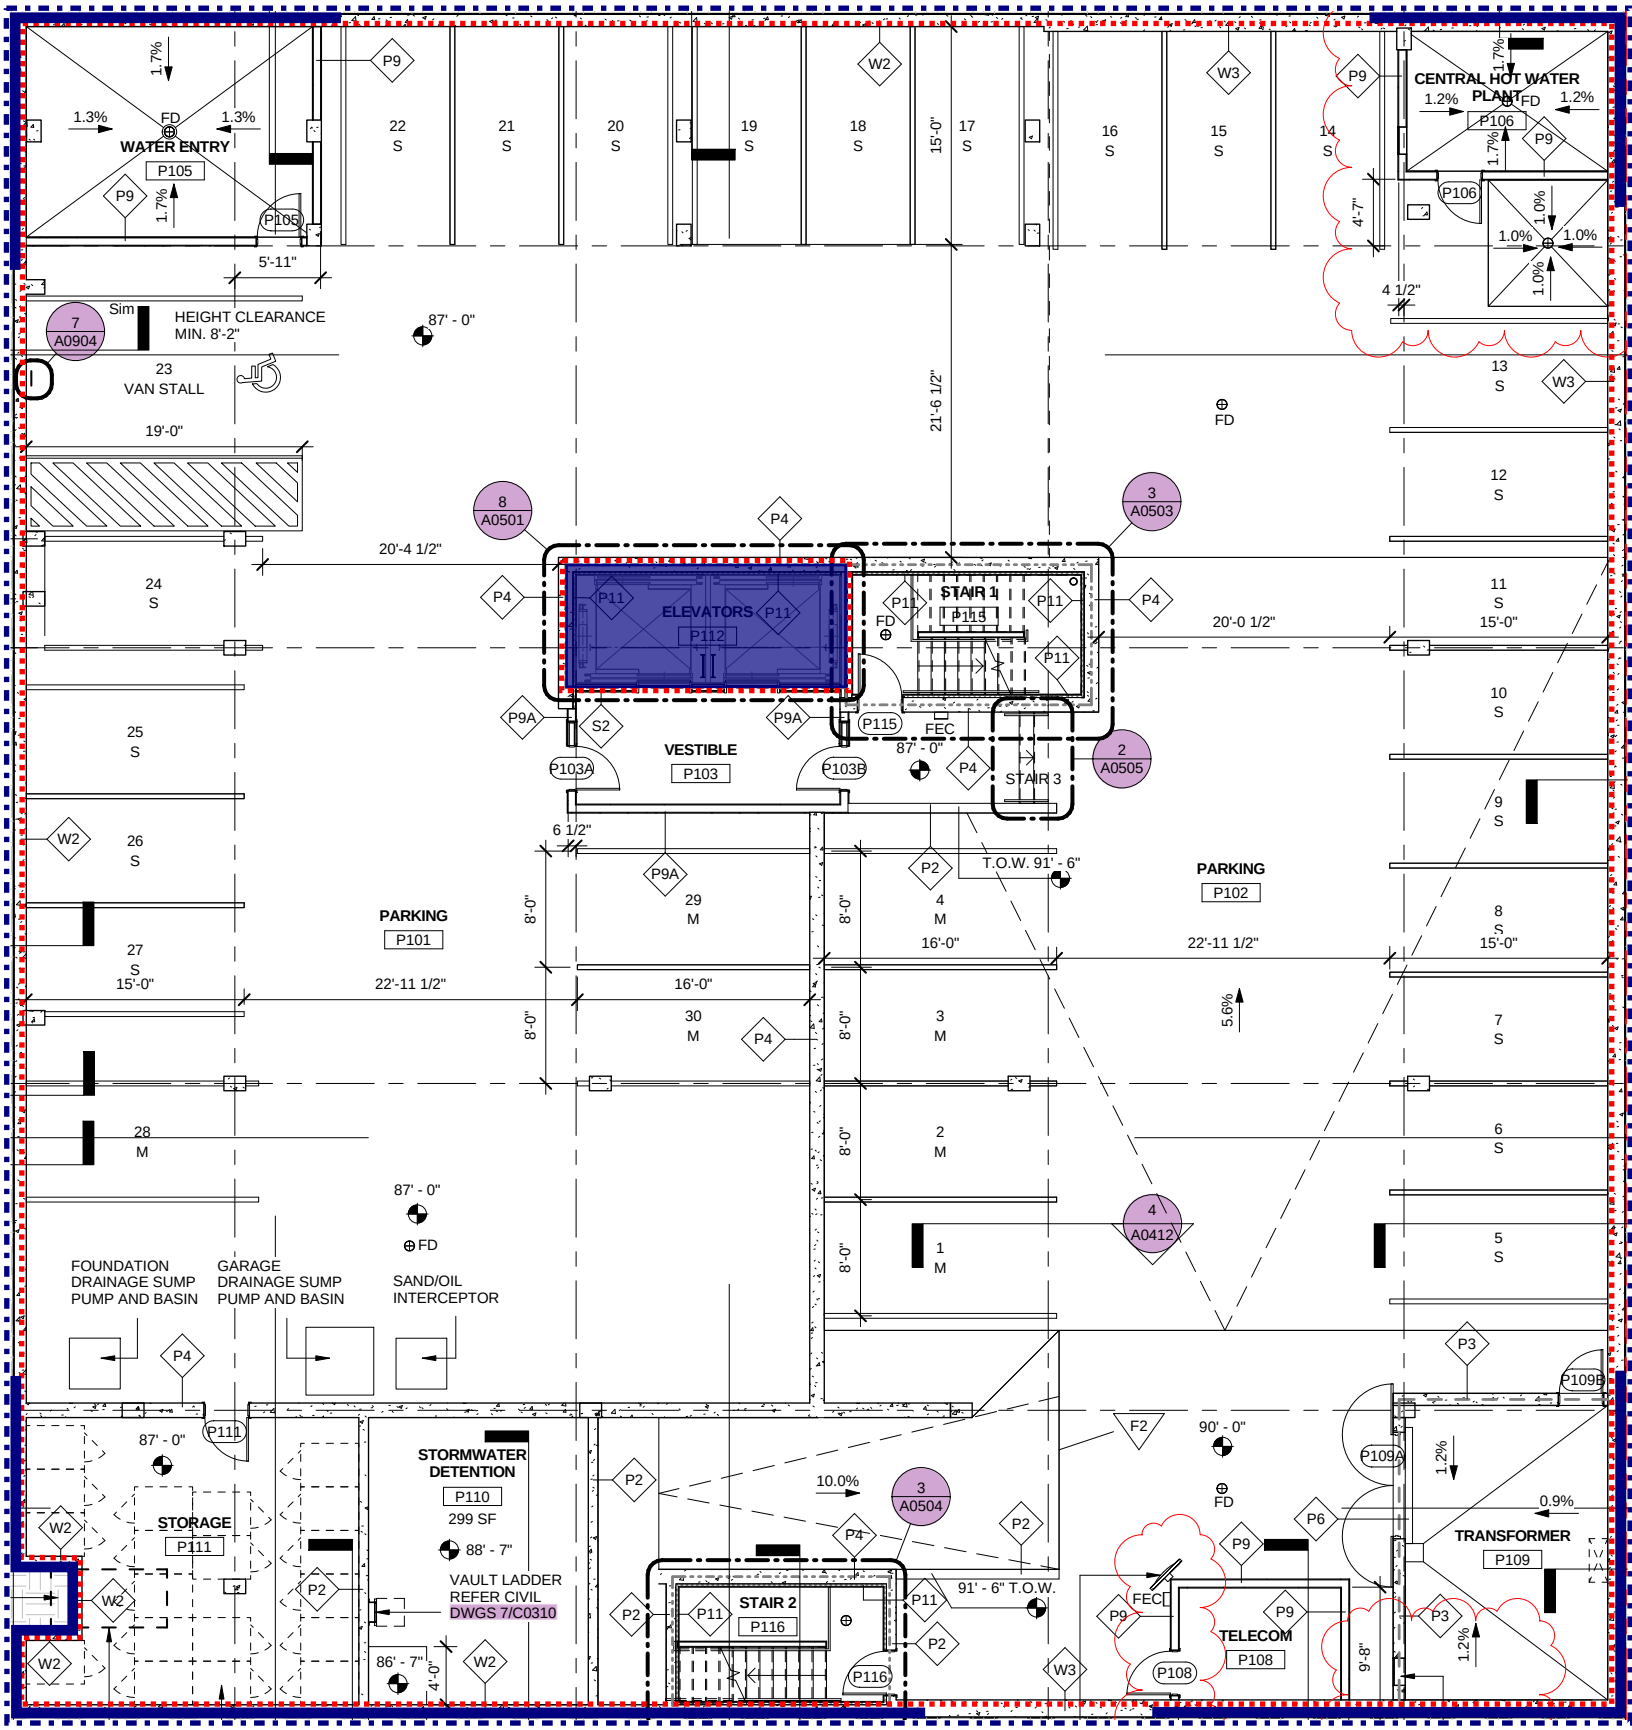
WATERSTOP RX
