EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
1	**TOTAL PROJECT DURATION**	**398 days**	**Fri 1/8/16**	**Mon 7/31/17**
2	**UMP**	**82 days**	**Fri 1/8/16**	**Mon 5/2/16**
107	**Building**	**317 days**	**Mon 5/2/16**	**Mon 7/31/17**
108	**Substantial Completion / TCO / Residential Occupancy**	0 days	**Thu 7/13/17**	**Thu 7/13/17**
109	**Project Completion**	0 days	**Mon 7/31/17**	**Mon 7/31/17**
110	**Excavation / Shoring**	**17 days**	**Mon 5/2/16**	**Tue 5/24/16**
111	Construction Commencement	0 days	**Mon 5/2/16**	**Mon 5/2/16**
112	Site Survey and layout	1 day	Mon 5/2/16	Mon 5/2/16
113	Cap Side Sewer	1 day	Mon 5/2/16	Mon 5/2/16
114	Drill Verticle	3 days	Tue 5/3/16	Thu 5/5/16
115	Shoring lagging & tieback	8 days	Mon 5/9/16	Wed 5/18/16
116	Mass Exc & Lagging	12 days	Mon 5/9/16	Tue 5/24/16
117	**Structure**	**161 days**	**Thu 5/26/16**	**Mon 1/16/17**
118	**Concrete**	**95 days**	**Thu 5/26/16**	**Mon 10/10/16**
119	**P1 Parking Level**	**32 days**	**Thu 5/26/16**	**Tue 7/12/16**
120	Footing Exc	5 days	Thu 5/26/16	Thu 6/9/16
121	Footings	8 days	Mon 6/6/16	Wed 6/15/16
122	Sub underslab slab MEP	6 days	Mon 6/13/16	Mon 6/20/16
123	Water proofing	8 days	Thu 6/2/16	Mon 6/13/16
124	Exterior Walls	11 days	Fri 6/10/16	Fri 6/24/16
125	Columns	5 days	Thu 6/16/16	Wed 6/22/16
126	Interior Walls	7 days	Thu 6/16/16	Fri 6/24/16
127	Bkfl Fndtn & SOG	8 days	Mon 6/27/16	Thu 7/7/16
128	Slab on Grade	3 days	Fri 7/8/16	Tue 7/12/16
129	**Level 1**	**27 days**	**Wed 7/13/16**	**Thu 8/18/16**
130	Suspended slab	14 days	Wed 7/13/16	Mon 8/1/16
131	Water proofing	5 days	Tue 7/19/16	Mon 7/25/16
132	Exterior Walls	5 days	Tue 8/2/16	Mon 8/8/16
133	Columns	5 days	Fri 8/5/16	Thu 8/11/16
134	Interior Walls	7 days	Wed 8/10/16	Thu 8/18/16
135	**Level 2**	**21 days**	**Fri 8/19/16**	**Mon 9/19/16**
136	Suspended slab	14 days	Fri 8/19/16	Thu 9/8/16
137	Columns	5 days	Fri 9/9/16	Thu 9/15/16
138	Walls	7 days	Fri 9/9/16	Mon 9/19/16
139	**Level 3**	**15 days**	**Tue 9/20/16**	**Mon 10/10/16**
140	Suspended Transfer Slab	15 days	Tue 9/20/16	Mon 10/10/16
141	**Metal Frame**	**13 days**	**Tue 10/25/16**	**Thu 11/10/16**
142	**Level 2 Common & LW**	**7 days**	**Tue 10/25/16**	**Wed 11/2/16**
143	Layout	2 days	Tue 10/25/16	Wed 10/26/16
144	Frame walls	5 days	Thu 10/27/16	Wed 11/2/16
145	Stairs and landings	2 days	Thu 10/27/16	Fri 10/28/16
146	**Level 1 Common & LW**	**9 days**	**Mon 10/31/16**	**Thu 11/10/16**
147	Layout	2 days	Mon 10/31/16	Tue 11/1/16
148	Frame walls	5 days	Wed 11/2/16	Tue 11/8/16
149	Stairs and landings	2 days	Wed 11/9/16	Thu 11/10/16
150	**Wood Frame**	**63 days**	**Fri 10/14/16**	**Mon 1/16/17**
151	**Level 3 (14 Units)**	**8 days**	**Fri 10/14/16**	**Tue 10/25/16**
152	Layout	2 days	Fri 10/14/16	Mon 10/17/16
153	Frame walls	6 days	Tue 10/18/16	Tue 10/25/16
154	**Level 4 (14 Units)**	**10 days**	**Wed 10/26/16**	**Tue 11/8/16**

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
155	Joists & Deck	4 days	Wed 10/26/16	Mon 10/31/16
156	Layout	1 day	Tue 11/1/16	Tue 11/1/16
157	Frame walls	5 days	Wed 11/2/16	Tue 11/8/16
158	**Level 5 (14 Units)**	**10 days**	**Wed 11/9/16**	**Tue 11/22/16**
159	Joists & Deck	4 days	Wed 11/9/16	Mon 11/14/16
160	Layout	1 day	Tue 11/15/16	Tue 11/15/16
161	Frame walls	5 days	Wed 11/16/16	Tue 11/22/16
162	**Level 6 (14 Units)**	**10 days**	**Wed 11/23/16**	**Thu 12/8/16**
163	Joists & Deck	4 days	Wed 11/23/16	Wed 11/30/16
164	Layout	1 day	Thu 12/1/16	Thu 12/1/16
165	Frame walls	5 days	Fri 12/2/16	Thu 12/8/16
166	**Level 7 (14 Units)**	**10 days**	**Fri 12/9/16**	**Thu 12/22/16**
167	Joists & Deck	4 days	Fri 12/9/16	Wed 12/14/16
168	Layout	1 day	Thu 12/15/16	Thu 12/15/16
169	Frame walls	5 days	Fri 12/16/16	Thu 12/22/16
170	**Roof Level**	**15 days**	**Fri 12/23/16**	**Mon 1/16/17**
171	Joists & Deck	4 days	Fri 12/23/16	Thu 12/29/16
172	Layout	1 day	Fri 12/30/16	Fri 12/30/16
173	Parapets and Penthouse and Cricket Overframing	10 days	Tue 1/3/17	Mon 1/16/17
174	**Exterior Closure**	**70 days**	**Fri 12/23/16**	**Mon 4/3/17**
175	**Membrane Roofing**	**12 days**	**Tue 1/17/17**	**Wed 2/1/17**
176	Insulation	5 days	Tue 1/17/17	Mon 1/23/17
177	Roofing	7 days	Tue 1/24/17	Wed 2/1/17
178	**Exterior Finishes**	**70 days**	**Fri 12/23/16**	**Mon 4/3/17**
179	**West Elevation**	**70 days**	**Fri 12/23/16**	**Mon 4/3/17**
180	Scaffolding	5 days	Fri 12/23/16	Fri 12/30/16
181	Framing QC	3 days	Tue 1/3/17	Thu 1/5/17
182	Window Prep	5 days	Fri 1/6/17	Thu 1/12/17
183	**Window Install - Qty 85**	**12 days**	**Fri 1/13/17**	**Mon 1/30/17**
184	L7 Window Install (14)	2 days	Fri 1/13/17	Mon 1/16/17
185	L6 Window Install (14)	2 days	Tue 1/17/17	Wed 1/18/17
186	L5 Window Install (14)	2 days	Thu 1/19/17	Fri 1/20/17
187	L4 Window Install (14)	2 days	Mon 1/23/17	Tue 1/24/17
188	L3 Window Install (14)	2 days	Wed 1/25/17	Thu 1/26/17
189	L2 Window Install (15)	2 days	Fri 1/27/17	Mon 1/30/17
190	**Rain Screen**	**11 days**	**Tue 1/17/17**	**Tue 1/31/17**
191	L7 Rain Screen	1 day	Tue 1/17/17	Tue 1/17/17
192	L6 Rain Screen	1 day	Thu 1/19/17	Thu 1/19/17
193	L5 Rain Screen	1 day	Mon 1/23/17	Mon 1/23/17
194	L4 Rain Screen	1 day	Wed 1/25/17	Wed 1/25/17
195	L3 Rain Screen	1 day	Fri 1/27/17	Fri 1/27/17
196	L2 Rain Screen	1 day	Tue 1/31/17	Tue 1/31/17
197	Brick Veneer & Scaffolding	15 days	Wed 2/1/17	Tue 2/21/17
198	Siding 6,000 SF	15 days	Wed 2/22/17	Tue 3/14/17
199	Paint	5 days	Wed 3/15/17	Tue 3/21/17
200	Punch	2 days	Wed 3/22/17	Thu 3/23/17
201	Scaffolding Dismantle & Deck Installation (26 Each)	7 days	Fri 3/24/17	Mon 4/3/17
202	**North Elevation**	**48 days**	**Tue 1/3/17**	**Thu 3/9/17**
203	Scaffolding	5 days	Tue 1/3/17	Mon 1/9/17

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
204	Framing QC	2 days	Tue 1/10/17	Wed 1/11/17
205	Window Prep	3 days	Thu 1/12/17	Mon 1/16/17
206	**Window Install - Qty 72**	**12 days**	**Tue 1/17/17**	**Wed 2/1/17**
207	L7 Window Install (12)	2 days	Tue 1/17/17	Wed 1/18/17
208	L6 Window Install (12)	2 days	Thu 1/19/17	Fri 1/20/17
209	L5 Window Install (12)	2 days	Mon 1/23/17	Tue 1/24/17
210	L4 Window Install (12)	2 days	Wed 1/25/17	Thu 1/26/17
211	L3 Window Install (12)	2 days	Fri 1/27/17	Mon 1/30/17
212	L2 Window Install (12)	2 days	Tue 1/31/17	Wed 2/1/17
213	**Rain Screen**	**11 days**	**Thu 1/19/17**	**Thu 2/2/17**
214	L7 Rain Screen	1 day	Thu 1/19/17	Thu 1/19/17
215	L6 Rain Screen	1 day	Mon 1/23/17	Mon 1/23/17
216	L5 Rain Screen	1 day	Wed 1/25/17	Wed 1/25/17
217	L4 Rain Screen	1 day	Fri 1/27/17	Fri 1/27/17
218	L3 Rain Screen	1 day	Tue 1/31/17	Tue 1/31/17
219	L2 Rain Screen	1 day	Thu 2/2/17	Thu 2/2/17
220	Siding 6,000 SF	15 days	Fri 2/3/17	Thu 2/23/17
221	Paint	5 days	Fri 2/24/17	Thu 3/2/17
222	Punch	2 days	Fri 3/3/17	Mon 3/6/17
223	Scaffolding Dismantle & Deck Installation (4 ea)	3 days	Tue 3/7/17	Thu 3/9/17
224	**East Elevation + CY**	**55 days**	**Tue 1/10/17**	**Mon 3/27/17**
225	Scaffolding	6 days	Tue 1/10/17	Tue 1/17/17
226	Framing QC	3 days	Wed 1/18/17	Fri 1/20/17
227	Window Prep	4 days	Mon 1/23/17	Thu 1/26/17
228	**Window Install - Qty 95**	**10 days**	**Fri 1/27/17**	**Thu 2/9/17**
229	L7 Window Install (19)	2 days	Fri 1/27/17	Mon 1/30/17
230	L6 Window Install (19)	2 days	Tue 1/31/17	Wed 2/1/17
231	L5 Window Install (19)	2 days	Thu 2/2/17	Fri 2/3/17
232	L4 Window Install (19)	2 days	Mon 2/6/17	Tue 2/7/17
233	L3 Window Install (19)	2 days	Wed 2/8/17	Thu 2/9/17
234	**Rain Screen**	**9 days**	**Tue 1/31/17**	**Fri 2/10/17**
235	L7 Rain Screen	1 day	Tue 1/31/17	Tue 1/31/17
236	L6 Rain Screen	1 day	Thu 2/2/17	Thu 2/2/17
237	L5 Rain Screen	1 day	Mon 2/6/17	Mon 2/6/17
238	L4 Rain Screen	1 day	Wed 2/8/17	Wed 2/8/17
239	L3 Rain Screen	1 day	Fri 2/10/17	Fri 2/10/17
240	Siding 9,700 SF	20 days	Mon 2/13/17	Fri 3/10/17
241	Paint	5 days	Mon 3/13/17	Fri 3/17/17
242	Punch	2 days	Mon 3/20/17	Tue 3/21/17
243	Scaffolding Dismantle & Deck Installation (12 Each)	4 days	Wed 3/22/17	Mon 3/27/17
244	**South Elevation**	**34 days**	**Wed 1/18/17**	**Mon 3/6/17**
245	Swing Scaffolding	2 days	Wed 1/18/17	Thu 1/19/17
246	Framing QC	2 days	Fri 1/20/17	Mon 1/23/17
247	Window Prep	1 day	Tue 1/24/17	Tue 1/24/17
248	**Window Install - Qty 5**	**5 days**	**Wed 1/25/17**	**Tue 1/31/17**
249	L7 Window Install (1)	1 day	Wed 1/25/17	Wed 1/25/17
250	L6 Window Install (1)	1 day	Thu 1/26/17	Thu 1/26/17
251	L5 Window Install (1)	1 day	Fri 1/27/17	Fri 1/27/17
252	L4 Window Install (1)	1 day	Mon 1/30/17	Mon 1/30/17

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
253	L3 Window Install (1)	1 day	Tue 1/31/17	Tue 1/31/17
254	**Rain Screen**	**5 days**	**Thu 1/26/17**	**Wed 2/1/17**
255	L7 Rain Screen	1 day	Thu 1/26/17	Thu 1/26/17
256	L6 Rain Screen	1 day	Fri 1/27/17	Fri 1/27/17
257	L5 Rain Screen	1 day	Mon 1/30/17	Mon 1/30/17
258	L4 Rain Screen	1 day	Tue 1/31/17	Tue 1/31/17
259	L3 Rain Screen	1 day	Wed 2/1/17	Wed 2/1/17
260	Siding 6,000 SF	15 days	Thu 2/2/17	Wed 2/22/17
261	Paint	5 days	Thu 2/23/17	Wed 3/1/17
262	Punch	2 days	Thu 3/2/17	Fri 3/3/17
263	Scaffolding Dismantle	1 day	Mon 3/6/17	Mon 3/6/17
264	**Interior Finishes**	**158 days**	**Tue 11/1/16**	**Thu 6/15/17**
265	**Elevators**	**60 days**	**Thu 2/2/17**	**Wed 4/26/17**
266	Elevator install	60 days	Thu 2/2/17	Wed 4/26/17
267	**MEP Rough-In Up**	**36 days**	**Tue 11/1/16**	**Thu 12/22/16**
268	P1 MEP Rough-In Up	20 days	Tue 11/1/16	Wed 11/30/16
269	L1 MEP Rough-In Up	5 days	Thu 12/1/16	Wed 12/7/16
270	L2 MEP Rough-In Up	5 days	Thu 12/8/16	Wed 12/14/16
271	L3 MEP Rough-In Up	5 days	Wed 11/16/16	Tue 11/22/16
272	L4 MEP Rough-In Up	5 days	Wed 11/23/16	Thu 12/1/16
273	L5 MEP Rough-In Up	5 days	Fri 12/2/16	Thu 12/8/16
274	L6 MEP Rough-In Up	5 days	Fri 12/9/16	Thu 12/15/16
275	L7 MEP Rough-In Up	5 days	Fri 12/16/16	Thu 12/22/16
276	**Level P1**	**20 days**	**Tue 3/14/17**	**Mon 4/10/17**
277	Finishes @ Rooms	10 days	Tue 3/14/17	Mon 3/27/17
278	Striping, paint	10 days	Tue 3/28/17	Mon 4/10/17
279	**Level 7**	**74 days**	**Thu 2/2/17**	**Tue 5/16/17**
280	Mech/ Elec roughings	7 days	Thu 2/2/17	Fri 2/10/17
281	Dryout	10 days	Thu 2/2/17	Wed 2/15/17
282	Prerock	2 days	Thu 2/16/17	Fri 2/17/17
283	Insulation	3 days	Mon 2/20/17	Wed 2/22/17
284	Hang Sheetrock	4 days	Thu 2/23/17	Tue 2/28/17
285	Tape and Finish	6 days	Wed 3/1/17	Wed 3/8/17
286	Texture and Paint	5 days	Thu 3/9/17	Wed 3/15/17
287	Gypcrete	2 days	Thu 3/16/17	Fri 3/17/17
288	Cabinets	4 days	Mon 3/27/17	Thu 3/30/17
289	Tops	3 days	Fri 4/7/17	Tue 4/11/17
290	Doors and Trim	7 days	Wed 4/12/17	Thu 4/20/17
291	Sheet Flooring	3 days	Fri 4/21/17	Tue 4/25/17
292	Carpet	3 days	Wed 4/26/17	Fri 4/28/17
293	Appliances	2 days	Mon 5/1/17	Tue 5/2/17
294	Touch up and Punch	10 days	Wed 5/3/17	Tue 5/16/17
295	**Level 6**	**74 days**	**Mon 2/13/17**	**Thu 5/25/17**
296	Mech/ Elec roughings	7 days	Mon 2/13/17	Tue 2/21/17
297	Dryout	10 days	Mon 2/13/17	Fri 2/24/17
298	Prerock	2 days	Mon 2/27/17	Tue 2/28/17
299	Insulation	3 days	Wed 3/1/17	Fri 3/3/17
300	Hang Sheetrock	4 days	Mon 3/6/17	Thu 3/9/17
301	Tape and Finish	6 days	Fri 3/10/17	Fri 3/17/17
302	Texture and Paint	5 days	Mon 3/20/17	Fri 3/24/17
303	Gypcrete	2 days	Mon 3/27/17	Tue 3/28/17

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
304	Cabinets	4 days	Wed 4/5/17	Mon 4/10/17
305	Tops	3 days	Tue 4/18/17	Thu 4/20/17
306	Doors and Trim	7 days	Fri 4/21/17	Mon 5/1/17
307	Sheet Flooring	3 days	Tue 5/2/17	Thu 5/4/17
308	Carpet	3 days	Fri 5/5/17	Tue 5/9/17
309	Appliances	2 days	Wed 5/10/17	Thu 5/11/17
310	Touch up and Punch	10 days	Fri 5/12/17	Thu 5/25/17
311	**Level 5**	**74 days**	**Wed 2/22/17**	**Tue 6/6/17**
312	Mech/ Elec roughings	7 days	Wed 2/22/17	Thu 3/2/17
313	Dryout	10 days	Wed 2/22/17	Tue 3/7/17
314	Prerock	2 days	Wed 3/8/17	Thu 3/9/17
315	Insulation	3 days	Fri 3/10/17	Tue 3/14/17
316	Hang Sheetrock	4 days	Wed 3/15/17	Mon 3/20/17
317	Tape and Finish	6 days	Tue 3/21/17	Tue 3/28/17
318	Texture and Paint	5 days	Wed 3/29/17	Tue 4/4/17
319	Gypcrete	2 days	Wed 4/5/17	Thu 4/6/17
320	Cabinets	4 days	Fri 4/14/17	Wed 4/19/17
321	Tops	3 days	Thu 4/27/17	Mon 5/1/17
322	Doors and Trim	7 days	Tue 5/2/17	Wed 5/10/17
323	Sheet Flooring	3 days	Thu 5/11/17	Mon 5/15/17
324	Carpet	3 days	Tue 5/16/17	Thu 5/18/17
325	Appliances	2 days	Fri 5/19/17	Mon 5/22/17
326	Touch up and Punch	10 days	Tue 5/23/17	Tue 6/6/17
327	**Level 4**	**74 days**	**Fri 3/3/17**	**Thu 6/15/17**
328	Mech/ Elec roughings	7 days	Fri 3/3/17	Mon 3/13/17
329	Dryout	10 days	Fri 3/3/17	Thu 3/16/17
330	Prerock	2 days	Fri 3/17/17	Mon 3/20/17
331	Insulation	3 days	Tue 3/21/17	Thu 3/23/17
332	Hang Sheetrock	4 days	Fri 3/24/17	Wed 3/29/17
333	Tape and Finish	6 days	Thu 3/30/17	Thu 4/6/17
334	Texture and Paint	5 days	Fri 4/7/17	Thu 4/13/17
335	Gypcrete	2 days	Fri 4/14/17	Mon 4/17/17
336	Cabinets	4 days	Tue 4/25/17	Fri 4/28/17
337	Tops	3 days	Mon 5/8/17	Wed 5/10/17
338	Doors and Trim	7 days	Thu 5/11/17	Fri 5/19/17
339	Sheet Flooring	3 days	Mon 5/22/17	Wed 5/24/17
340	Carpet	3 days	Thu 5/25/17	Tue 5/30/17
341	Appliances	2 days	Wed 5/31/17	Thu 6/1/17
342	Touch up and Punch	10 days	Fri 6/2/17	Thu 6/15/17
343	**Level 3**	**67 days**	**Tue 3/14/17**	**Thu 6/15/17**
344	Mech/ Elec roughings	7 days	Tue 3/14/17	Wed 3/22/17
345	Dryout	10 days	Tue 3/14/17	Mon 3/27/17
346	Prerock	2 days	Tue 3/28/17	Wed 3/29/17
347	Insulation	3 days	Thu 3/30/17	Mon 4/3/17
348	Hang Sheetrock	4 days	Tue 4/4/17	Fri 4/7/17
349	Tape and Finish	6 days	Mon 4/10/17	Mon 4/17/17
350	Texture and Paint	5 days	Tue 4/18/17	Mon 4/24/17
351	Cabinets	4 days	Tue 4/25/17	Fri 4/28/17
352	Tops	3 days	Mon 5/8/17	Wed 5/10/17
353	Doors and Trim	7 days	Thu 5/11/17	Fri 5/19/17
354	Sheet Flooring	3 days	Mon 5/22/17	Wed 5/24/17

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
355	Carpet	3 days	Thu 5/25/17	Tue 5/30/17
356	Appliances	2 days	Wed 5/31/17	Thu 6/1/17
357	Touch up and Punch	10 days	Fri 6/2/17	Thu 6/15/17
358	**Level 2 Common & (4) LW & (1) Flat**	**51 days**	**Tue 3/14/17**	**Tue 5/23/17**
359	Mech/ Elec roughings	7 days	Tue 3/14/17	Wed 3/22/17
360	Dryout	3 days	Tue 3/14/17	Thu 3/16/17
361	Prerock	2 days	Tue 3/21/17	Wed 3/22/17
362	Insulation	2 days	Thu 3/23/17	Fri 3/24/17
363	Hang Sheetrock	4 days	Mon 3/27/17	Thu 3/30/17
364	Tape and Finish	7 days	Fri 3/31/17	Mon 4/10/17
365	Texture and Paint	5 days	Tue 4/11/17	Mon 4/17/17
366	Cabinets	4 days	Tue 4/18/17	Fri 4/21/17
367	Tops	2 days	Mon 4/24/17	Tue 4/25/17
368	Doors and Trim	5 days	Wed 4/26/17	Tue 5/2/17
369	Sheet Flooring	3 days	Wed 5/3/17	Fri 5/5/17
370	Carpet	2 days	Mon 5/8/17	Tue 5/9/17
371	Touch up and Punch	10 days	Wed 5/10/17	Tue 5/23/17
372	**Level 1 Common & (4) LW**	**57 days**	**Thu 3/23/17**	**Mon 6/12/17**
373	Mech/ Elec roughings	7 days	Thu 3/23/17	Fri 3/31/17
374	Dryout	3 days	Thu 3/23/17	Mon 3/27/17
375	Prerock	2 days	Thu 3/30/17	Fri 3/31/17
376	Insulation	2 days	Mon 4/3/17	Tue 4/4/17
377	Hang Sheetrock	4 days	Wed 4/5/17	Mon 4/10/17
378	Tape and Finish	7 days	Tue 4/11/17	Wed 4/19/17
379	Texture and Paint	5 days	Thu 4/20/17	Wed 4/26/17
380	Cabinets	4 days	Thu 4/27/17	Tue 5/2/17
381	Tops	2 days	Wed 5/10/17	Thu 5/11/17
382	Doors and Trim	5 days	Fri 5/12/17	Thu 5/18/17
383	Sheet Flooring	3 days	Fri 5/19/17	Tue 5/23/17
384	Carpet	2 days	Wed 5/24/17	Thu 5/25/17
385	Appliances	1 day	Fri 5/26/17	Fri 5/26/17
386	Touch up and Punch	10 days	Tue 5/30/17	Mon 6/12/17
387	**Roof Finishes**	**35 days**	**Thu 4/27/17**	**Thu 6/15/17**
388	Decking	20 days	Thu 4/27/17	Wed 5/24/17
389	Landscaping	15 days	Thu 5/25/17	Thu 6/15/17
390	**Site Finishes**	**111 days**	**Thu 12/8/16**	**Mon 5/15/17**
391	**Utilities**	**100 days**	**Thu 12/8/16**	**Mon 5/1/17**
392	Fire & H2O vaults	15 days	Thu 12/8/16	Thu 12/29/16
393	Electrical transformer	15 days	Thu 2/2/17	Wed 2/22/17
394	Energize Bldg. main SCL	30 days	Mon 3/20/17	Mon 5/1/17
395	**Street level**	**35 days**	**Tue 3/28/17**	**Mon 5/15/17**
396	ROW curb & sidewalk	20 days	Tue 4/4/17	Mon 5/1/17
397	Courtyard	20 days	Tue 3/28/17	Mon 4/24/17
398	Landscaping	15 days	Tue 4/25/17	Mon 5/15/17
399	**Project Inspections and TCO**	**19 days**	**Fri 6/16/17**	**Thu 7/13/17**
400	Interior finish final	10 days	Fri 6/16/17	Thu 6/29/17
401	Planning	1 day	Fri 6/30/17	Fri 6/30/17
402	Fire Alarm	5 days	Fri 6/30/17	Fri 7/7/17
403	Electrical final	5 days	Fri 6/30/17	Fri 7/7/17
404	Elevator	2 days	Mon 7/10/17	Tue 7/11/17
405	Balance & testing	6 days	Fri 6/30/17	Mon 7/10/17

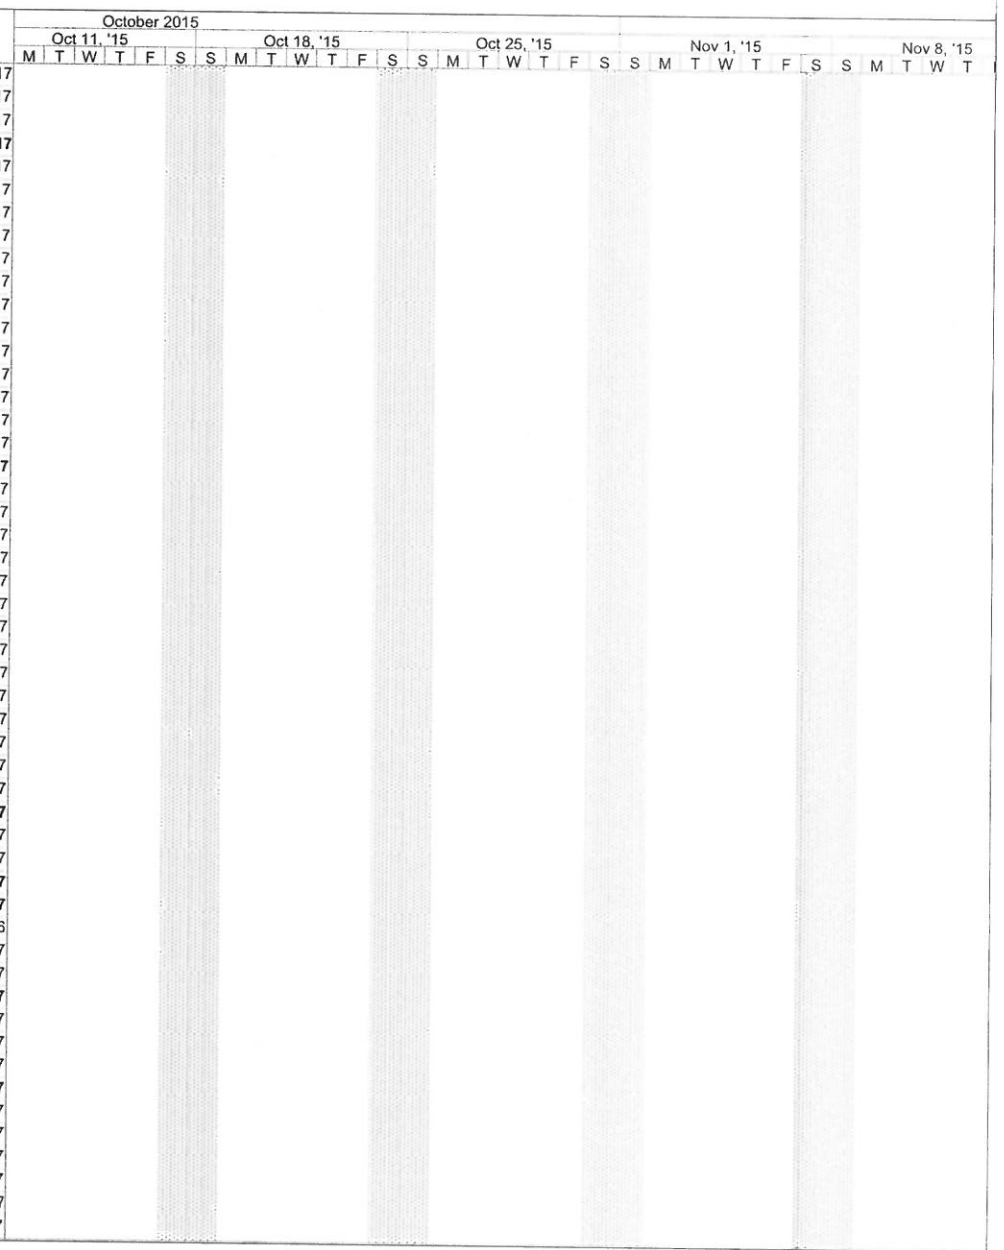

EXXEL PACIFIC
GENERAL CONTRACTORS

19 W. Harrison

ID	Task Name	Duration	Start	Finish
406	Substantial completion	3 days	Tue 7/11/17	Thu 7/13/17
407	**Final and Closeout**	**10 days**	**Fri 7/14/17**	**Thu 7/27/17**
408	Project Complete	10 days	Fri 7/14/17	Thu 7/27/17

October 2015
Oct 11, '15 | Oct 18, '15 | Oct 25, '15 | Nov 1, '15 | Nov 8, '15
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
