Hadley Mixed use
Legacy
3 wk Look ahead
1-11-2016

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
2		**North**	**6 days**	**Mon 1/11/16**	**Mon 1/18/16**
3		Drainline/Backfill NE Ret wall	2 days	Mon 1/11/16	Tue 1/12/16
4		Grade/Excavate Transformer Vault	3 days	Thu 1/14/16	Mon 1/18/16
5					
6		**PSE/Gas**	**2 days**	**Tue 1/26/16**	**Wed 1/27/16**
7		Permanent Service North	2 days	Tue 1/26/16	Wed 1/27/16
8		**Site/Structure**	**17 days**	**Mon 1/11/16**	**Tue 2/2/16**
9		**North**	**17 days**	**Mon 1/11/16**	**Tue 2/2/16**
10		Strip Stair Walls	3 days	Mon 1/11/16	Wed 1/13/16
11		F&P Transformer Rm Ftgs/SOG	4 days	Tue 1/19/16	Fri 1/22/16
12		F&P Transformer Walls	7 days	Mon 1/25/16	Tue 2/2/16
13					
14		**East**	**4 days**	**Mon 1/11/16**	**Thu 1/14/16**
15		Set Com Sleeves	2 days	Mon 1/11/16	Tue 1/12/16
16		Set Scaffold	4 days	Mon 1/11/16	Thu 1/14/16
17					
18		**Wood Framing/Roofing**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
19		**North/Southwest**	**6 days**	**Mon 1/11/16**	**Mon 1/18/16**
20		Parapet Cap	5 days	Tue 1/12/16	Mon 1/18/16
21		Set Mech Equipment	1 day	Mon 1/11/16	Mon 1/11/16
22		**Southeast**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
23		Frame Trellis Walls	4 days	Wed 1/13/16	Mon 1/18/16
24		Crickets	2 days	Mon 1/11/16	Tue 1/12/16
25		Roofing	8 days	Wed 1/13/16	Fri 1/22/16
26		Parapet Caps	5 days	Mon 1/25/16	Fri 1/29/16
27					
28		**Exterior**	**15 days**	**Mon 1/11/16**	**Fri 1/29/16**
29		**West**	**12 days**	**Mon 1/11/16**	**Tue 1/26/16**
30		Flashing Mock-up	2 days	Mon 1/11/16	Tue 1/12/16
31		Production Siding	10 days	Wed 1/13/16	Tue 1/26/16
32		**North**	**13 days**	**Wed 1/13/16**	**Fri 1/29/16**
33		Set Rem Scaffold	2 days	Wed 1/13/16	Thu 1/14/16
34		Prep Densglass/Trim Openings	3 days	Fri 1/15/16	Tue 1/19/16

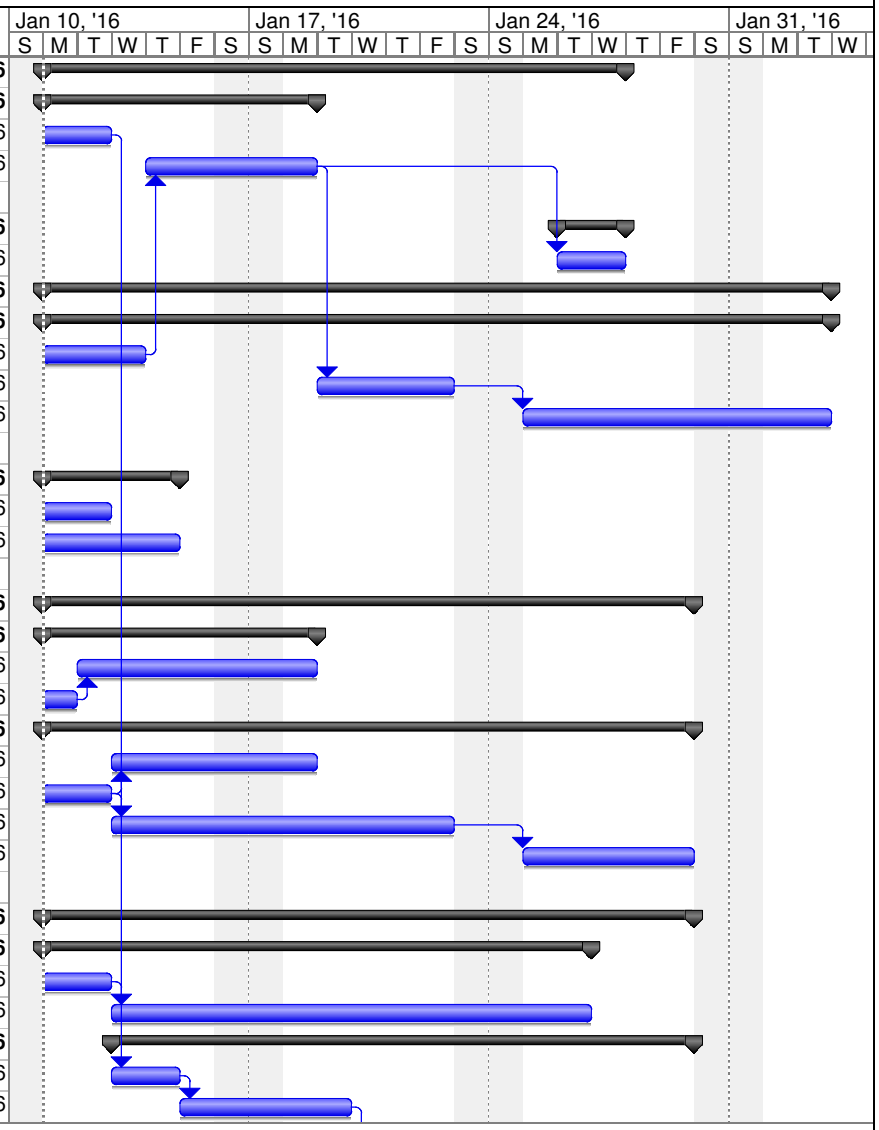

Project: 3wk 1-11-2016
Date: Mon 1/11/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
1-11-2016

ID		Task Name	Duration	Start	Finish
35		Wrap Openings/Set Windows	8 days	Wed 1/20/16	Fri 1/29/16
36					
37		**Courtyard**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
38		**East**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
39		Prep D-Glass/Openings	5 days	Mon 1/11/16	Fri 1/15/16
40		Wrap/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16
41		**East Face**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
42		Set Scaffold/Bonnet /Greenscreen	4 days	Mon 1/11/16	Thu 1/14/16
43		Fix Dens-Glass	5 days	Wed 1/13/16	Tue 1/19/16
44		Wrap/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16

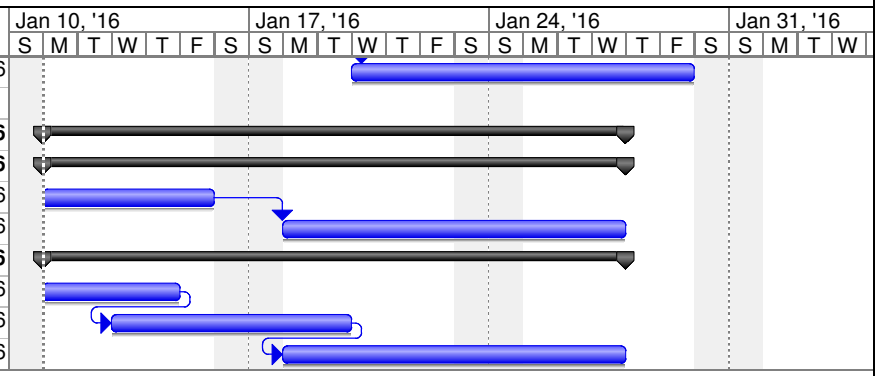

Project: 3wk 1-11-2016
Date: Mon 1/11/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
