Hadley Mixed use
Legacy
3 wk Look ahead
1-18-2016

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**10 days**	**Mon 1/18/16**	**Fri 1/29/16**
2		**North**	**3 days**	**Mon 1/18/16**	**Wed 1/20/16**
3		Drainline/Backfill NE Ret wall	2 days	Mon 1/18/16	Tue 1/19/16
4		Excavate Transformer Ftgs.	3 days	Mon 1/18/16	Wed 1/20/16
5					
6		**PSE/Gas**	**2 days**	**Thu 1/28/16**	**Fri 1/29/16**
7		North Gas Sleeve	2 days	Thu 1/28/16	Fri 1/29/16
8					
9		**Site/Structure**	**14 days**	**Mon 1/18/16**	**Thu 2/4/16**
10		**North**	**11 days**	**Thu 1/21/16**	**Thu 2/4/16**
11		F&P Transformer Rm Ftgs/SOG	4 days	Thu 1/21/16	Tue 1/26/16
12		F&P Transformer Walls	7 days	Wed 1/27/16	Thu 2/4/16
13		**East**	**4 days**	**Mon 1/18/16**	**Thu 1/21/16**
14		Set Scaffold	4 days	Mon 1/18/16	Thu 1/21/16
15					
16		**Wood Framing/Roofing**	**13 days**	**Mon 1/18/16**	**Wed 2/3/16**
17		**North/Southwest**	**6 days**	**Mon 1/18/16**	**Mon 1/25/16**
18		Parapet Cap	5 days	Tue 1/19/16	Mon 1/25/16
19		Set Mech Equipment	1 day	Mon 1/18/16	Mon 1/18/16
20		**Southeast**	**13 days**	**Mon 1/18/16**	**Wed 2/3/16**
21		Frame Trellis Walls	4 days	Wed 1/20/16	Mon 1/25/16
22		Crickets	2 days	Mon 1/18/16	Tue 1/19/16
23		Roofing	8 days	Mon 1/18/16	Wed 1/27/16
24		Parapet Caps	5 days	Thu 1/28/16	Wed 2/3/16
25					
26		**Exterior**	**10 days**	**Mon 1/18/16**	**Fri 1/29/16**
27		**West**	**10 days**	**Mon 1/18/16**	**Fri 1/29/16**
28		Rem. L3 Glass	1 day	Mon 1/18/16	Mon 1/18/16
29		Battons/Siding	10 days	Mon 1/18/16	Fri 1/29/16
30		**South**	**2 days**	**Wed 1/20/16**	**Thu 1/21/16**
31		Set Windows	2 days	Wed 1/20/16	Thu 1/21/16
32					
33		**North**	**10 days**	**Mon 1/18/16**	**Fri 1/29/16**
34		Set Rem Scaffold	2 days	Mon 1/18/16	Tue 1/19/16

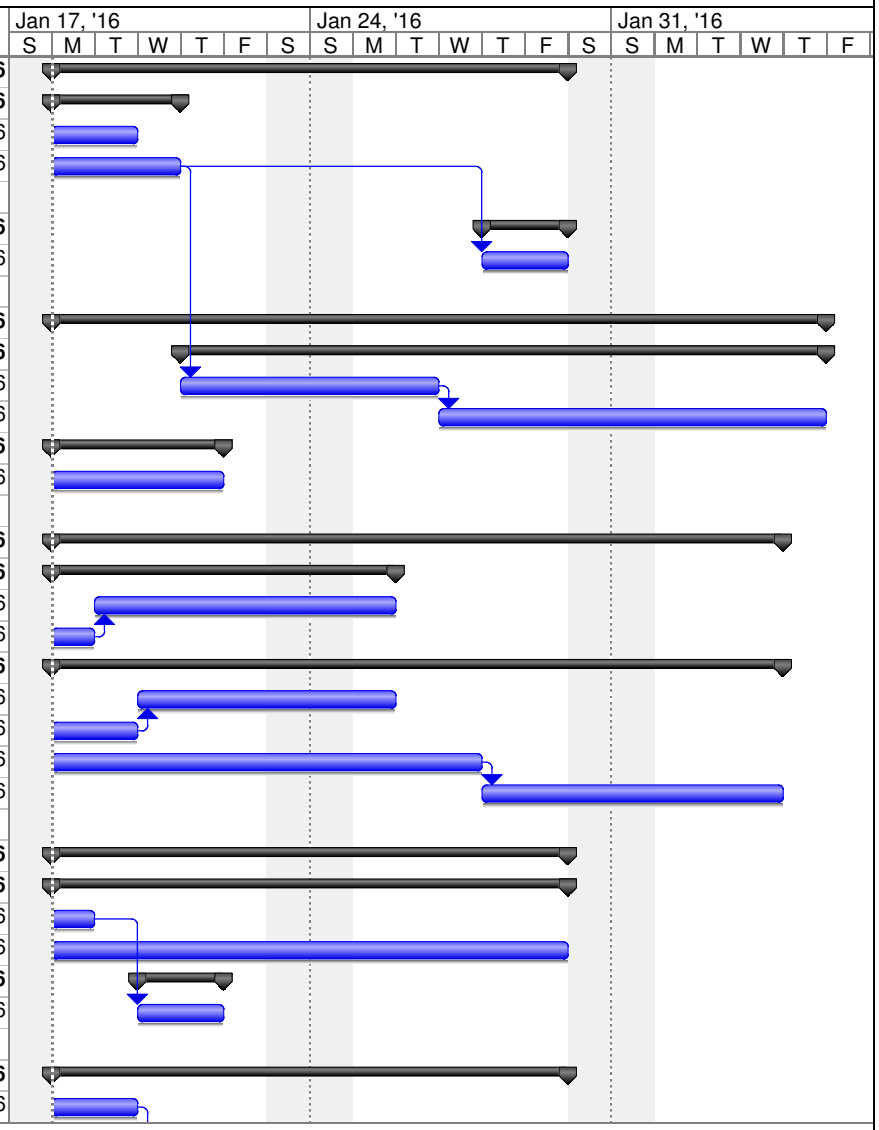

Project: 3wk 1-18-2016
Date: Mon 1/18/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
1-18-2016

ID		Task Name	Duration	Start	Finish
35		Prep Densglass/Trim Openings	3 days	Wed 1/20/16	Fri 1/22/16
36		Wrap Openings/Set Windows	5 days	Mon 1/25/16	Fri 1/29/16
37					
38		**Courtyard**	**8 days**	**Mon 1/18/16**	**Wed 1/27/16**
39		**East**	**8 days**	**Mon 1/18/16**	**Wed 1/27/16**
40		Wrap/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16
41		**East Face**	**13 days**	**Mon 1/18/16**	**Wed 2/3/16**
42		Set Scaffold/Bonnet /Greenscreen	4 days	Mon 1/18/16	Thu 1/21/16
43		Fix Dens-Glass	5 days	Wed 1/20/16	Tue 1/26/16
44		Wrap/Set Windows	8 days	Mon 1/25/16	Wed 2/3/16

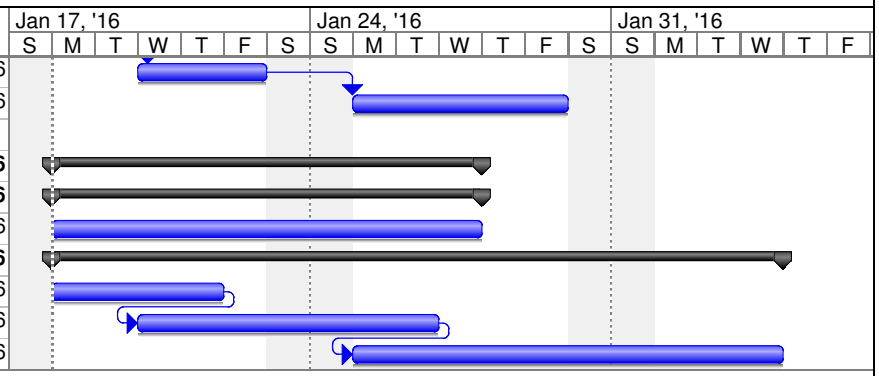

Project: 3wk 1-18-2016
Date: Mon 1/18/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
