Hadley Mixed use
Legacy
3 wk Look ahead
2-1-2016

ID		Task Name	Duration	Start	Finish	Predecessors
1		**Site Grading/Utilities**	**6 days**	**Fri 2/5/16**	**Fri 2/12/16**	
2		**North**	**6 days**	**Fri 2/5/16**	**Fri 2/12/16**	
3		Install Gas Sleeve	2 days	Mon 2/8/16	Tue 2/9/16	10FS-5 days
4		Backfill Crane Pad	1 day	Fri 2/5/16	Fri 2/5/16	10FS-6 days
5		Demob Crane	2 days	Thu 2/11/16	Fri 2/12/16	4FS+3 days
6						
7		**Site/Structure**	**10 days**	**Mon 2/1/16**	**Fri 2/12/16**	
8		**North**	**10 days**	**Mon 2/1/16**	**Fri 2/12/16**	
9		F&P Transformer Rm Ftgs/SOG	4 days	Mon 2/1/16	Thu 2/4/16	
10		F&P Transformer Walls	7 days	Thu 2/4/16	Fri 2/12/16	9FS-1 day
11						
12		**Wood Framing/Roofing**	**5 days**	**Mon 2/1/16**	**Fri 2/5/16**	
13		**North/Southwest**	**5 days**	**Mon 2/1/16**	**Fri 2/5/16**	
14		Parapet Cap	3 days	Mon 2/1/16	Wed 2/3/16	
15		Set Mech Equipment	5 days	Mon 2/1/16	Fri 2/5/16	
16						
17						
18		**Southeast**	**12 days**	**Mon 2/1/16**	**Tue 2/16/16**	
23		Complete Crickets	4 days	Mon 2/1/16	Thu 2/4/16	
24		Roof	2 days	Fri 2/5/16	Mon 2/8/16	23
25		Paper Penthouses	2 days	Tue 2/9/16	Wed 2/10/16	24
26		Set Windows	1 day	Thu 2/11/16	Thu 2/11/16	25
27						
28		**Exterior**	**10 days**	**Mon 2/1/16**	**Fri 2/12/16**	
29		**West**	**10 days**	**Mon 2/1/16**	**Fri 2/12/16**	
30		Window Test West L5/6	1 day	Mon 2/1/16	Mon 2/1/16	
31		Battons/Siding West	10 days	Mon 2/1/16	Fri 2/12/16	
32		**South**	**2 days**	**Mon 2/1/16**	**Tue 2/2/16**	
33		Set Windows	2 days	Mon 2/1/16	Tue 2/2/16	
34		**North**	**6 days**	**Mon 2/1/16**	**Mon 2/8/16**	
35		Tyvek	3 days	Mon 2/1/16	Wed 2/3/16	
36		Wrap Openings/Set Windows	5 days	Tue 2/2/16	Mon 2/8/16	35FS-2 days
37						
38		**Courtyard**	**4 days**	**Mon 2/1/16**	**Thu 2/4/16**	

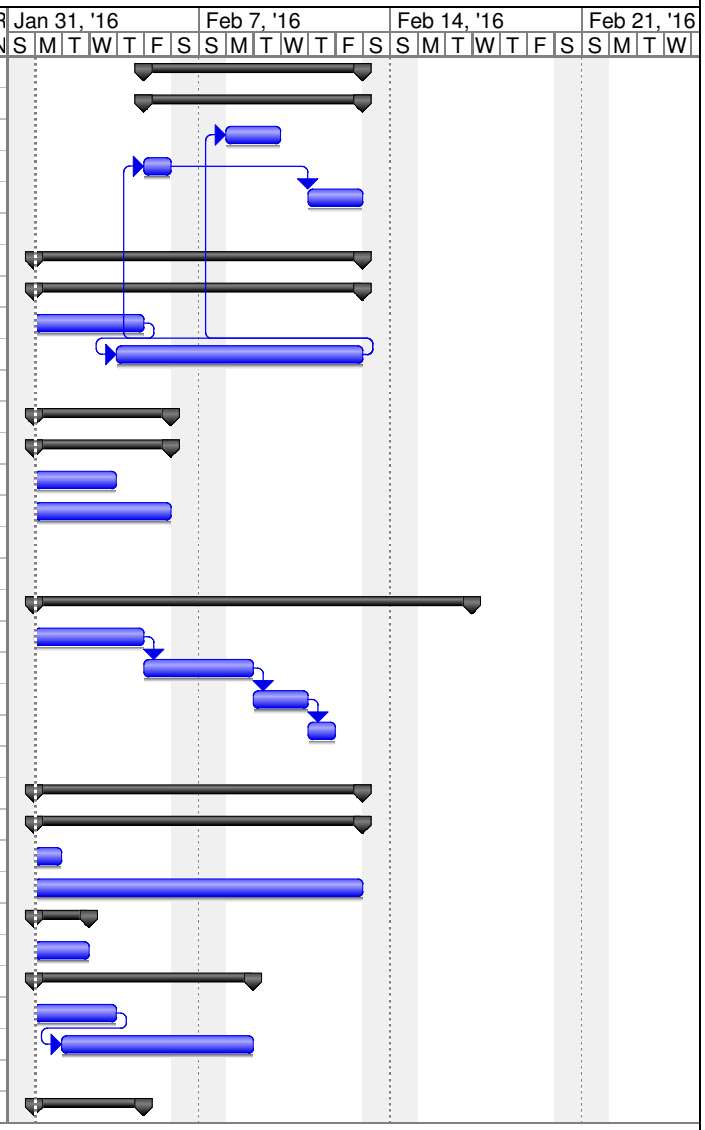

Project: 3wk 2-1-2016
Date: Mon 2/1/16

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

Hadley Mixed use
Legacy
3 wk Look ahead
2-1-2016

ID		Task Name	Duration	Start	Finish	Predecessors
39		**East**	**3 days**	**Mon 2/1/16**	**Wed 2/3/16**	
40		Wrap/Set Windows	3 days	Mon 2/1/16	Wed 2/3/16	
41		**North**	**4 days**	**Mon 2/1/16**	**Thu 2/4/16**	
42		Scaffold Accsess Unit	1 day	Mon 2/1/16	Mon 2/1/16	
43		Replace Densglass/Set Windows	4 days	Mon 2/1/16	Thu 2/4/16	
44		**East Perimeter**	**17 days**	**Mon 2/1/16**	**Tue 2/23/16**	
45		Scaffold/Bonnet /Greenscreen	2 days	Mon 2/1/16	Tue 2/2/16	
46		Fix Dens-Glass	6 days	Mon 2/1/16	Mon 2/8/16	
47		Tyvek	3 days	Tue 2/9/16	Thu 2/11/16	46
48		Wrap/Set Windows	8 days	Fri 2/12/16	Tue 2/23/16	47

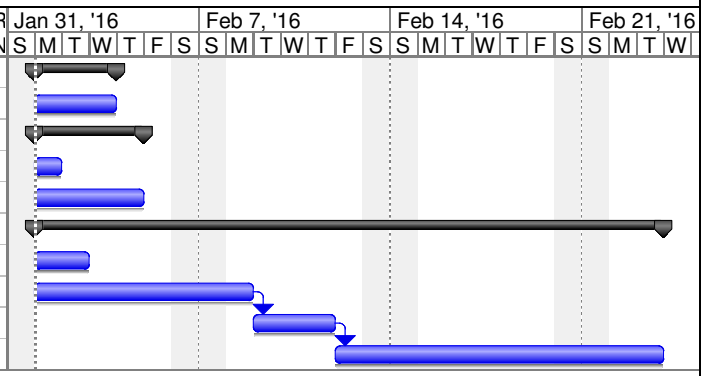

Project: 3wk 2-1-2016
Date: Mon 2/1/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
