Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016

Exterior

ID		Task Name	Duration	Start	Finish
1		**Garage**	**23 days**	**Mon 3/21/16**	**Wed 4/20/16**
2		**Level P**	**16 days**	**Mon 3/21/16**	**Mon 4/11/16**
3		Pull Secondary's	3 days	Mon 3/21/16	Wed 3/23/16
4		Set Transformer/Pull main	3 days	Thu 4/7/16	Mon 4/11/16
5		FT Plywood Comm Rm.	3 days	Mon 3/21/16	Wed 3/23/16
6		Swing Elect HM doors	2 days	Thu 3/24/16	Fri 3/25/16
7		Light Fixtures Garage	10 days	Mon 3/21/16	Fri 4/1/16
8					
9		**Level 1**	**13 days**	**Mon 3/21/16**	**Wed 4/6/16**
10		Replace Rock	5 days	Mon 3/21/16	Fri 3/25/16
11		Swing HM	2 days	Mon 3/28/16	Tue 3/29/16
12		Garage Light Fixtures	5 days	Tue 3/29/16	Mon 4/4/16
13		Insulate Lid	7 days	Tue 3/29/16	Wed 4/6/16
14					
15		**Level 2**	**23 days**	**Mon 3/21/16**	**Wed 4/20/16**
16		Complete Insul/Dens-Glass Ext L@	2 days	Mon 3/21/16	Tue 3/22/16
17		Tyvek Wrap	2 days	Wed 3/23/16	Thu 3/24/16
18		Set Doors/Windows	3 days	Fri 3/25/16	Tue 3/29/16
19		Insulate Lids	10 days	Thu 4/7/16	Wed 4/20/16
20		Garage Lights	5 days	Mon 3/21/16	Fri 3/25/16
21					
22		**Site/Structure**	**17 days**	**Mon 3/21/16**	**Tue 4/12/16**
23		**North**	**17 days**	**Mon 3/21/16**	**Tue 4/12/16**
24		Gas Main/Manifold	5 days	Mon 3/21/16	Fri 3/25/16
25		Install Gas Branch lines	3 days	Mon 3/28/16	Wed 3/30/16
26		Install Vault Grating and Gate	4 days	Mon 3/21/16	Thu 3/24/16
27		Set Transformer/Pull Mains	3 days	Fri 4/8/16	Tue 4/12/16
28					
29		**/Roofing**	**3 days**	**Mon 3/21/16**	**Wed 3/23/16**
30		**North/Southwest**	**3 days**	**Mon 3/21/16**	**Wed 3/23/16**
31		Walk Mats	3 days	Mon 3/21/16	Wed 3/23/16
32		Carlisle Inspection	1 day	Mon 3/21/16	Mon 3/21/16
33		BCRA Inspection	1 day	Mon 3/21/16	Mon 3/21/16
34					

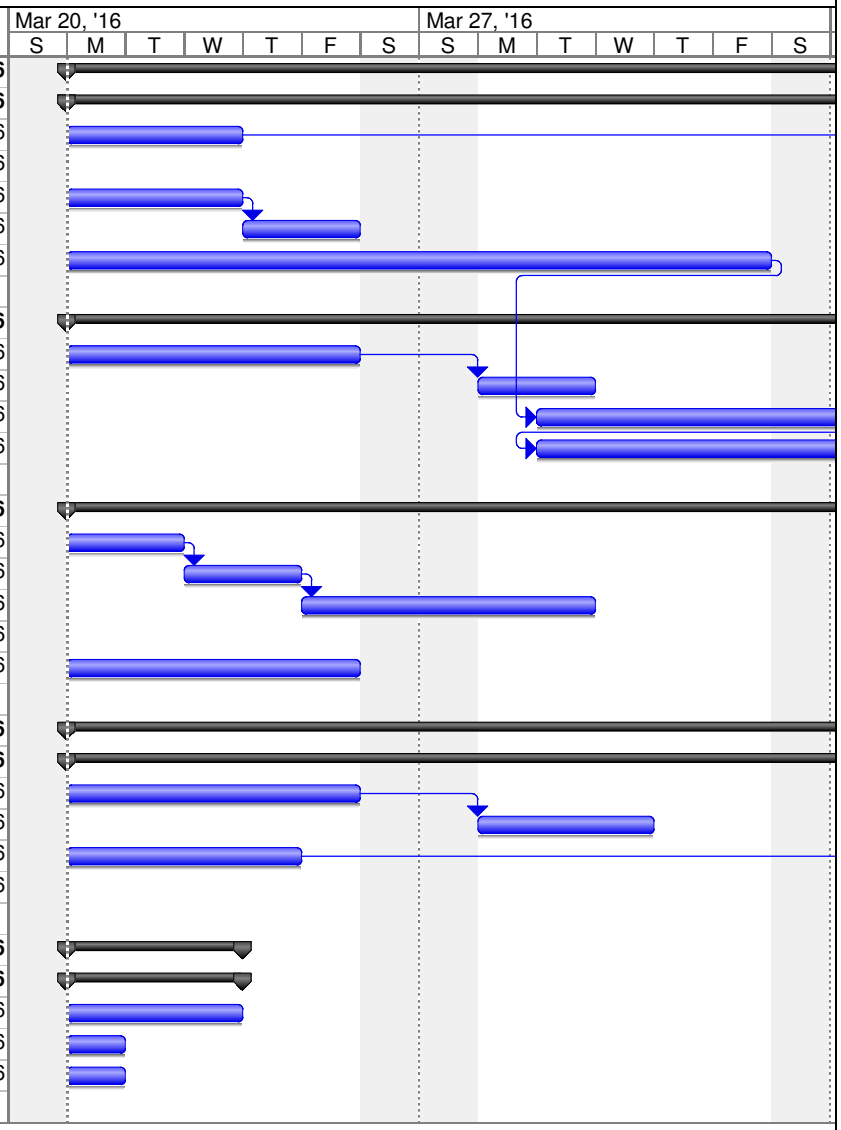

Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016

ID	Task Name	Duration	Start	Finish
35	**Penthouses**	**12 days**	**Mon 3/21/16**	**Tue 4/5/16**
40	Tyvek	1 day	Mon 3/21/16	Mon 3/21/16
41	Battons	3 days	Tue 3/22/16	Thu 3/24/16
42	Joist Walkway	4 days	Fri 3/25/16	Wed 3/30/16
43				
44	**Exterior**	**19 days**	**Mon 3/21/16**	**Thu 4/14/16**
45	**West**	**16 days**	**Mon 3/21/16**	**Mon 4/11/16**
46	Siding West	3 days	Mon 3/21/16	Wed 3/23/16
47	Stucco	5 days	Tue 3/22/16	Mon 3/28/16
48	Sill Flashing	4 days	Mon 3/21/16	Thu 3/24/16
49	Paint Mock-up	2 days	Thu 3/24/16	Fri 3/25/16
50	Paint	4 days	Mon 3/28/16	Thu 3/31/16
51	Caukling	3 days	Fri 4/1/16	Tue 4/5/16
52	Inspection	1 day	Wed 4/6/16	Wed 4/6/16
53	Remove Scafflod	3 days	Thu 4/7/16	Mon 4/11/16
54	**North**	**19 days**	**Mon 3/21/16**	**Thu 4/14/16**
55	Stucco	8 days	Mon 3/21/16	Wed 3/30/16
56	Siding	10 days	Thu 3/31/16	Wed 4/13/16
57	Tyvek L2	2 days	Fri 4/8/16	Mon 4/11/16
58	Set Windows/Doors	3 days	Tue 4/12/16	Thu 4/14/16
59				
60	**Courtyard**	**32 days**	**Mon 3/21/16**	**Tue 5/3/16**
61	Siding/Panels	5 days	Mon 3/21/16	Fri 3/25/16
62	Sill Flashing	5 days	Mon 3/28/16	Fri 4/1/16
63	Paint	10 days	Mon 4/4/16	Fri 4/15/16
64	Caulk	7 days	Mon 4/18/16	Tue 4/26/16
65	Inspect	1 day	Wed 4/27/16	Wed 4/27/16
66	Remove Scaffolding	4 days	Thu 4/28/16	Tue 5/3/16
67				
68	**East Perimeter**	**25 days**	**Mon 3/21/16**	**Fri 4/22/16**
69	Flashing	2 days	Mon 3/21/16	Tue 3/22/16
70	Siding	13 days	Wed 3/23/16	Fri 4/8/16
71	Storefront	15 days	Mon 4/4/16	Fri 4/22/16
72	**South**	**20 days**	**Mon 3/21/16**	**Fri 4/15/16**

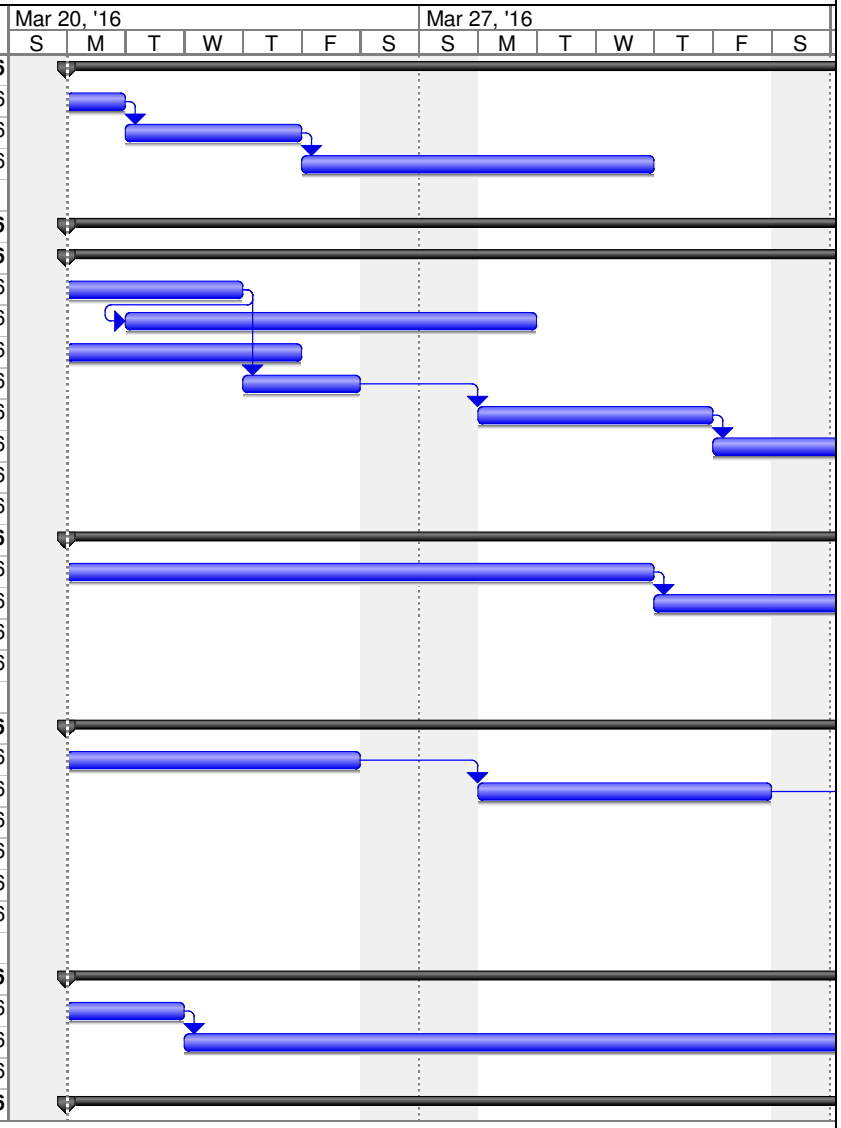

Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016

ID		Task Name	Duration	Start	Finish
73		Stucco	10 days	Mon 3/21/16	Fri 4/1/16
74		Siding	10 days	Mon 4/4/16	Fri 4/15/16



Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016

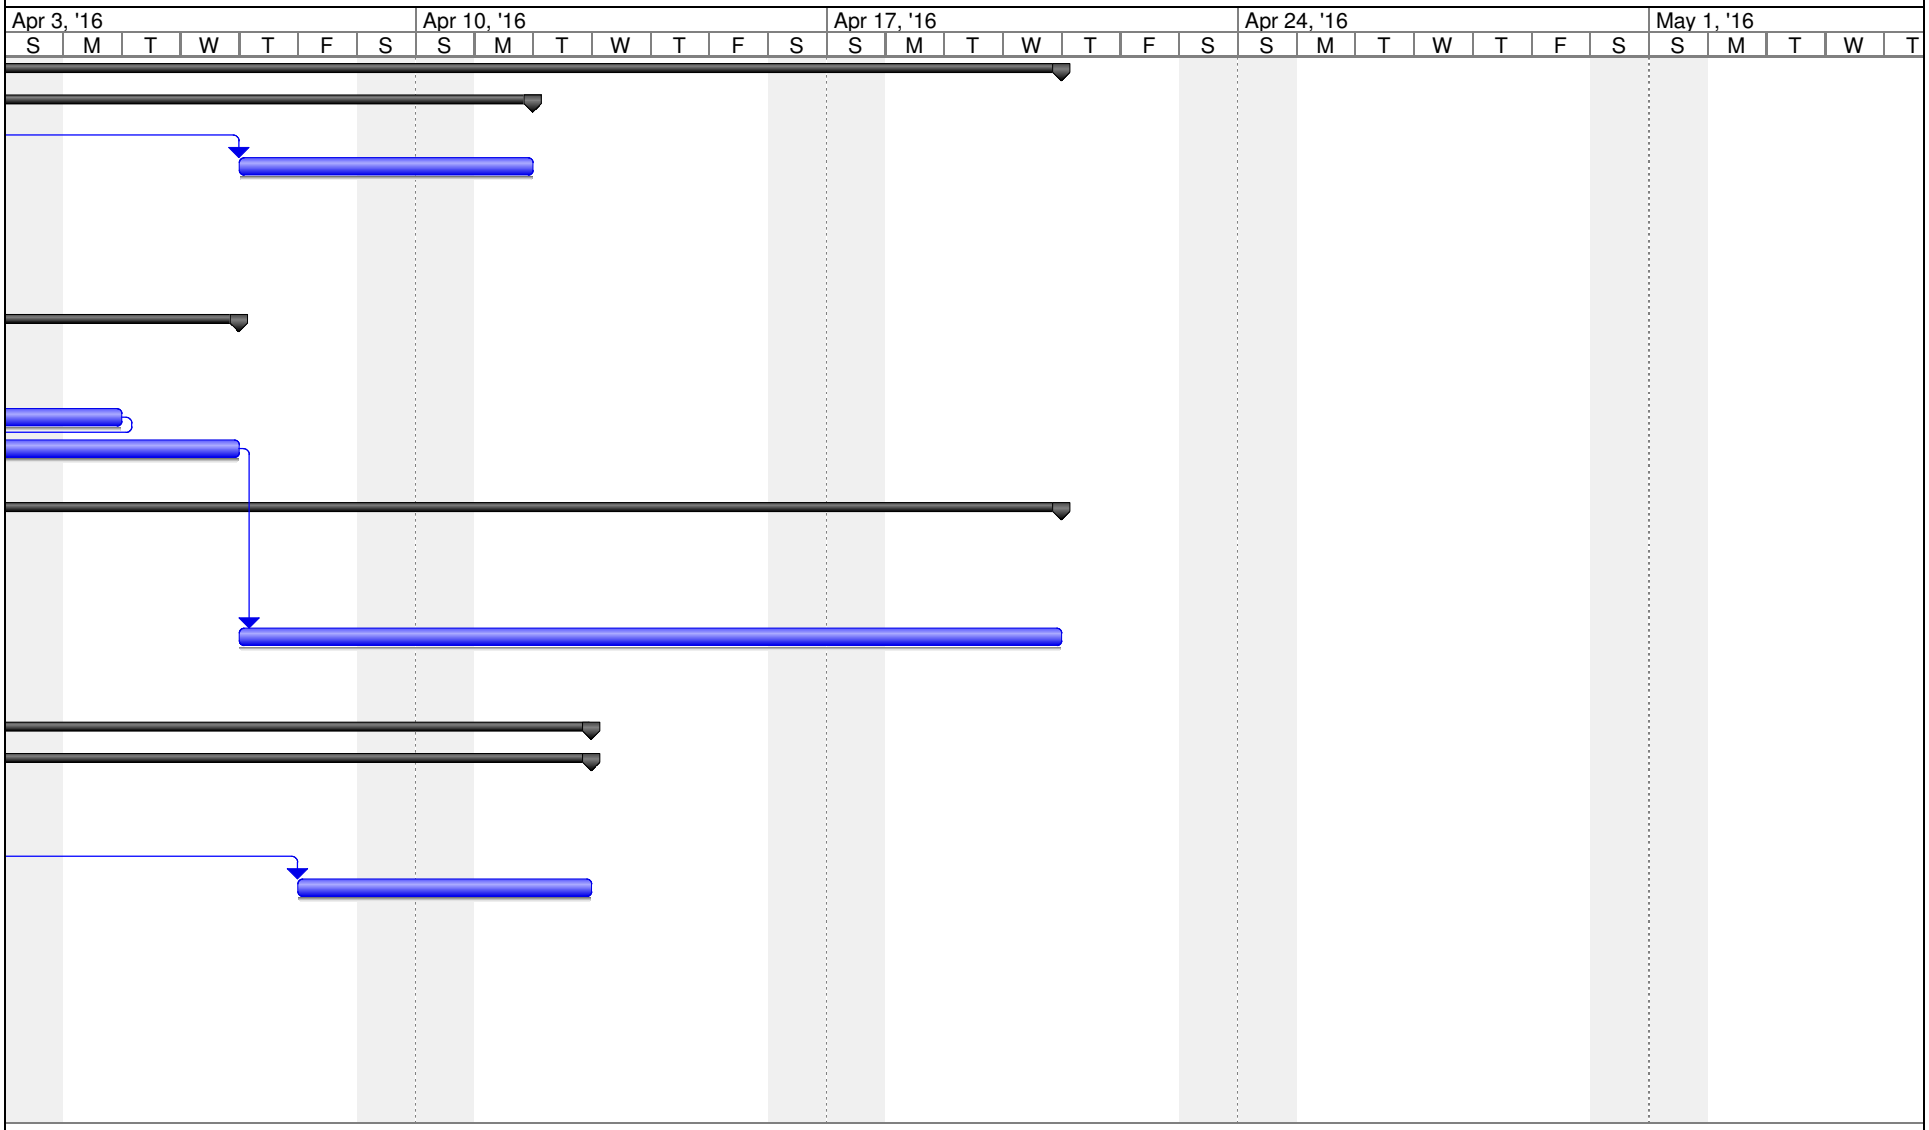

Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016

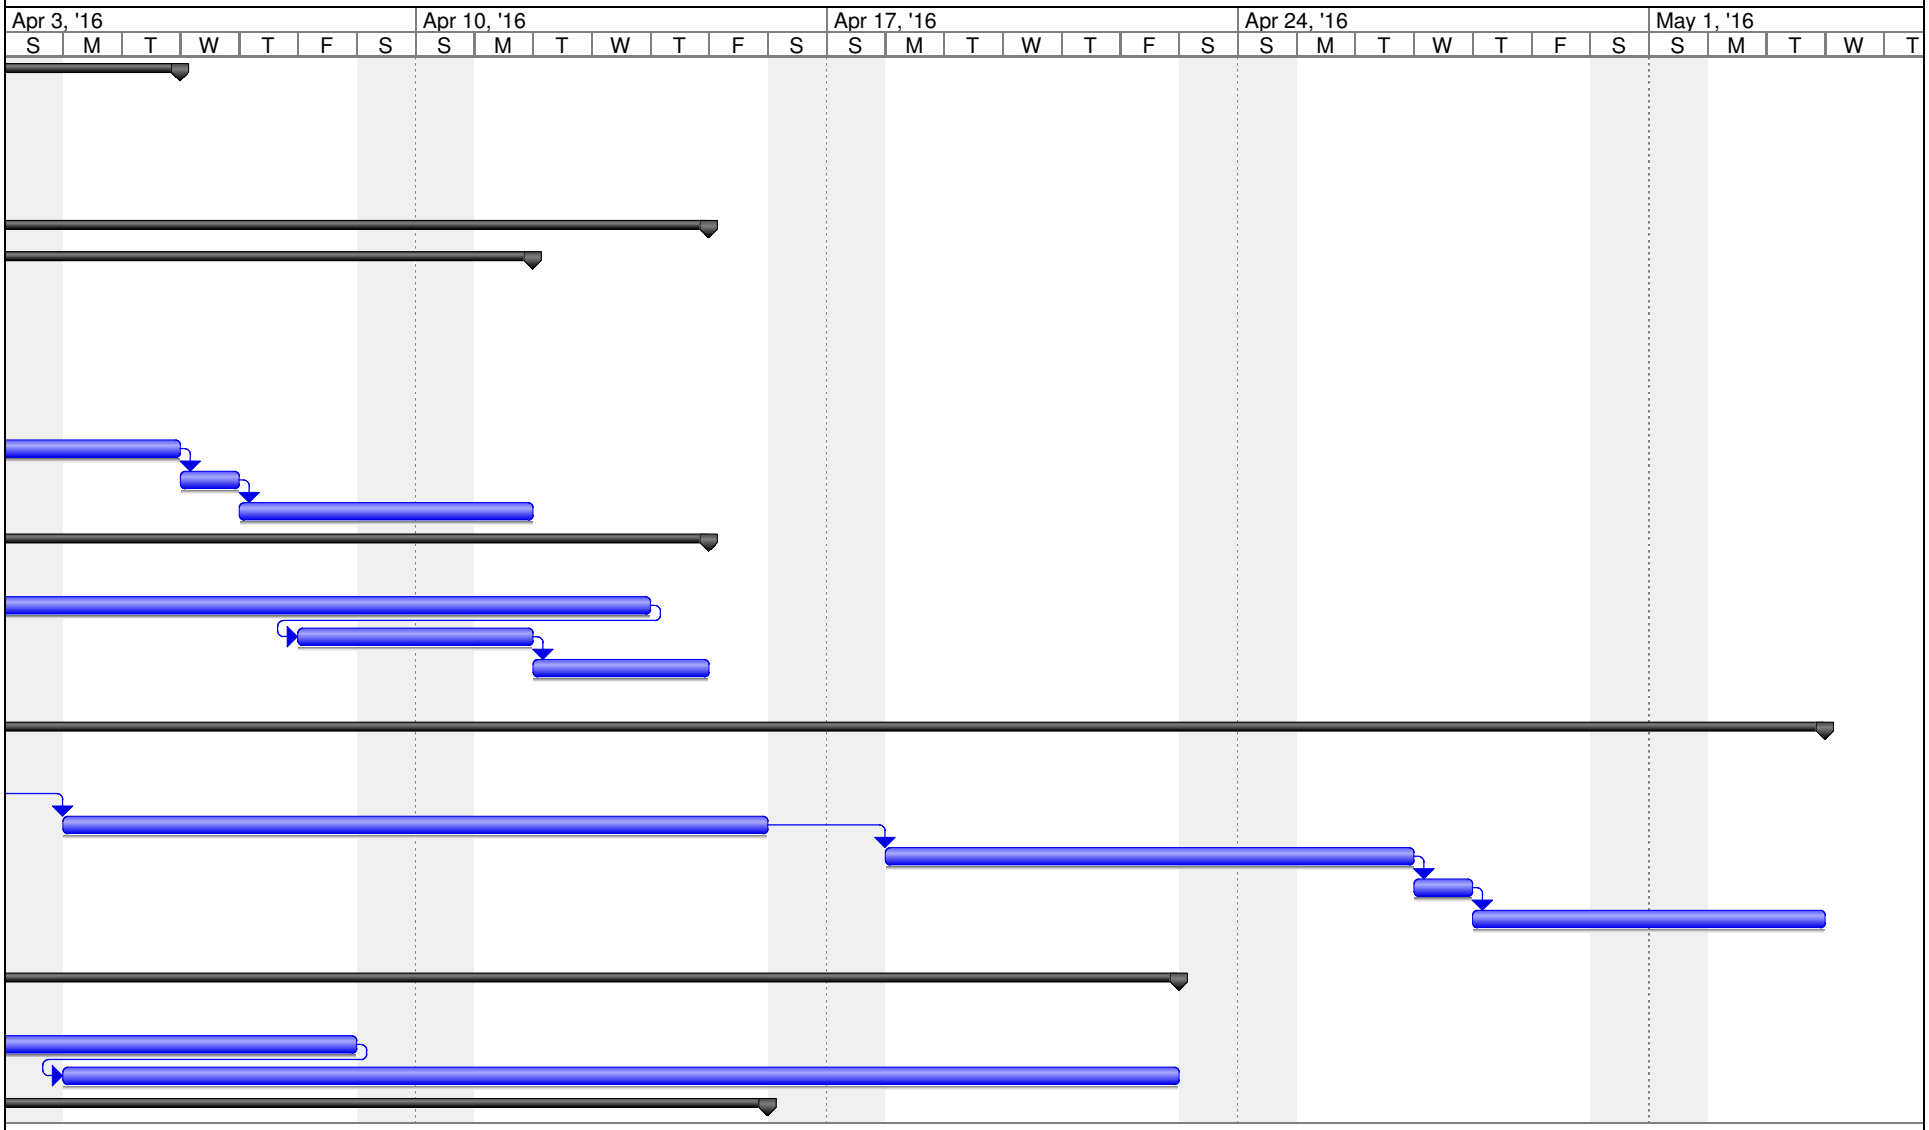

Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
3-21-2016



Project: 3wk 3-21-16 3wk
Date: Mon 3/21/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
