Hadley Mixed use
Legacy
3 wk Look ahead
1-4-2016

ID		Task Name	Duration	Start	Finish
1		**Site Grading/Utilities**	**10 days**	**Thu 1/7/16**	**Wed 1/20/16**
2		**North**	**3 days**	**Thu 1/7/16**	**Mon 1/11/16**
3		Backfill NE Ret wall	2 days	Thu 1/7/16	Fri 1/8/16
4		Grade/Excavate Transformer Vault	3 days	Thu 1/7/16	Mon 1/11/16
5					
6		**PSE/Gas**	**2 days**	**Tue 1/19/16**	**Wed 1/20/16**
7		Permanent Service North	2 days	Tue 1/19/16	Wed 1/20/16
8		**Site/Structure**	**17 days**	**Mon 1/4/16**	**Tue 1/26/16**
9		**North**	**17 days**	**Mon 1/4/16**	**Tue 1/26/16**
10		Stair Ftgs/Walls	3 days	Mon 1/4/16	Wed 1/6/16
11		F&P Transformer Rm Ftgs/SOG	4 days	Tue 1/12/16	Fri 1/15/16
12		F&P Transformer Walls	7 days	Mon 1/18/16	Tue 1/26/16
13					
14		**East**	**7 days**	**Tue 1/12/16**	**Wed 1/20/16**
15		Demob LAB Conex	1 day	Tue 1/12/16	Tue 1/12/16
16		Set Com Sleeves	2 days	Wed 1/13/16	Thu 1/14/16
17		Set Scaffold	4 days	Fri 1/15/16	Wed 1/20/16
18					
19		**Wood Framing/Roofing**	**17 days**	**Mon 1/4/16**	**Tue 1/26/16**
20		**North/Southwest**	**8 days**	**Mon 1/4/16**	**Wed 1/13/16**
21		Roof/Trimout	3 days	Mon 1/4/16	Wed 1/6/16
22		Parapet Cap	5 days	Thu 1/7/16	Wed 1/13/16
23		Set Mech Equipment	2 days	Tue 1/12/16	Wed 1/13/16
24		**Southeast**	**17 days**	**Mon 1/4/16**	**Tue 1/26/16**
25		Frame Trellis Walls	4 days	Fri 1/8/16	Wed 1/13/16
26		Crickets	4 days	Mon 1/4/16	Thu 1/7/16
27		Roofing	8 days	Fri 1/8/16	Tue 1/19/16
28		Parapet Caps	5 days	Wed 1/20/16	Tue 1/26/16
29					
30		**Exterior**	**18 days**	**Mon 1/4/16**	**Wed 1/27/16**
31		**West**	**13 days**	**Mon 1/4/16**	**Wed 1/20/16**
32		Tyvek West	1 day	Mon 1/4/16	Mon 1/4/16
33		Flashing Mock-up	2 days	Tue 1/5/16	Wed 1/6/16
34		Production Siding	10 days	Thu 1/7/16	Wed 1/20/16

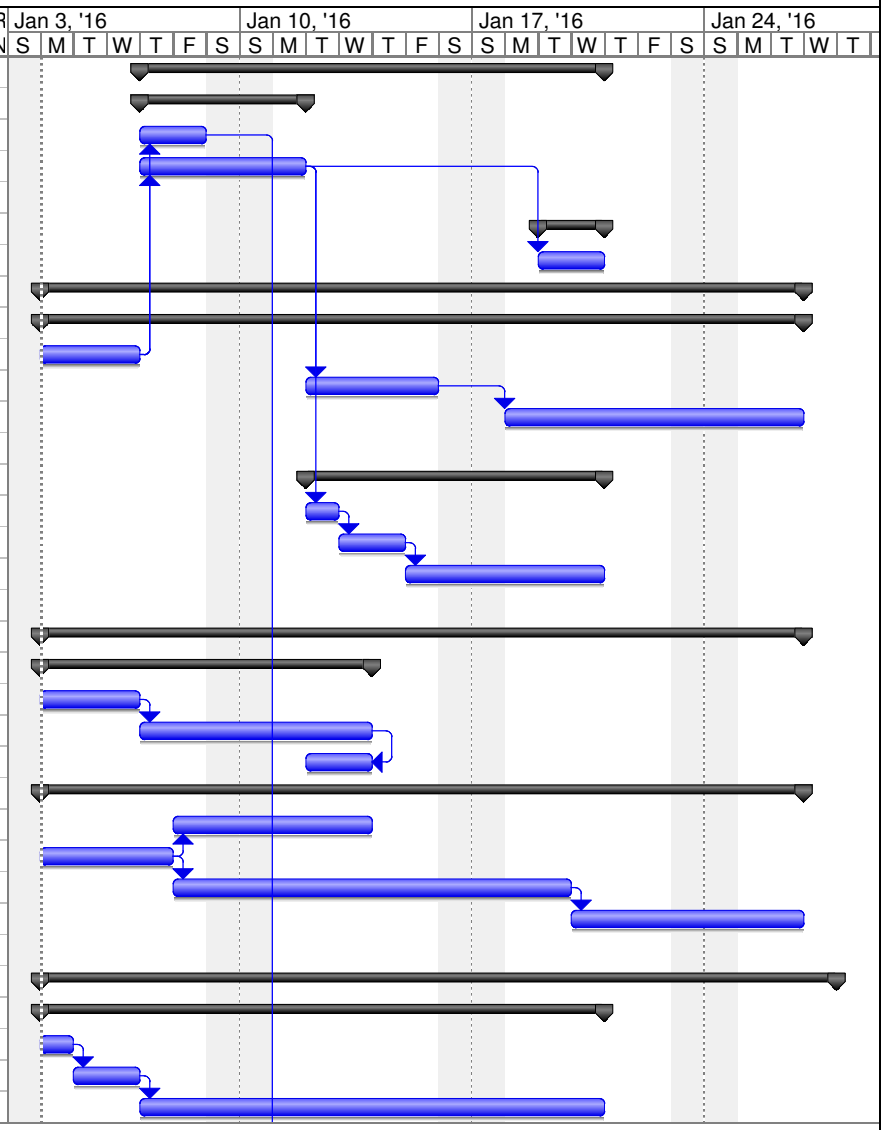

Project: 3wk 1-4-2016
Date: Mon 1/4/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
1-4-2016

ID		Task Name	Duration	Start	Finish
35		**North**	**13 days**	**Mon 1/11/16**	**Wed 1/27/16**
36		Set Rem Scaffold	2 days	Mon 1/11/16	Tue 1/12/16
37		Prep Densglass/Trim Openings	3 days	Wed 1/13/16	Fri 1/15/16
38		Wrap Openings/Set Windows	8 days	Mon 1/18/16	Wed 1/27/16
39					
40		**Courtyard**	**13 days**	**Mon 1/4/16**	**Wed 1/20/16**
41		**East**	**13 days**	**Mon 1/4/16**	**Wed 1/20/16**
42		Prep D-Glass/Openings	5 days	Mon 1/4/16	Fri 1/8/16
43		Wrap/Set Windows	8 days	Mon 1/11/16	Wed 1/20/16

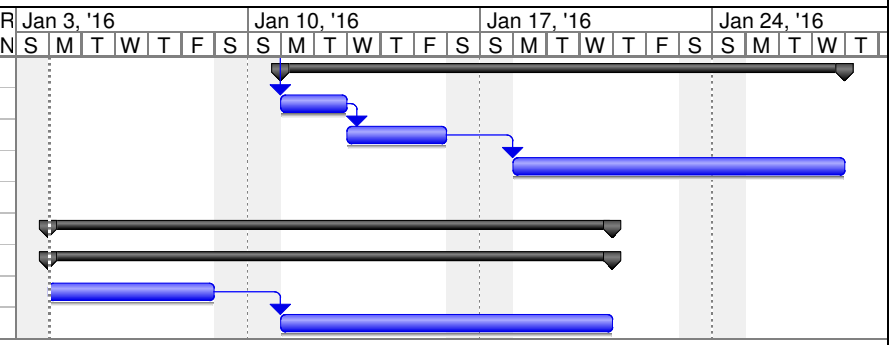

Project: 3wk 1-4-2016
Date: Mon 1/4/16

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
