Hadley Mixed use
Legacy
3 wk Look ahead
12-21-2015

ID	Task Name	Duration	Start	Finish
1	**Site Grading/Utilities**	**8 days**	**Mon 12/21/15**	**Tue 1/5/16**
2	**North**	**3 days**	**Mon 12/21/15**	**Wed 12/23/15**
3	Backfill NE Ret wall	1 day	Mon 12/21/15	Mon 12/21/15
4	Grade/Excavate Transformer Vault	3 days	Mon 12/21/15	Wed 12/23/15
5				
6	**PSE/Gas**	**8 days**	**Mon 12/21/15**	**Tue 1/5/16**
7	Temp Service South	3 days	Mon 12/21/15	Wed 12/23/15
8	Permanent Service North	2 days	Mon 1/4/16	Tue 1/5/16
9				
10	**Site/Structure**	**17 days**	**Mon 12/21/15**	**Mon 1/18/16**
11	**North**	**17 days**	**Mon 12/21/15**	**Mon 1/18/16**
12	Stair Ftgs/Walls	4 days	Mon 12/21/15	Mon 12/28/15
13	F&P Transformer Rm Ftgs/SOG	3 days	Mon 1/4/16	Wed 1/6/16
14	F&P Transformer Walls	8 days	Thu 1/7/16	Mon 1/18/16
15				
16	**South**	**2 days**	**Mon 1/4/16**	**Tue 1/5/16**
17	Set Scaffold	2 days	Mon 1/4/16	Tue 1/5/16
18				
19	**Wood Framing/Roofing**	**15 days**	**Mon 12/21/15**	**Thu 1/14/16**
20	**North/Southwest**	**3 days**	**Mon 12/21/15**	**Wed 12/23/15**
21	Roof	3 days	Mon 12/21/15	Wed 12/23/15
22	**Penthouse SE**	**3 days**	**Mon 12/21/15**	**Wed 12/23/15**
23	Joist/Sheath	3 days	Mon 12/21/15	Wed 12/23/15
24	**Southeast**	**15 days**	**Mon 12/21/15**	**Thu 1/14/16**
25	Frame Trellis Walls	4 days	Mon 1/4/16	Thu 1/7/16
26	Walkway Stanchions	3 days	Mon 12/21/15	Wed 12/23/15
27	Crickets	7 days	Mon 12/21/15	Mon 1/4/16
28	Roofing	8 days	Tue 1/5/16	Thu 1/14/16
29				
30	**Exterior**	**30 days**	**Mon 12/21/15**	**Thu 2/4/16**
31	**West**	**10 days**	**Mon 12/21/15**	**Thu 1/7/16**
32	Wrap/Set Door Pans/ Windows West	4 days	Mon 12/21/15	Mon 12/28/15
33	Tyvek West	1 day	Tue 12/29/15	Tue 12/29/15
34	Siding/Flashing Mock-up West	5 days	Wed 12/30/15	Thu 1/7/16

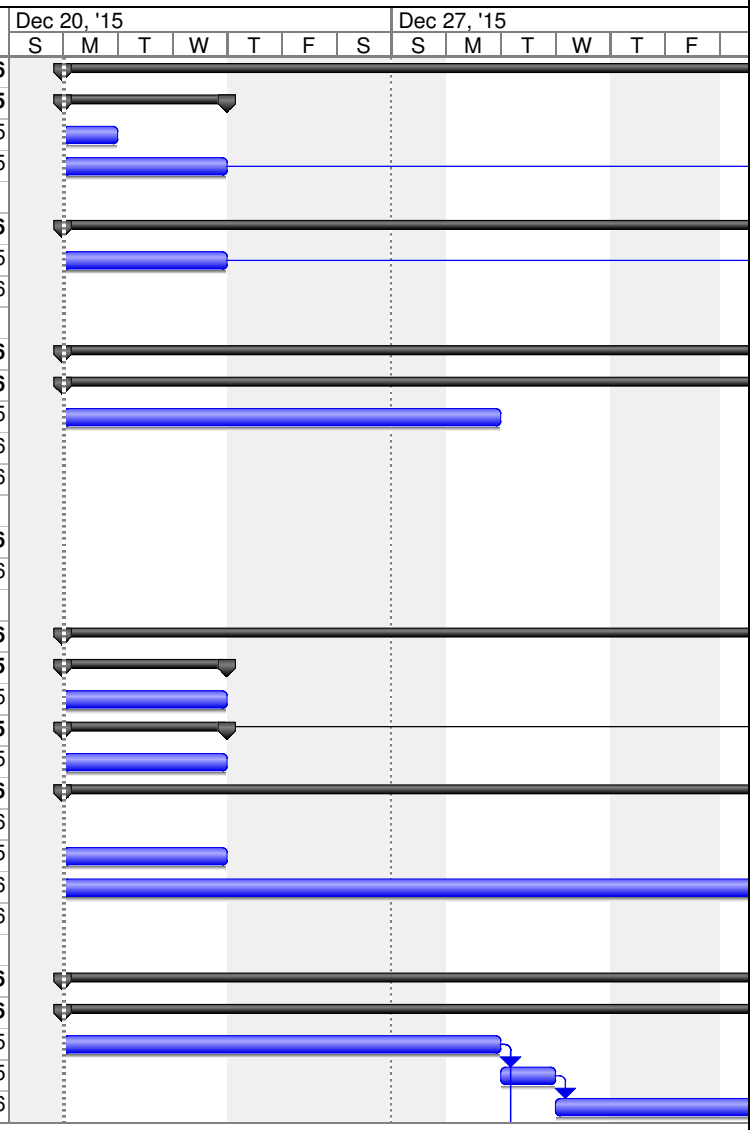

Project: 3wk 12-21-2015
Date: Mon 12/21/15

Task | Milestone | External Tasks
Split | Summary | External Milestone
Progress | Project Summary | Deadline

Hadley Mixed use
Legacy
3 wk Look ahead
12-21-2015

ID		Task Name	Duration	Start	Finish
35					
36		**North**	**13 days**	**Tue 1/19/16**	**Thu 2/4/16**
37		Set Rem Scaffold	2 days	Tue 1/19/16	Wed 1/20/16
38		Prep Densglass/Trim Openings	3 days	Thu 1/21/16	Mon 1/25/16
39		Wrap Openings/Set Windows	8 days	Tue 1/26/16	Thu 2/4/16
40					
41		**Courtyard**	**6 days**	**Tue 12/29/15**	**Thu 1/7/16**
42		**West**	**6 days**	**Tue 12/29/15**	**Thu 1/7/16**
43		Prep D-Glass/Openings	2 days	Tue 12/29/15	Wed 12/30/15
44		Wrap/Set Windows	6 days	Tue 12/29/15	Thu 1/7/16
45					
46		**Temp Heat**	**4 days**	**Mon 12/21/15**	**Mon 12/28/15**
47		Deliver/Set Equipment	3 days	Mon 12/21/15	Wed 12/23/15
48		Temp Heat West	1 day	Mon 12/28/15	Mon 12/28/15

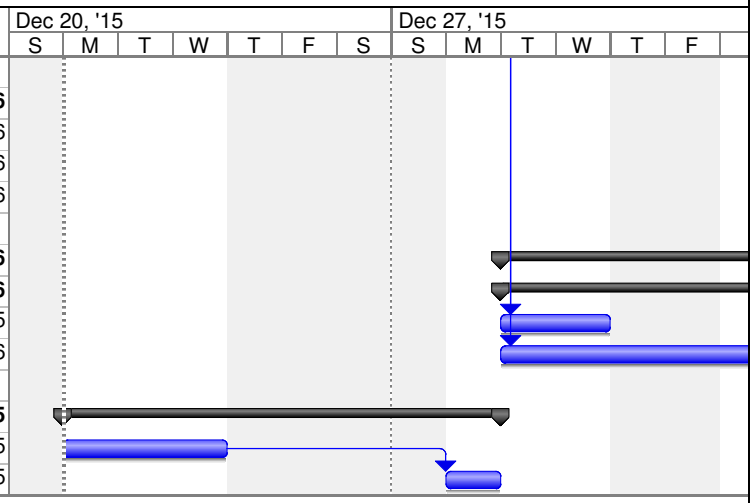

Project: 3wk 12-21-2015
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
12-21-2015

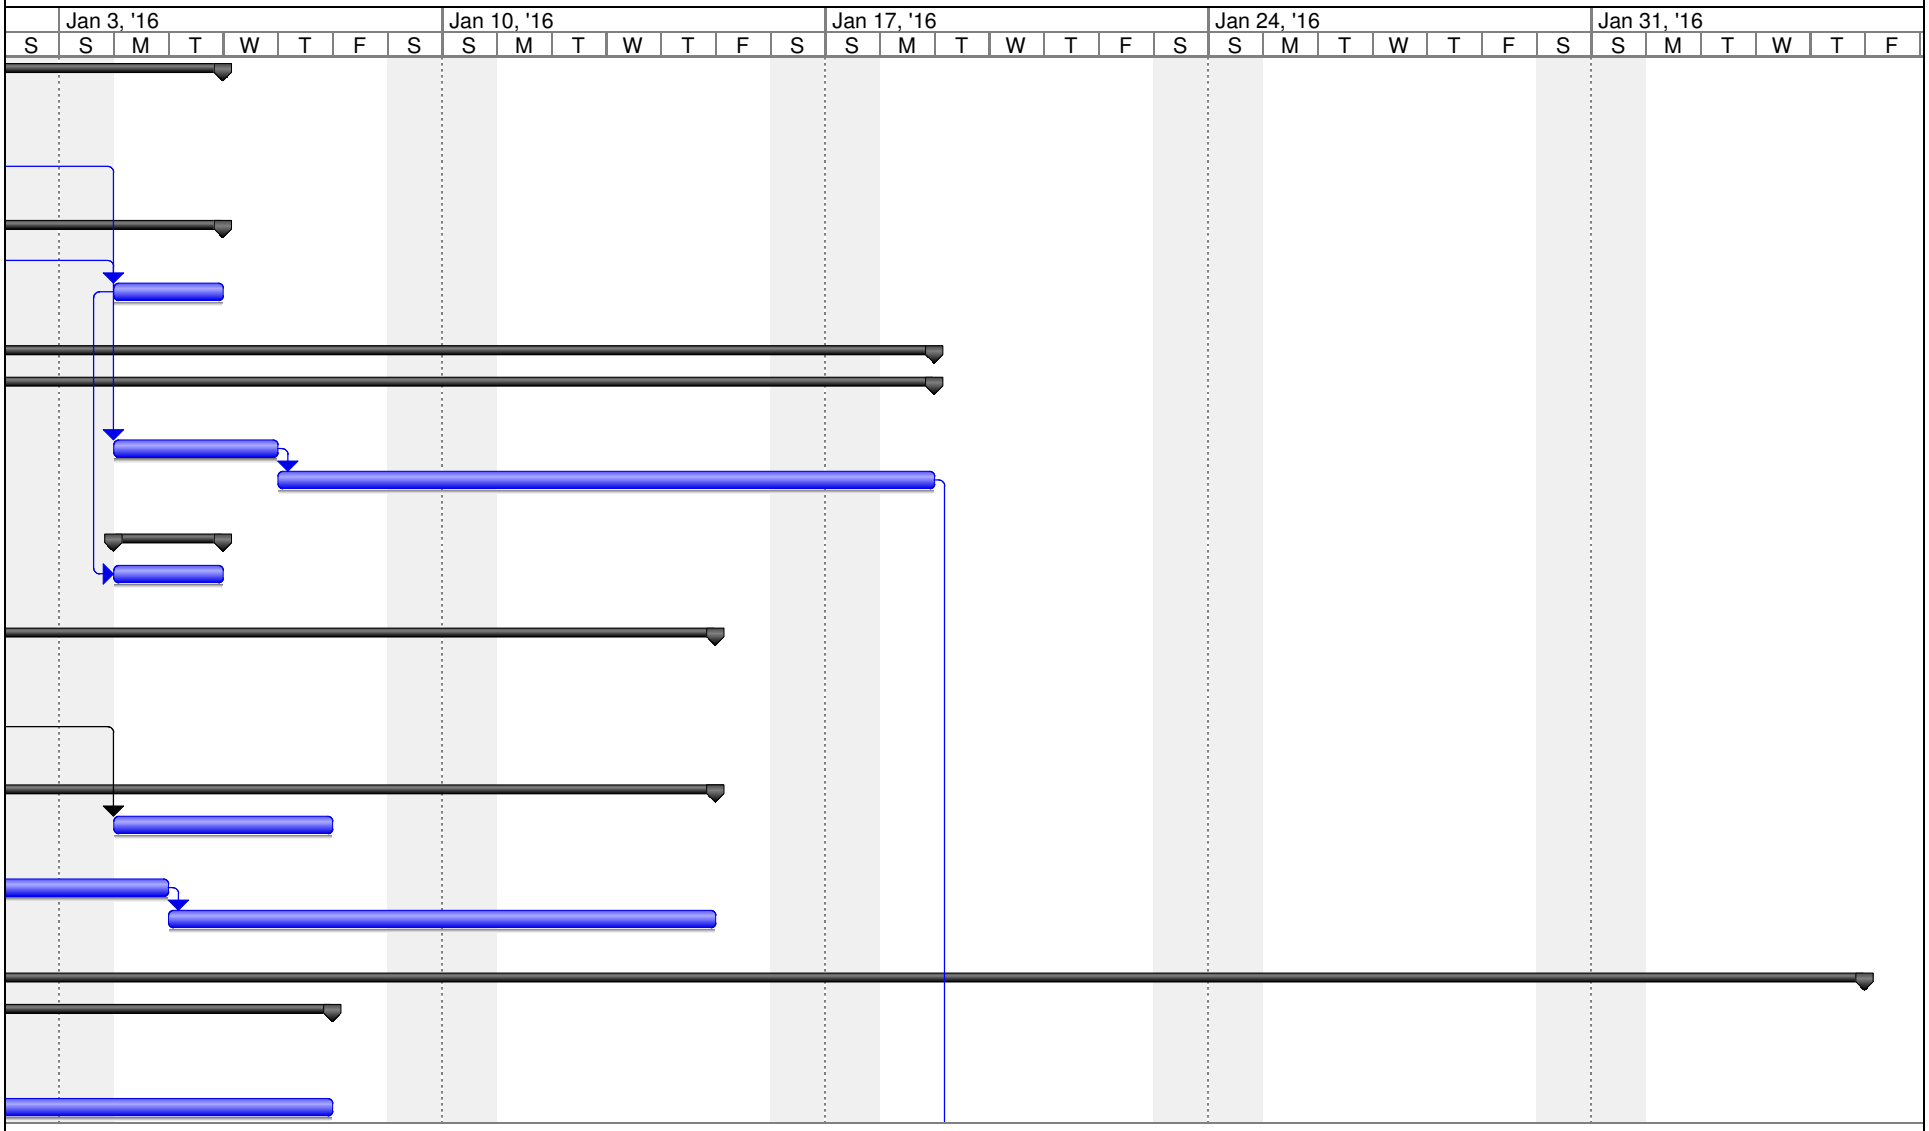

Project: 3wk 12-21-2015
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Hadley Mixed use
Legacy
3 wk Look ahead
12-21-2015

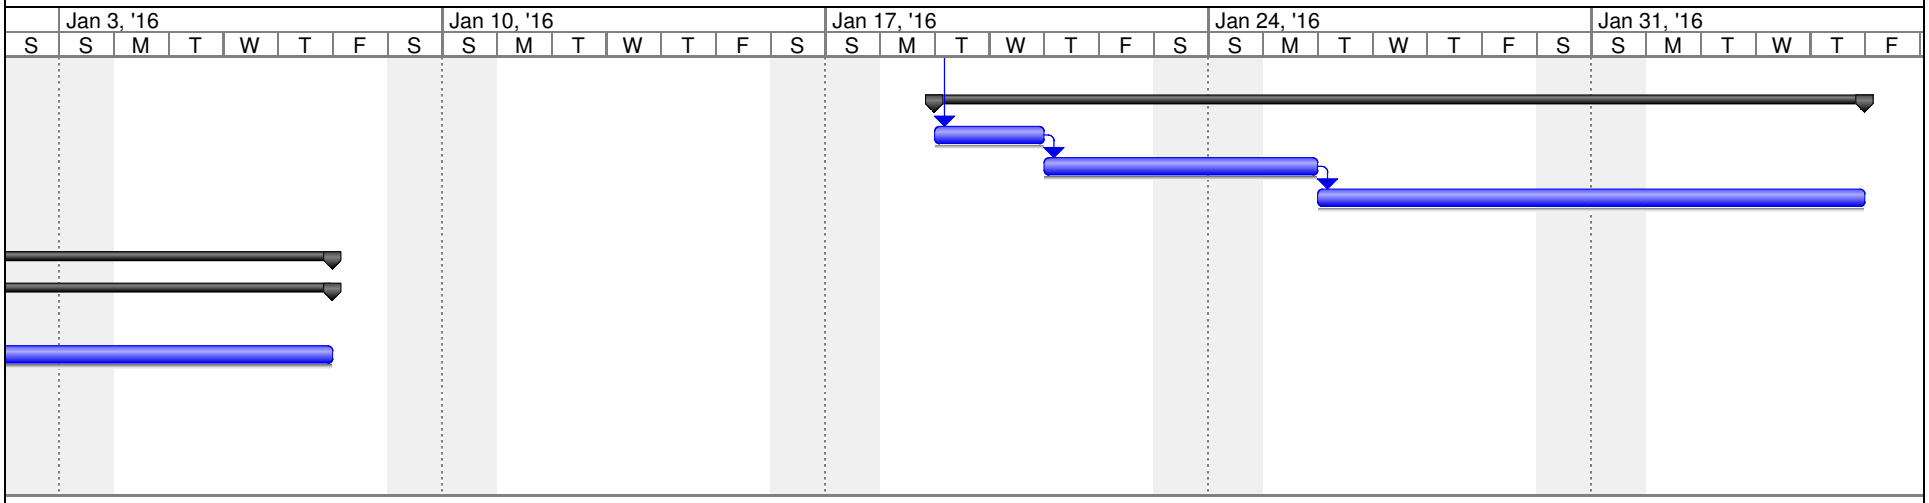

Project: 3wk 12-21-2015
Date: Mon 12/21/15

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
