Hadley 3 Week Schedule (Interior)
6-27-2016

ID	Task Name	Duration	Start	Finish
1	**MEP Roof Down**	**37 days**	**Thu 6/9/16**	**Fri 7/29/16**
2	**L5 Zone 1 (532-561)**	**32 days**	**Wed 6/15/16**	**Thu 7/28/16**
3	Paint doors and millwork	10 days	Wed 6/15/16	Tue 6/28/16
4	Plumbing Trim/QC	2 days	Wed 6/29/16	Thu 6/30/16
5	Electrical Trim/QC	2 days	Wed 6/29/16	Thu 6/30/16
6	Hardware Installation	3 days	Wed 6/29/16	Fri 7/1/16
7	Drywall Completion Repair	4 days	Wed 6/29/16	Mon 7/4/16
8	Appliance Major	4 days	Tue 7/5/16	Fri 7/8/16
9	Appliance Minor	2 days	Mon 7/11/16	Tue 7/12/16
10	Carpet Unit/Corridor	7 days	Fri 7/8/16	Mon 7/18/16
11	Final Paint	5 days	Tue 7/19/16	Mon 7/25/16
12	Unit Trim (shower door/Blinds/ Shelvi	3 days	Fri 7/22/16	Tue 7/26/16
13	Rough Clean	5 days	Fri 7/22/16	Thu 7/28/16
14				
15	**L4 Zone 1 (432-461)**	**24 days**	**Wed 6/22/16**	**Mon 7/25/16**
16	Paint doors and millwork	10 days	Wed 6/22/16	Tue 7/5/16
17	Plumbing Trim/QC	2 days	Wed 7/6/16	Thu 7/7/16
18	Electrical Trim/QC	2 days	Wed 7/6/16	Thu 7/7/16
19	Hardware Installation	3 days	Wed 7/6/16	Fri 7/8/16
20	Drywall Completion Repair	4 days	Wed 7/6/16	Mon 7/11/16
21	Appliance Major	4 days	Tue 7/12/16	Fri 7/15/16
22	Appliance Minor	2 days	Mon 7/18/16	Tue 7/19/16
23	Carpet Unit/Corridor	7 days	Fri 7/15/16	Mon 7/25/16
24				
25	**L6 Zone 1 (632-661)**	**14 days**	**Tue 7/5/16**	**Fri 7/22/16**
26	Paint doors and millwork	10 days	Tue 7/5/16	Mon 7/18/16
27	Plumbing Trim/QC	2 days	Tue 7/19/16	Wed 7/20/16
28	Electrical Trim/QC	2 days	Tue 7/19/16	Wed 7/20/16
29	Hardware Installation	3 days	Tue 7/19/16	Thu 7/21/16
30	Drywall Completion Repair	4 days	Tue 7/19/16	Fri 7/22/16
31				
32	**L3 Zone 1 (332-360)**	**21 days**	**Thu 6/30/16**	**Thu 7/28/16**

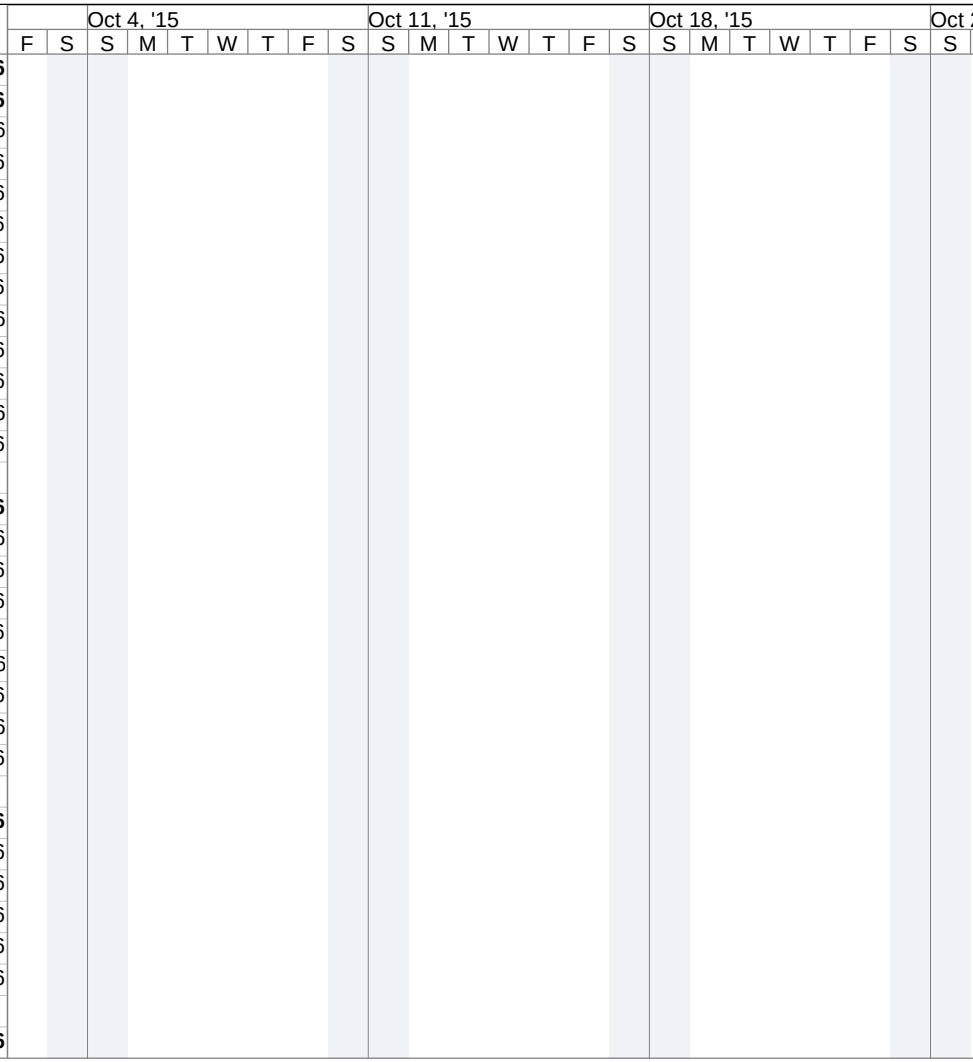

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Progress
External Tasks	Duration-only	Deadline

Hadley 3 Week Schedule (Interior)
6-27-2016

ID	Task Name	Duration	Start	Finish
33	Drywall Repair ADA	5 days	Thu 6/30/16	Wed 7/6/16
34	Doors and Millwork	5 days	Thu 7/7/16	Wed 7/13/16
35	Paint doors and millwork	10 days	Fri 7/15/16	Thu 7/28/16
36				
37	**L5 Zone 2 (501-531)**	**37 days**	**Thu 6/9/16**	**Fri 7/29/16**
38	Install cabinets	10 days	Thu 6/9/16	Wed 6/22/16
39	Install Flooring	10 days	Thu 6/16/16	Wed 6/29/16
40	Install counter tops	6 days	Mon 6/27/16	Mon 7/4/16
41	Intsall Backsplash	6 days	Wed 6/29/16	Wed 7/6/16
42	Doors and Millwork	8 days	Mon 7/4/16	Wed 7/13/16
43	Paint doors and millwork	12 days	Thu 7/14/16	Fri 7/29/16
44				
45	**L4 Zone 2 (401-431)**	**27 days**	**Wed 6/22/16**	**Thu 7/28/16**
46	Gypcrete dry time	10 days	Wed 6/22/16	Tue 7/5/16
47	Electrical trim	5 days	Wed 6/29/16	Tue 7/5/16
48	Fire/Sprinkler Trim	3 days	Wed 6/29/16	Fri 7/1/16
49	Install cabinets	6 days	Fri 7/1/16	Fri 7/8/16
50	Install Flooring	7 days	Wed 7/6/16	Thu 7/14/16
51	Install counter tops	6 days	Tue 7/12/16	Tue 7/19/16
52	Intsall Backsplash	6 days	Thu 7/14/16	Thu 7/21/16
53	Doors and Millwork	8 days	Tue 7/19/16	Thu 7/28/16
54				
55	**L6 Zone 2 (601-631)**	**25 days**	**Mon 6/27/16**	**Fri 7/29/16**
56	Hang and tape soffits/Texture/PVA	5 days	Mon 6/27/16	Fri 7/1/16
57	Paint	4 days	Mon 7/4/16	Thu 7/7/16
58	Gypcrete	3 days	Fri 7/8/16	Tue 7/12/16
59	Gypcrete dry time	10 days	Wed 7/13/16	Tue 7/26/16
60	Electrical trim	5 days	Wed 7/20/16	Tue 7/26/16
61	Fire/Sprinkler Trim	3 days	Wed 7/20/16	Fri 7/22/16
62	Install cabinets	6 days	Fri 7/22/16	Fri 7/29/16
63				
64				

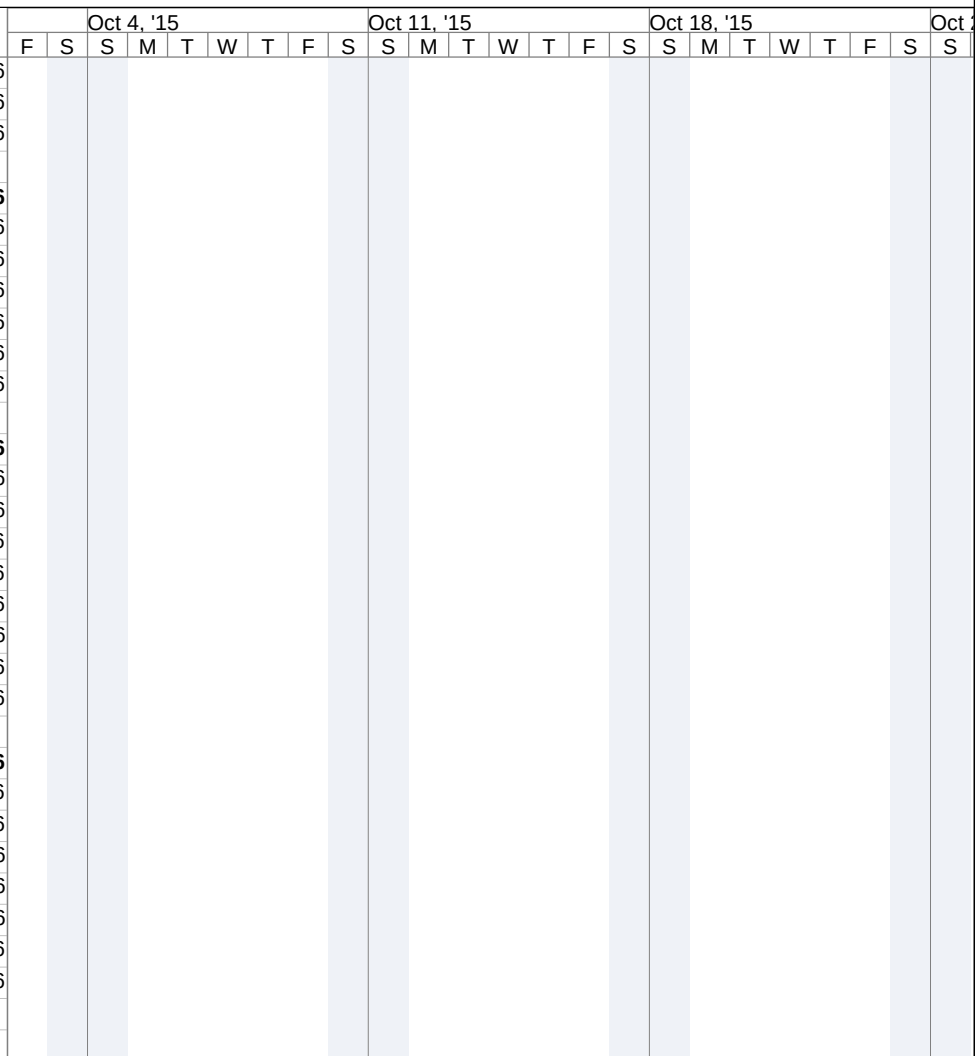

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

ID	Task Name	Duration	Start	Finish
65	**L3 Zone 2 (301-331)**	**22 days**	**Mon 6/27/16**	**Tue 7/26/16**
66	Frame soffits	5 days	Mon 6/27/16	Fri 7/1/16
67	Electrical at soffits	2 days	Mon 7/4/16	Tue 7/5/16
68	Vent soffits	5 days	Wed 7/6/16	Tue 7/12/16
69	Firecaulk soffits	2 days	Wed 7/13/16	Thu 7/14/16
70	HVAC/ Electrical inspection at soffits	1 day	Fri 7/15/16	Fri 7/15/16
71	Hang and tape soffits/Texture/PVA	7 days	Mon 7/18/16	Tue 7/26/16
72				
73	**L2 Zone 2 (201-208)**	**20 days**	**Mon 6/27/16**	**Fri 7/22/16**
74	Install tubs	1 day	Mon 6/27/16	Mon 6/27/16
75	elec rough in	1 day	Tue 6/28/16	Tue 6/28/16
76	Elec, Plmb Inspections	1 day	Tue 6/28/16	Tue 6/28/16
77	Fire Caulk	2 days	Tue 6/28/16	Wed 6/29/16
78	Framing inspection	1 day	Thu 6/30/16	Thu 6/30/16
79	Insulation	2 days	Fri 7/1/16	Mon 7/4/16
80	Insulation Inspection	1 day	Tue 7/5/16	Tue 7/5/16
81	Drywall Hang/Tape	5 days	Wed 7/6/16	Tue 7/12/16
82	Frame Soffits	2 days	Wed 7/13/16	Thu 7/14/16
83	Electrical at soffits	1 day	Fri 7/15/16	Fri 7/15/16
84	Vent soffits	3 days	Mon 7/18/16	Wed 7/20/16
85	Firecaulk soffits	1 day	Thu 7/21/16	Thu 7/21/16
86	HVAC/ Electrical inspection at soffits	1 day	Fri 7/22/16	Fri 7/22/16

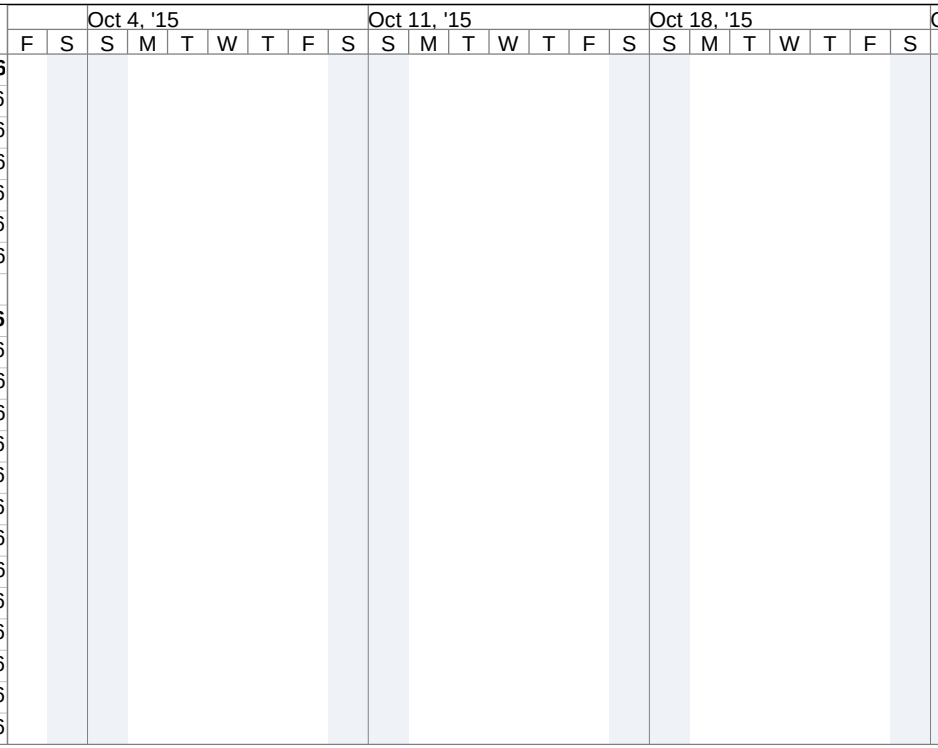

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Progress
External Tasks	Duration-only	Deadline

Hadley 3 Week Schedule (Interior)
6-27-2016

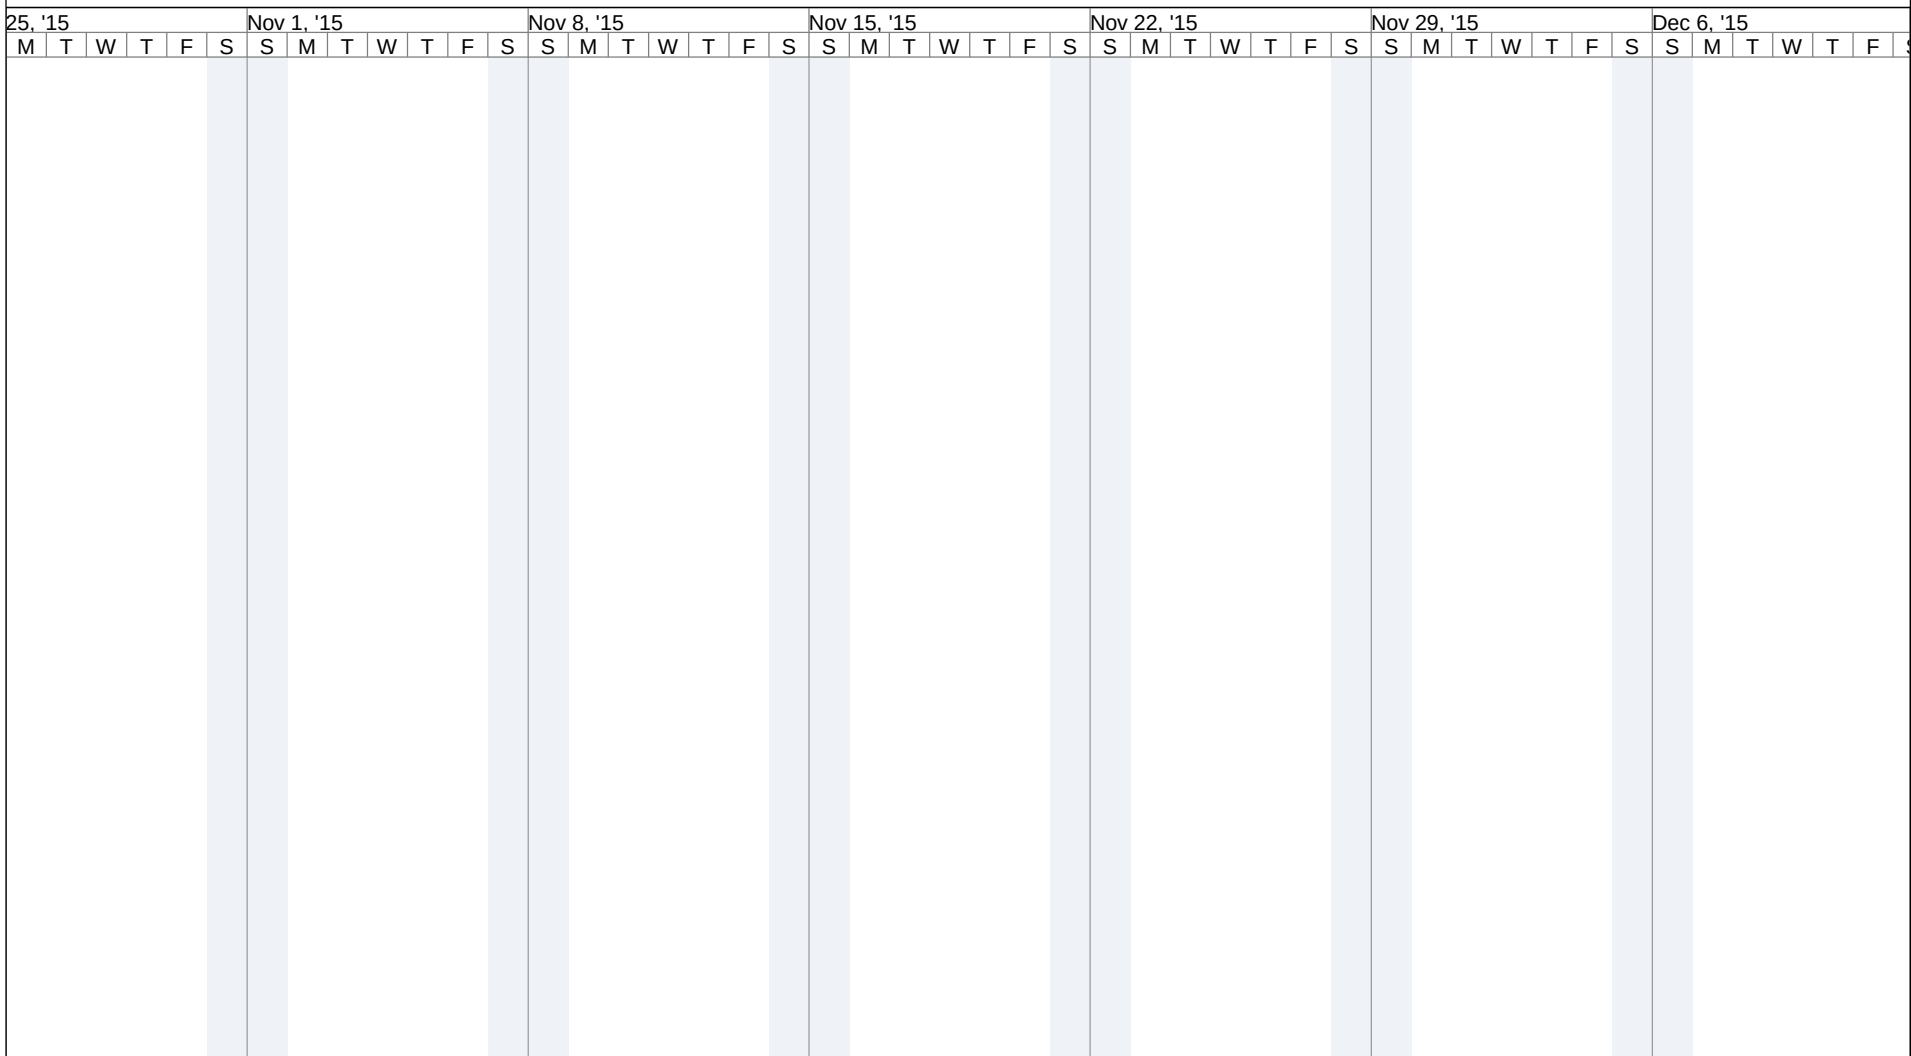

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

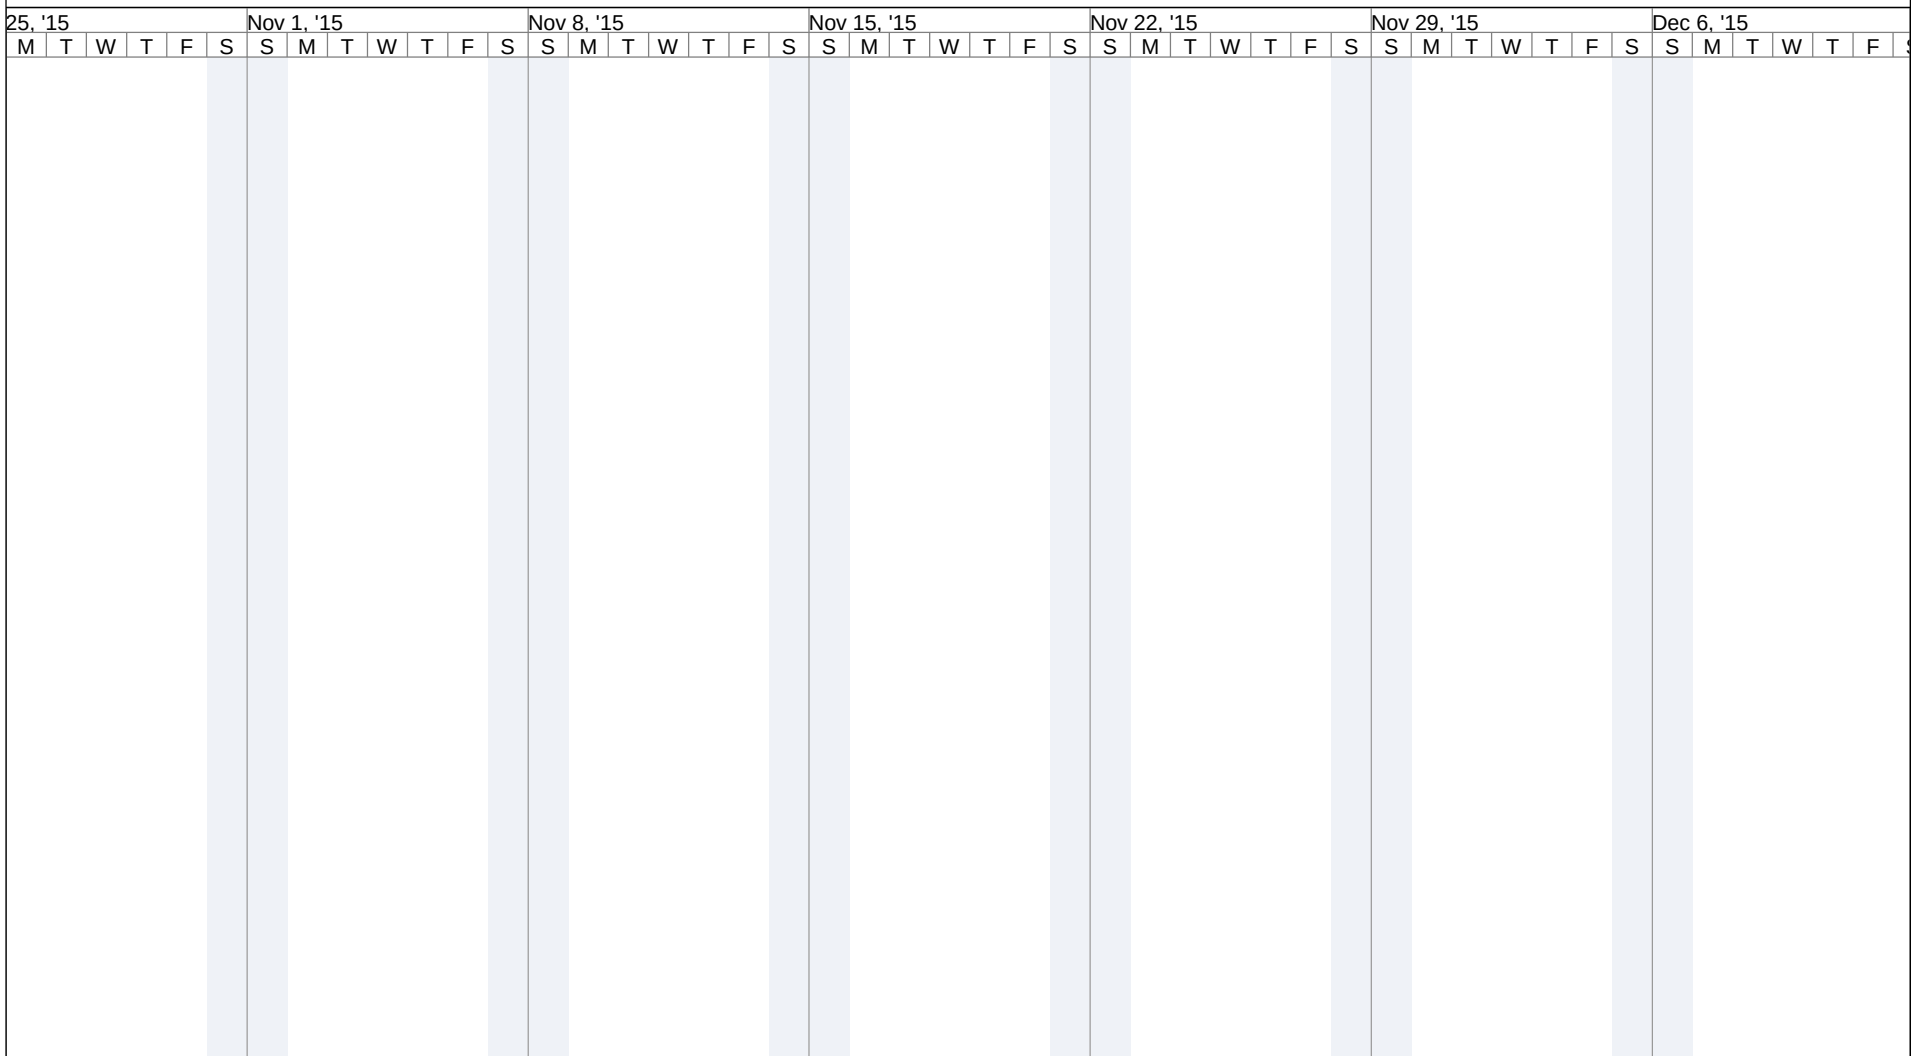

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

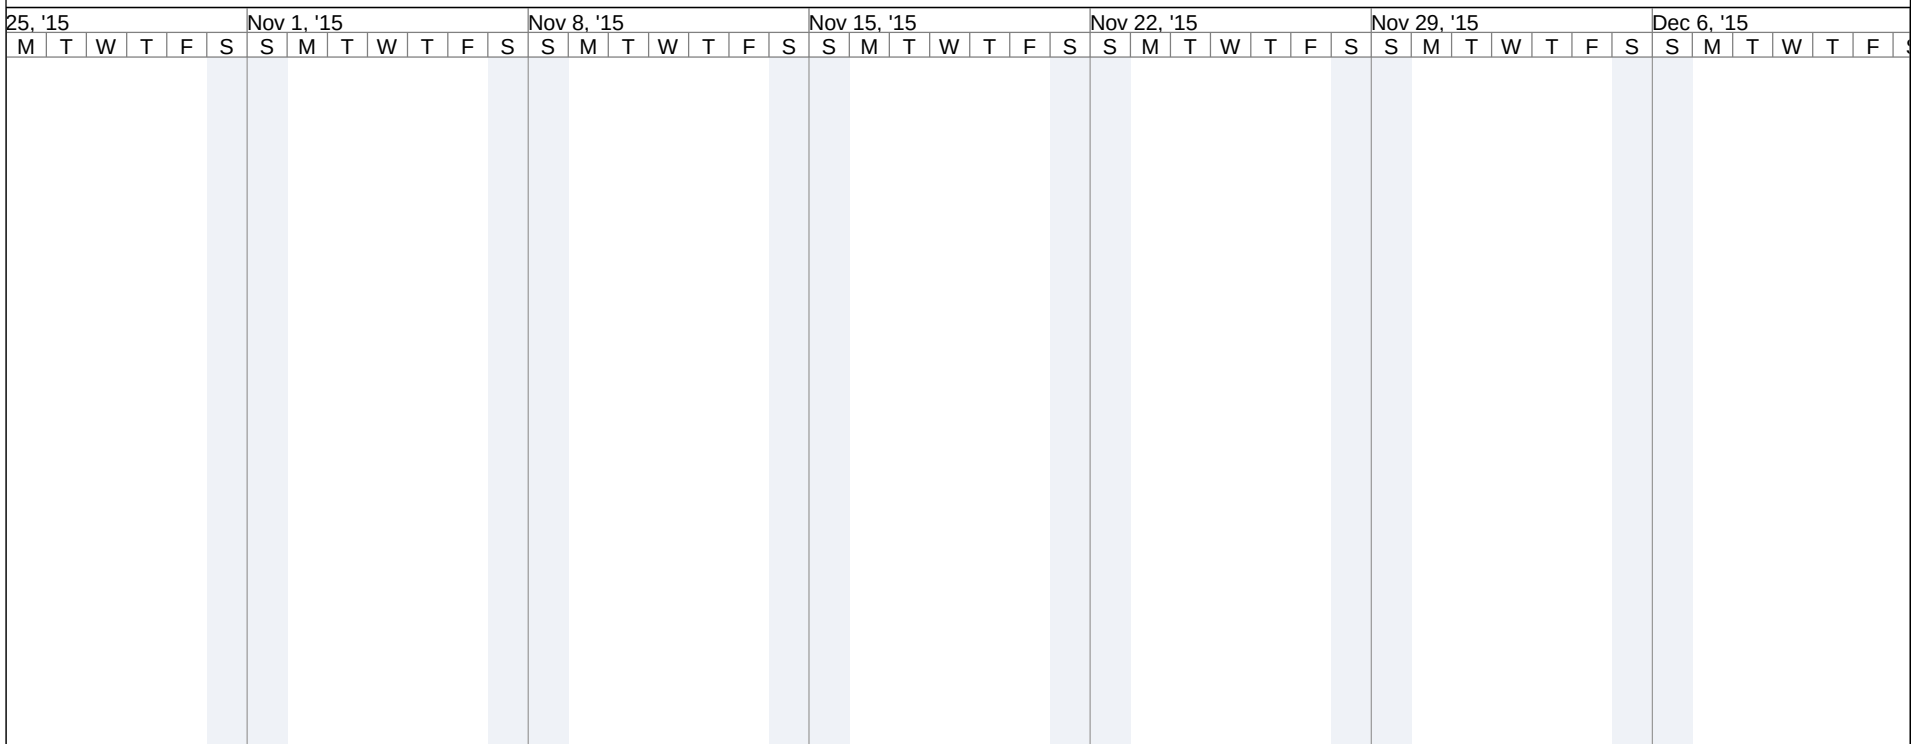

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

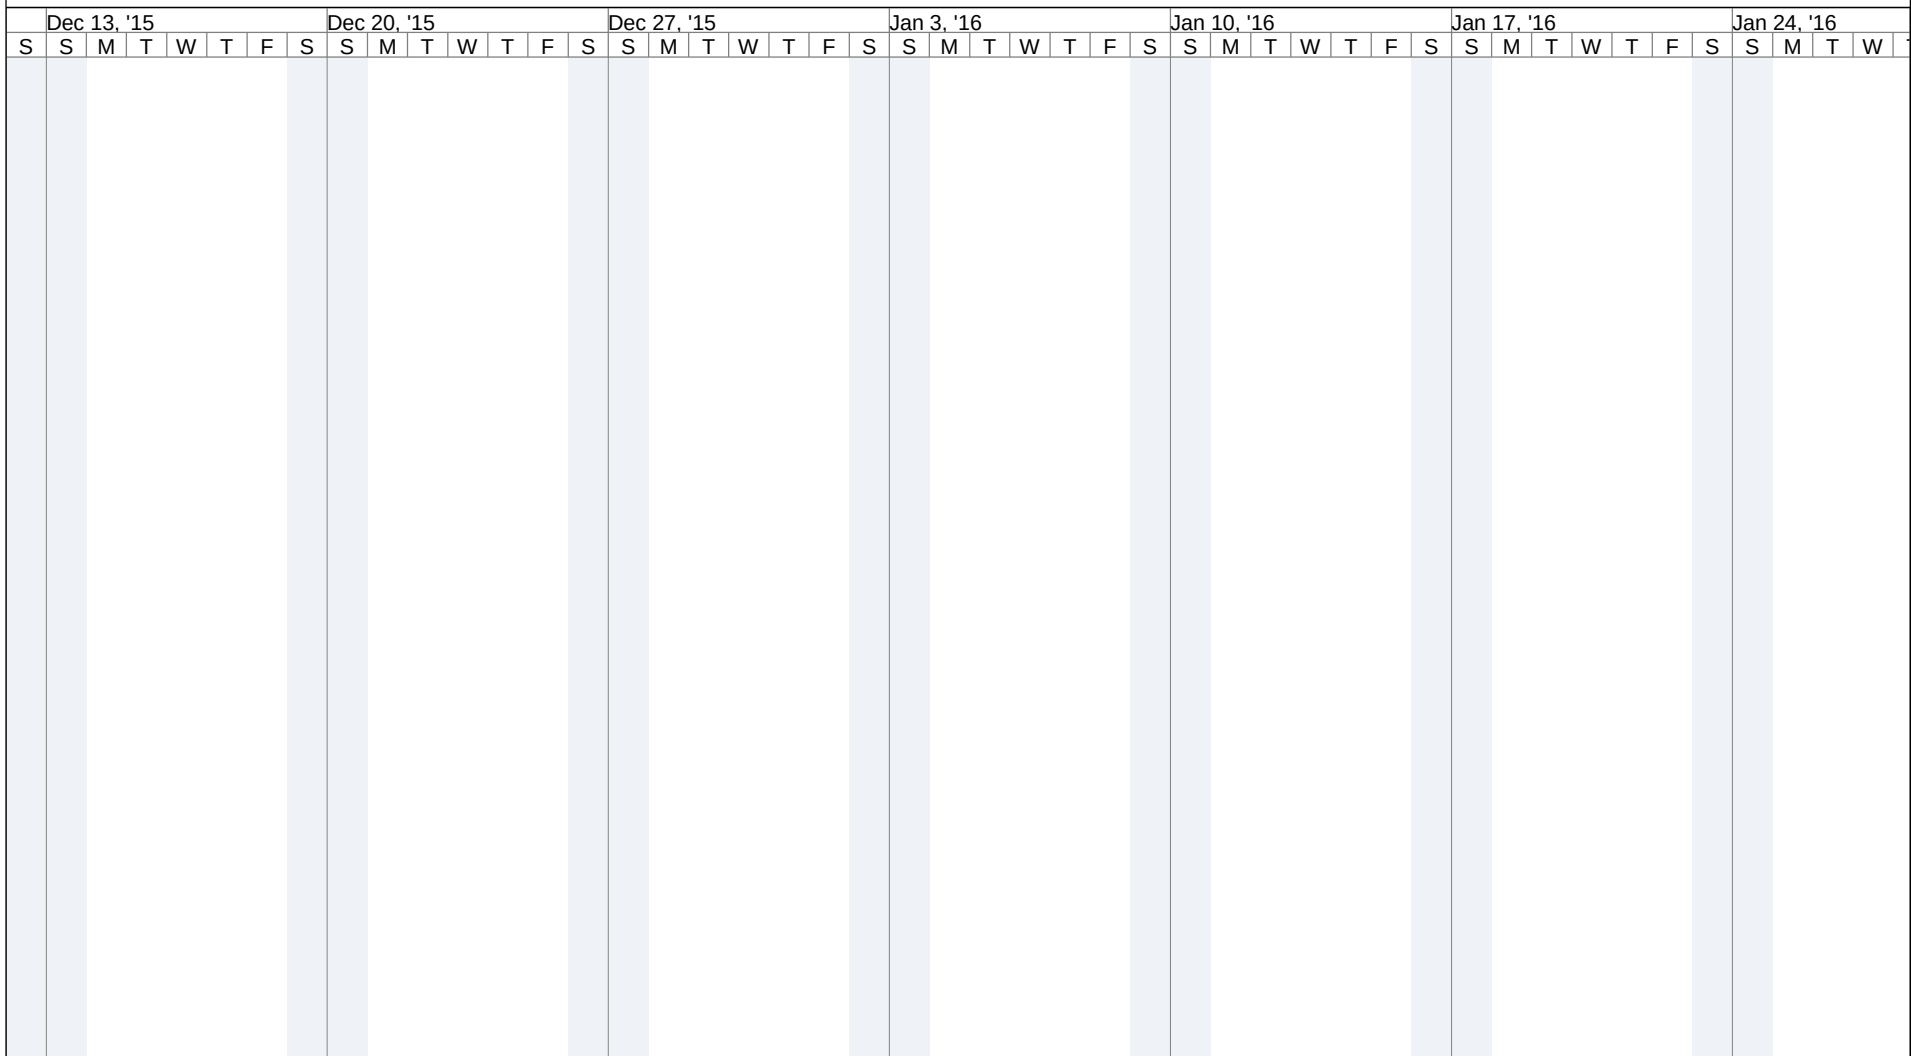

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

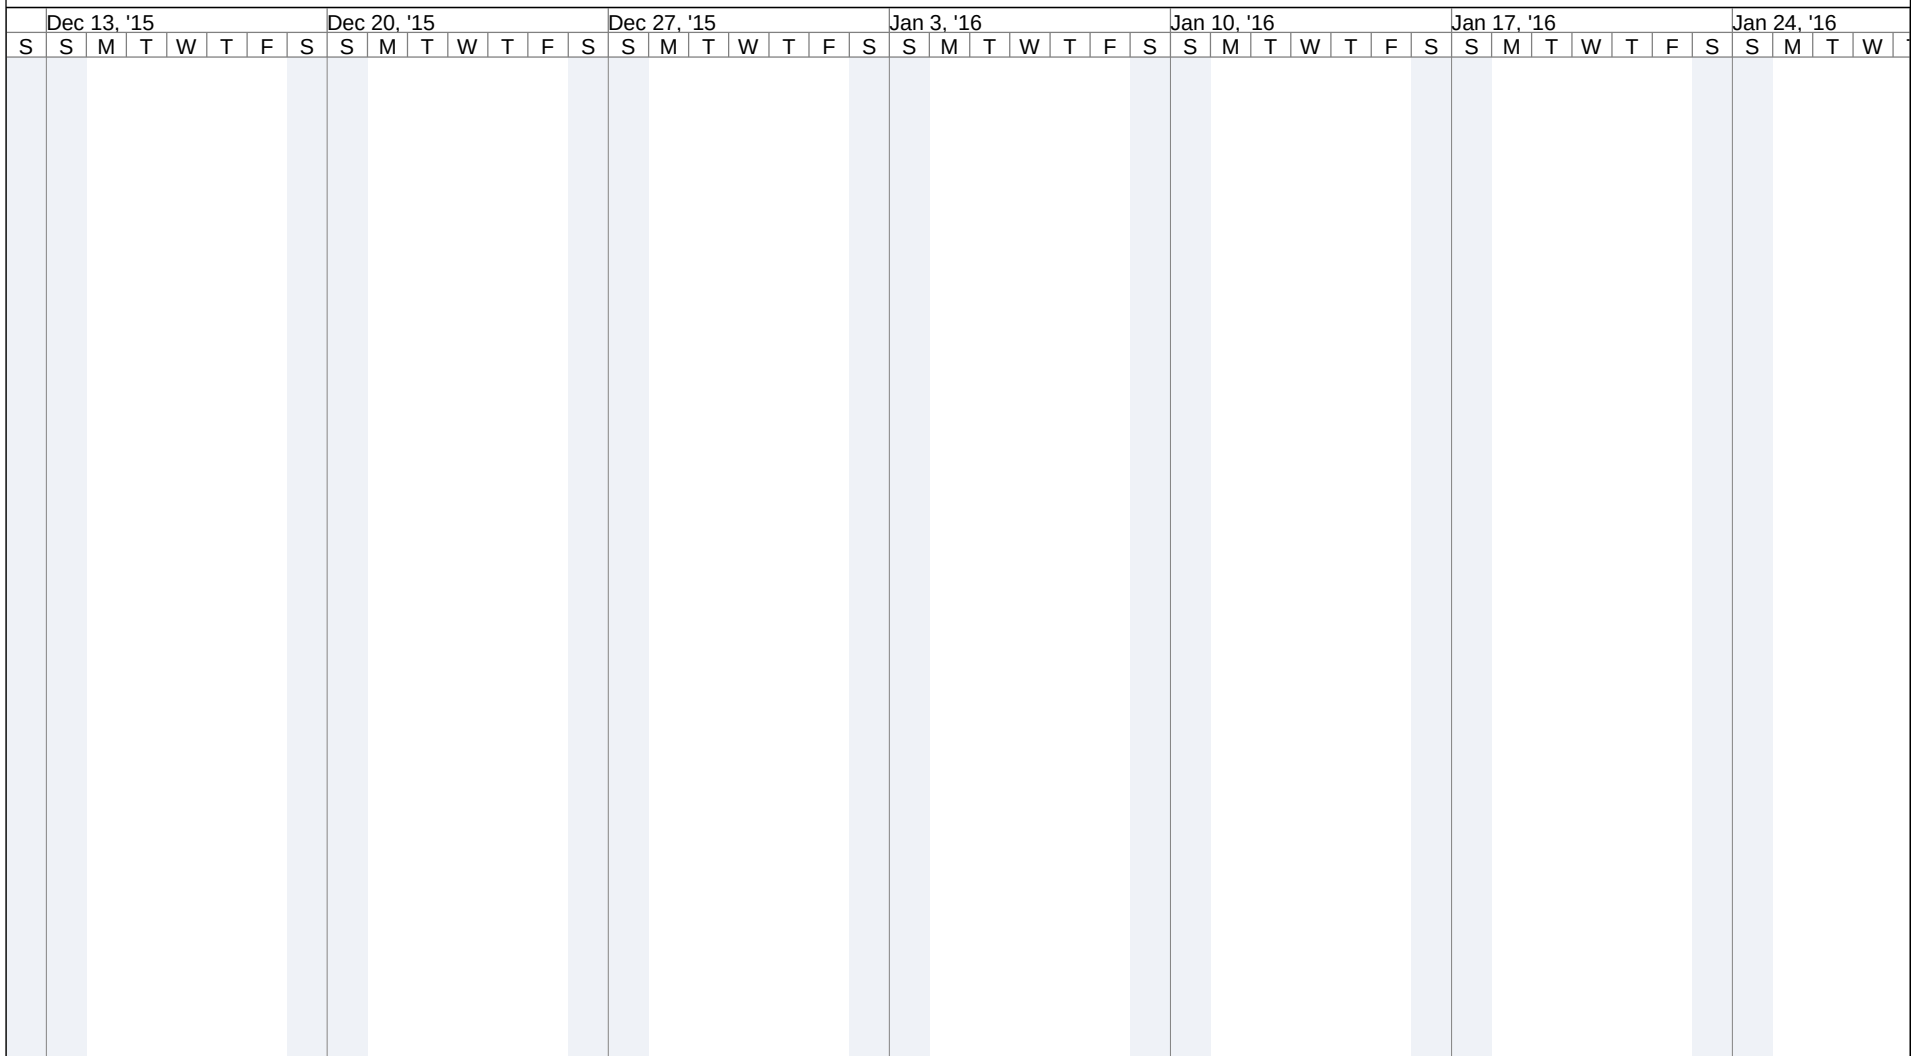

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

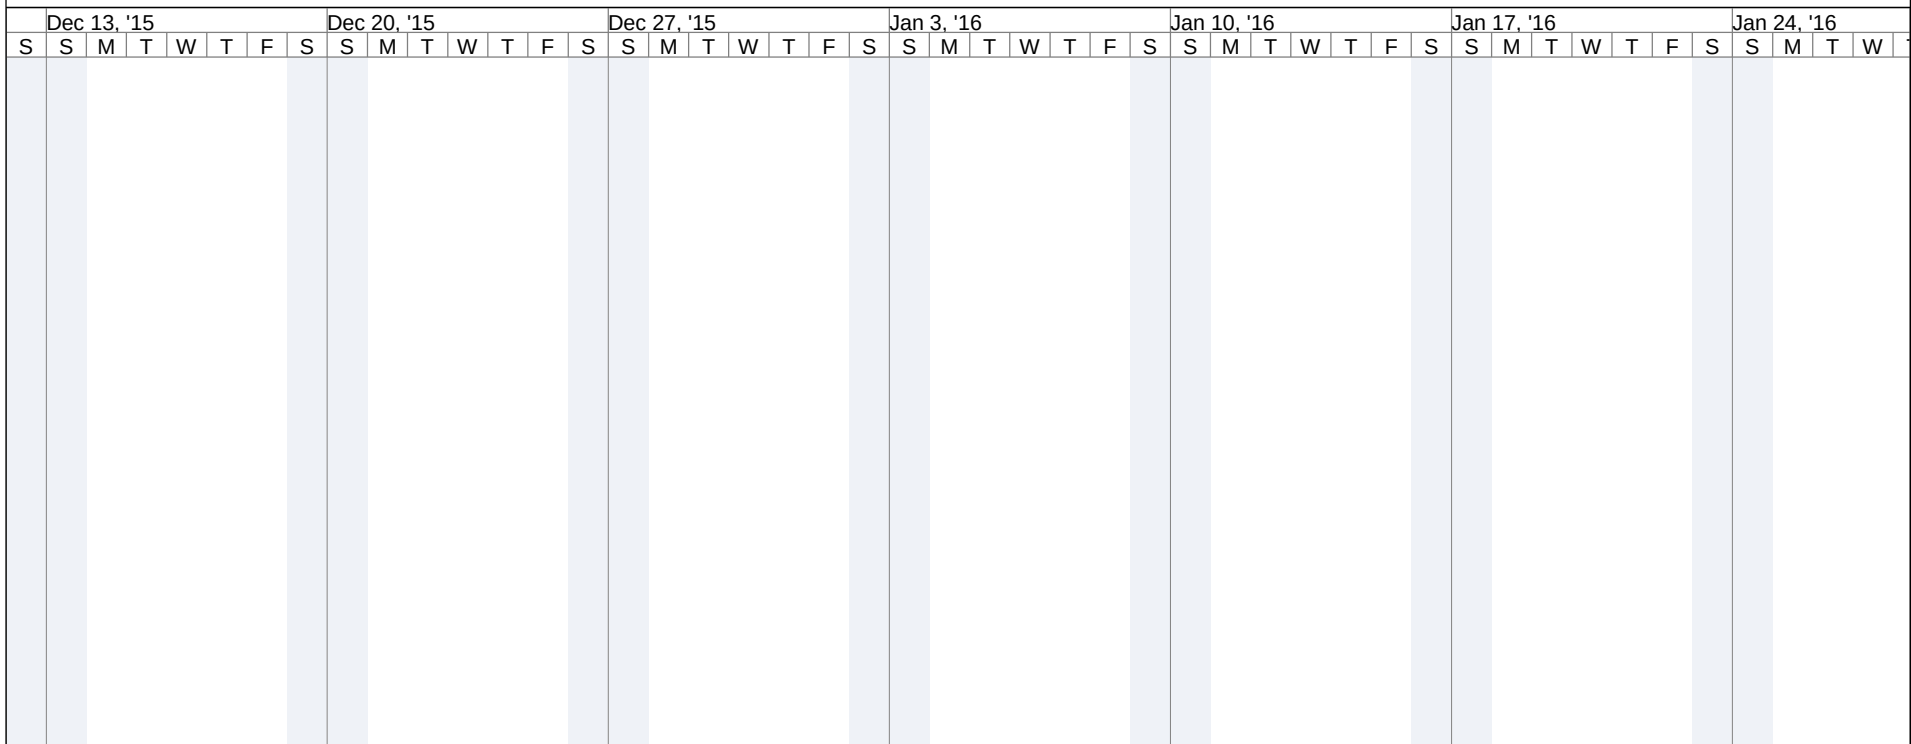

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

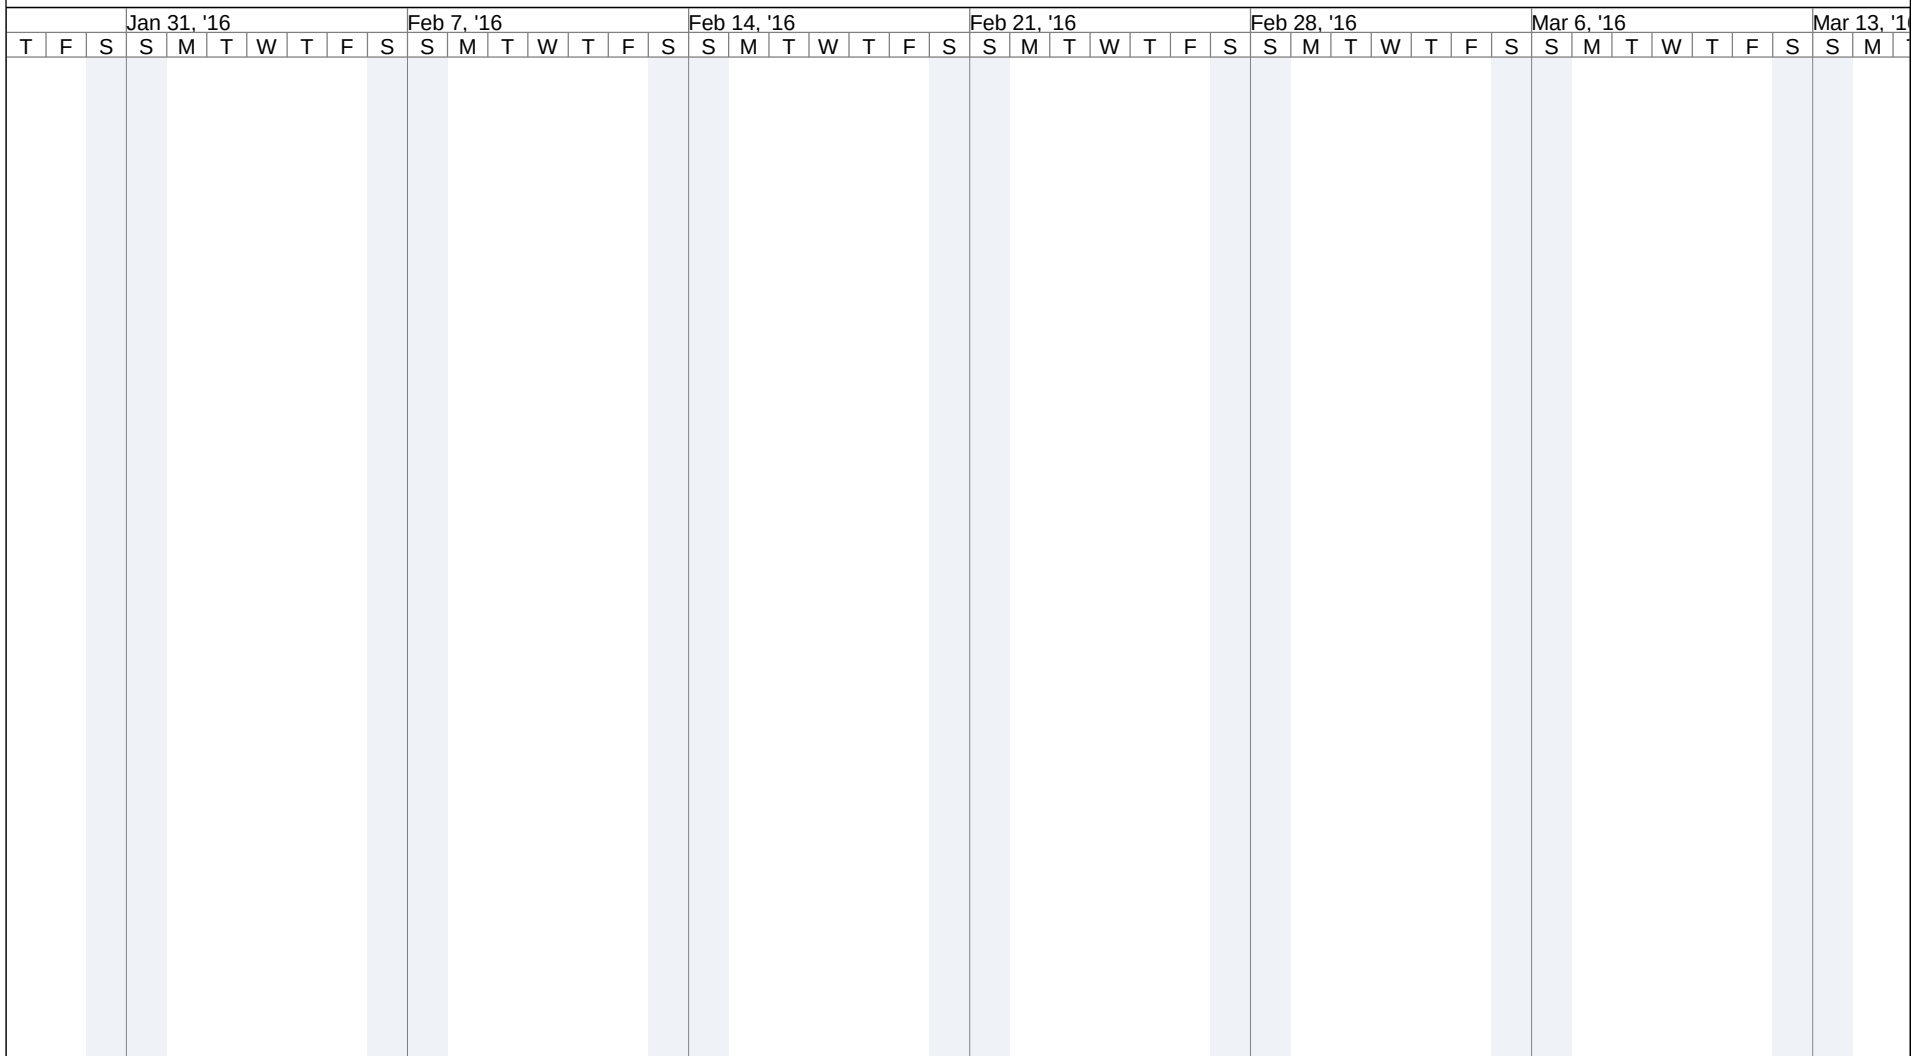

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

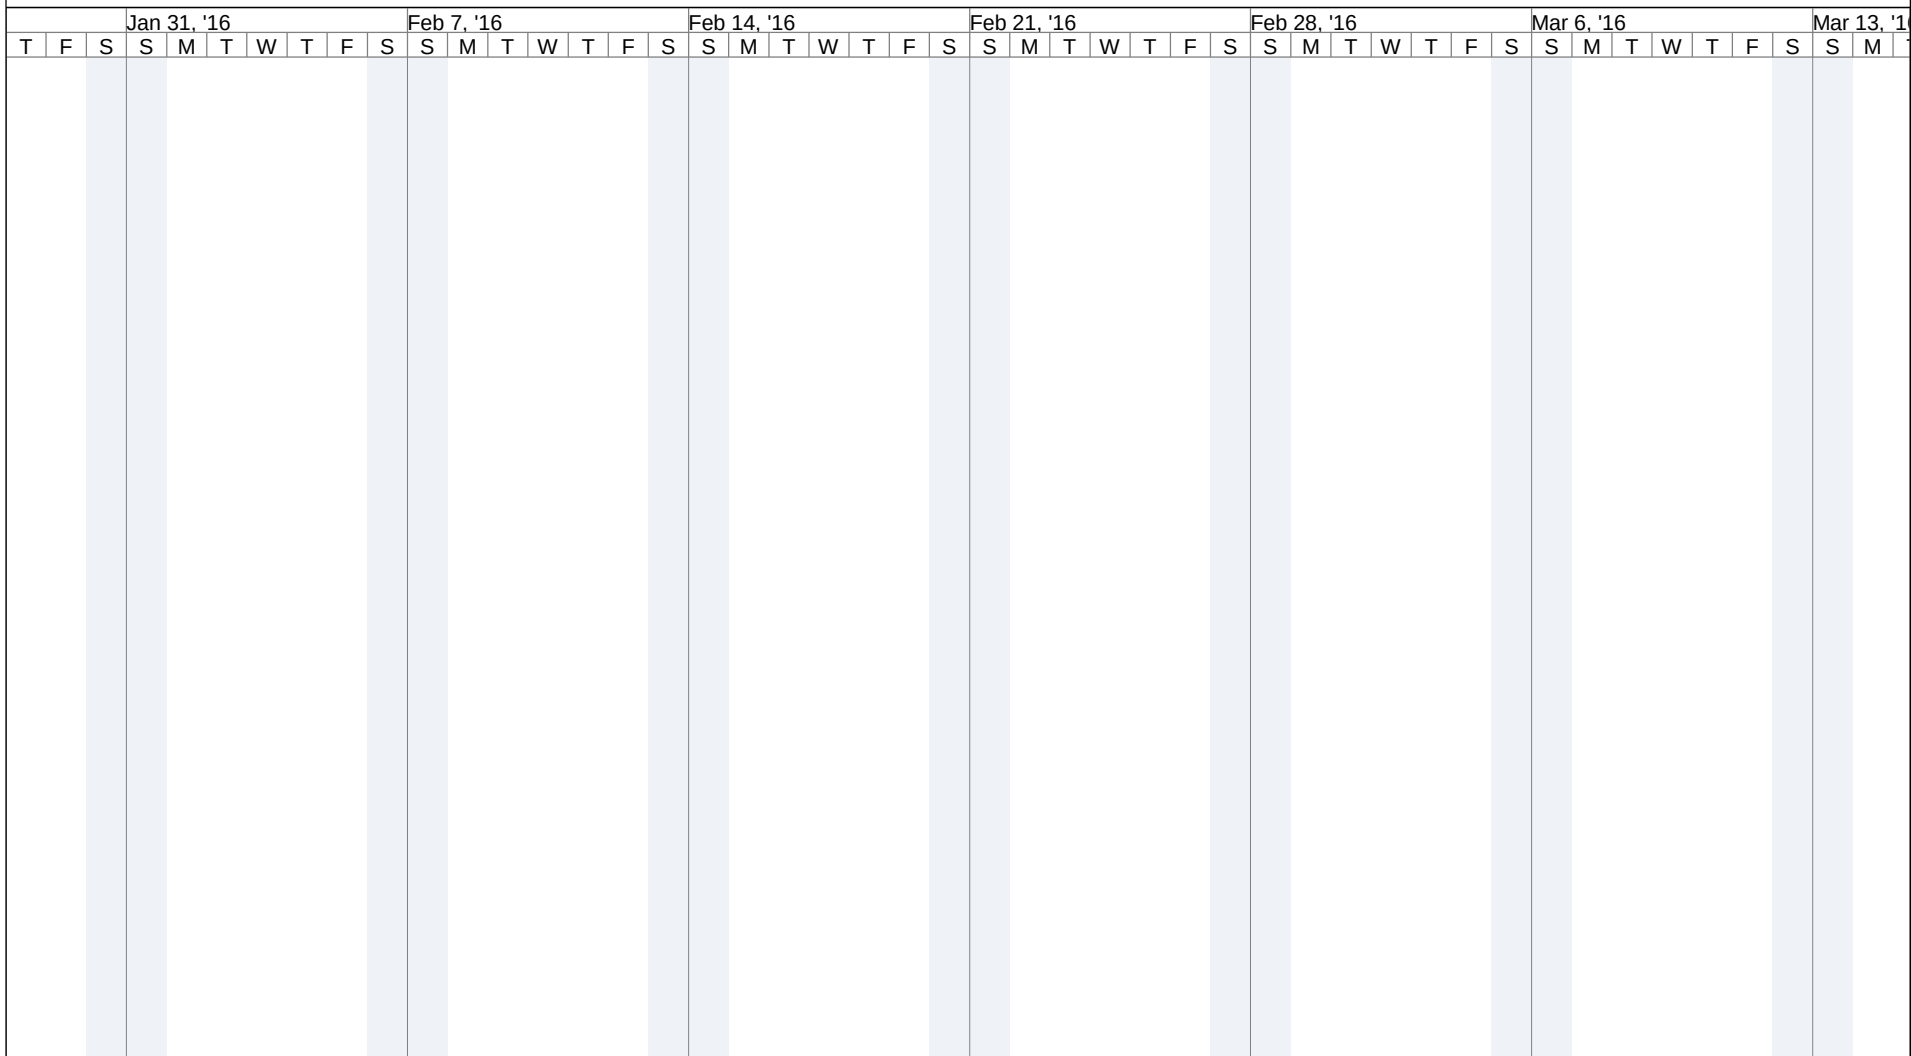

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

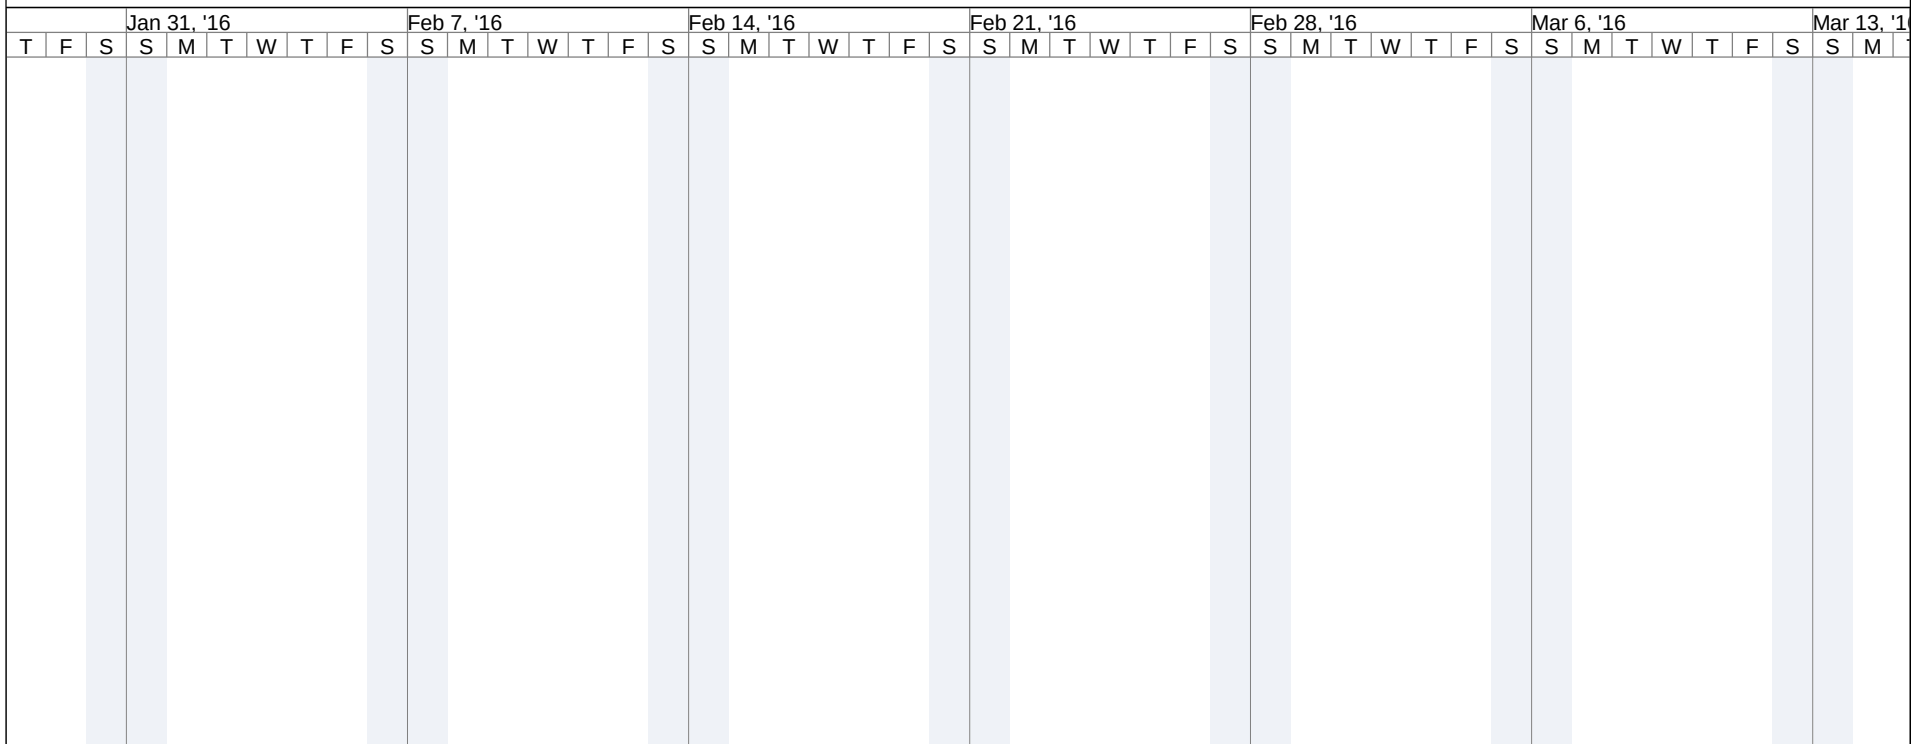

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

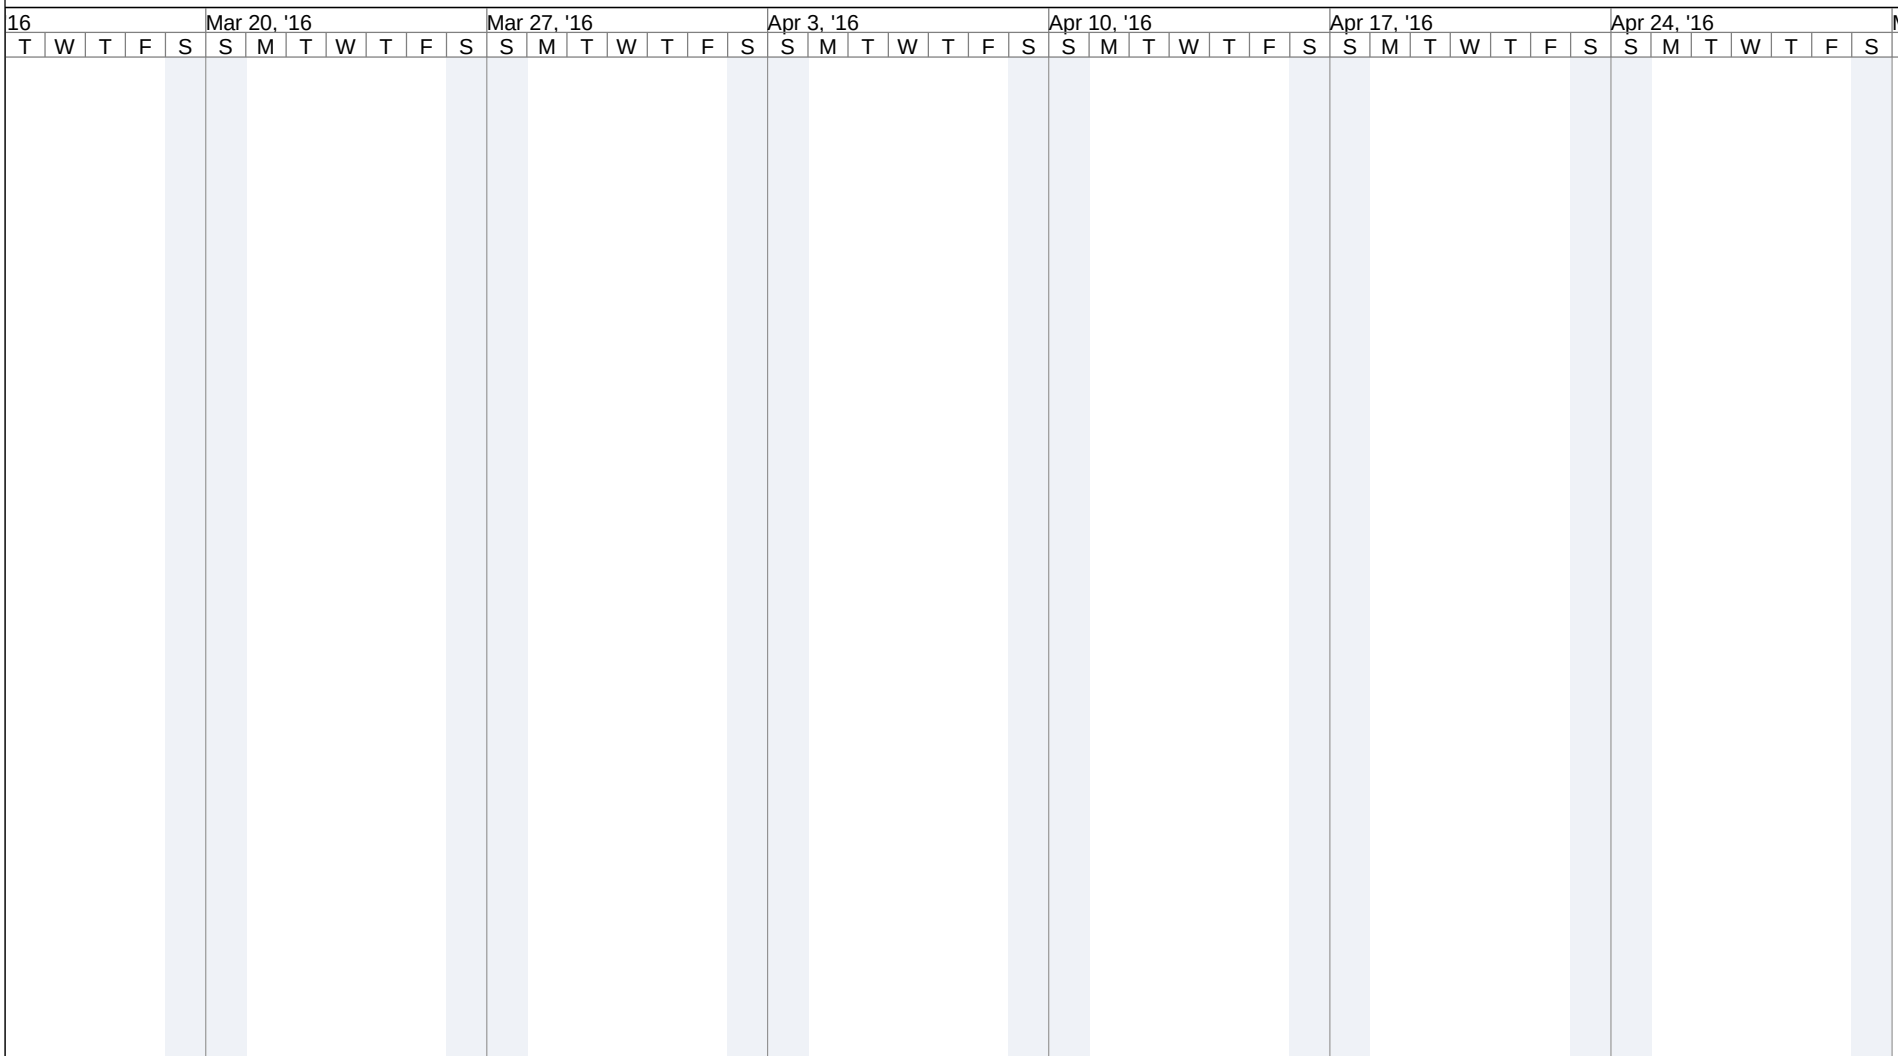

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

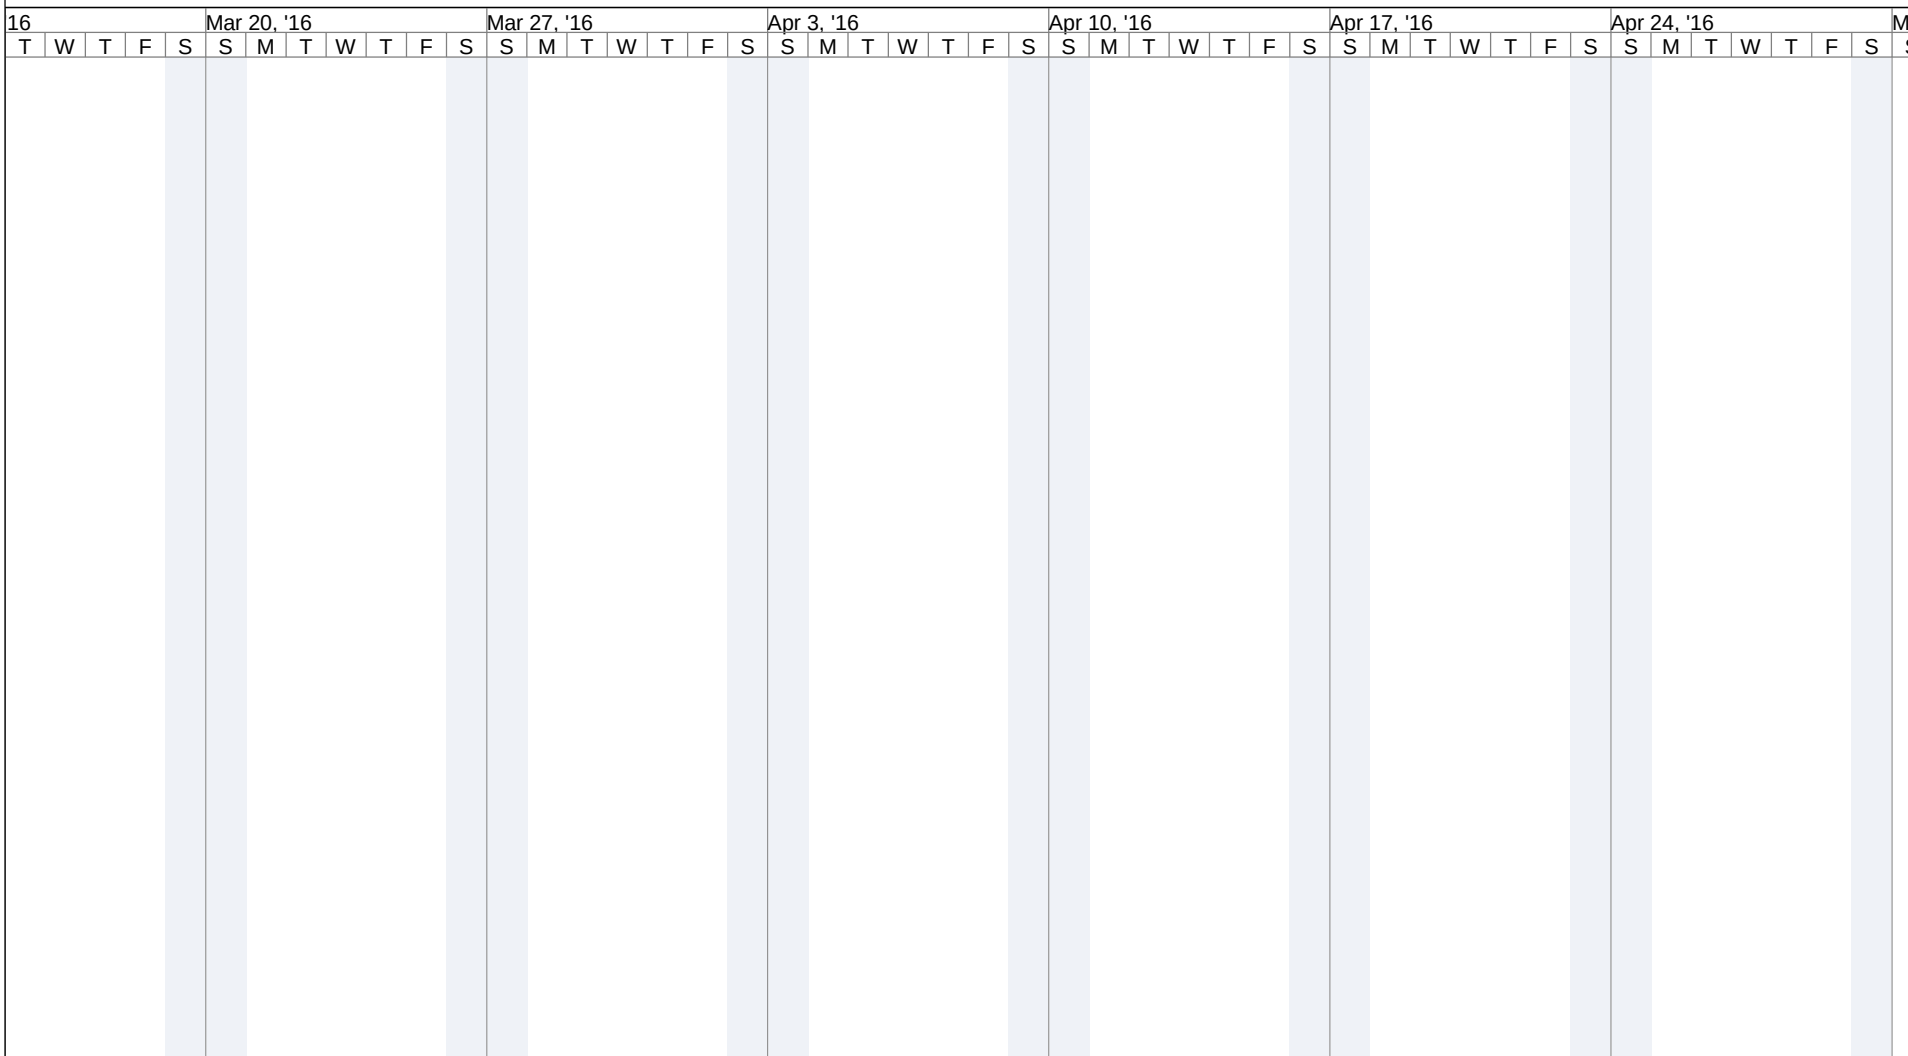

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

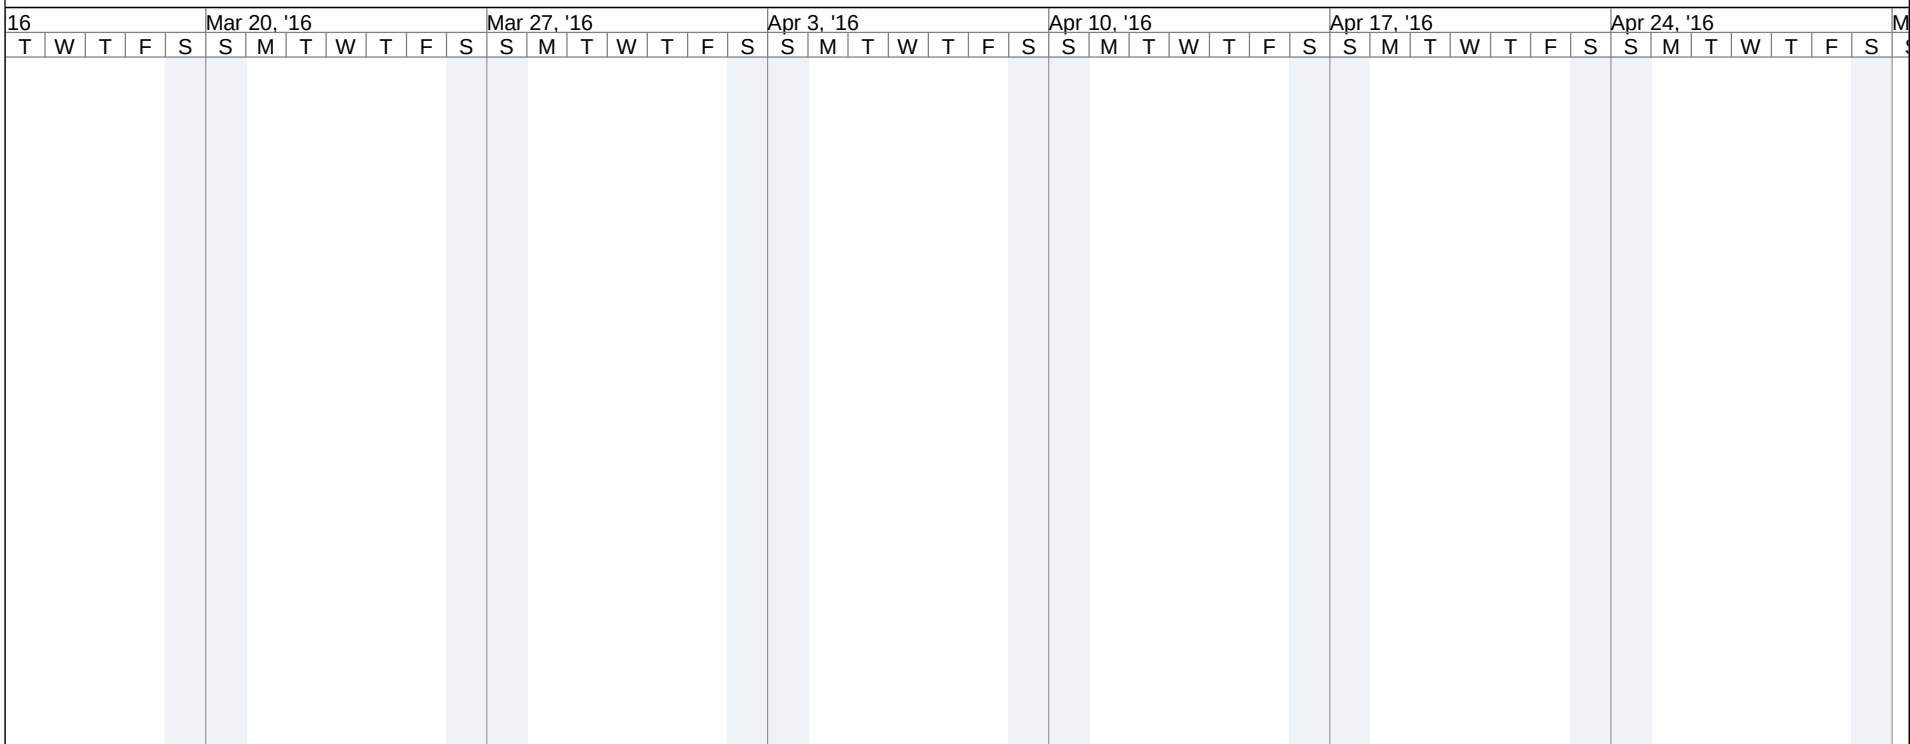

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

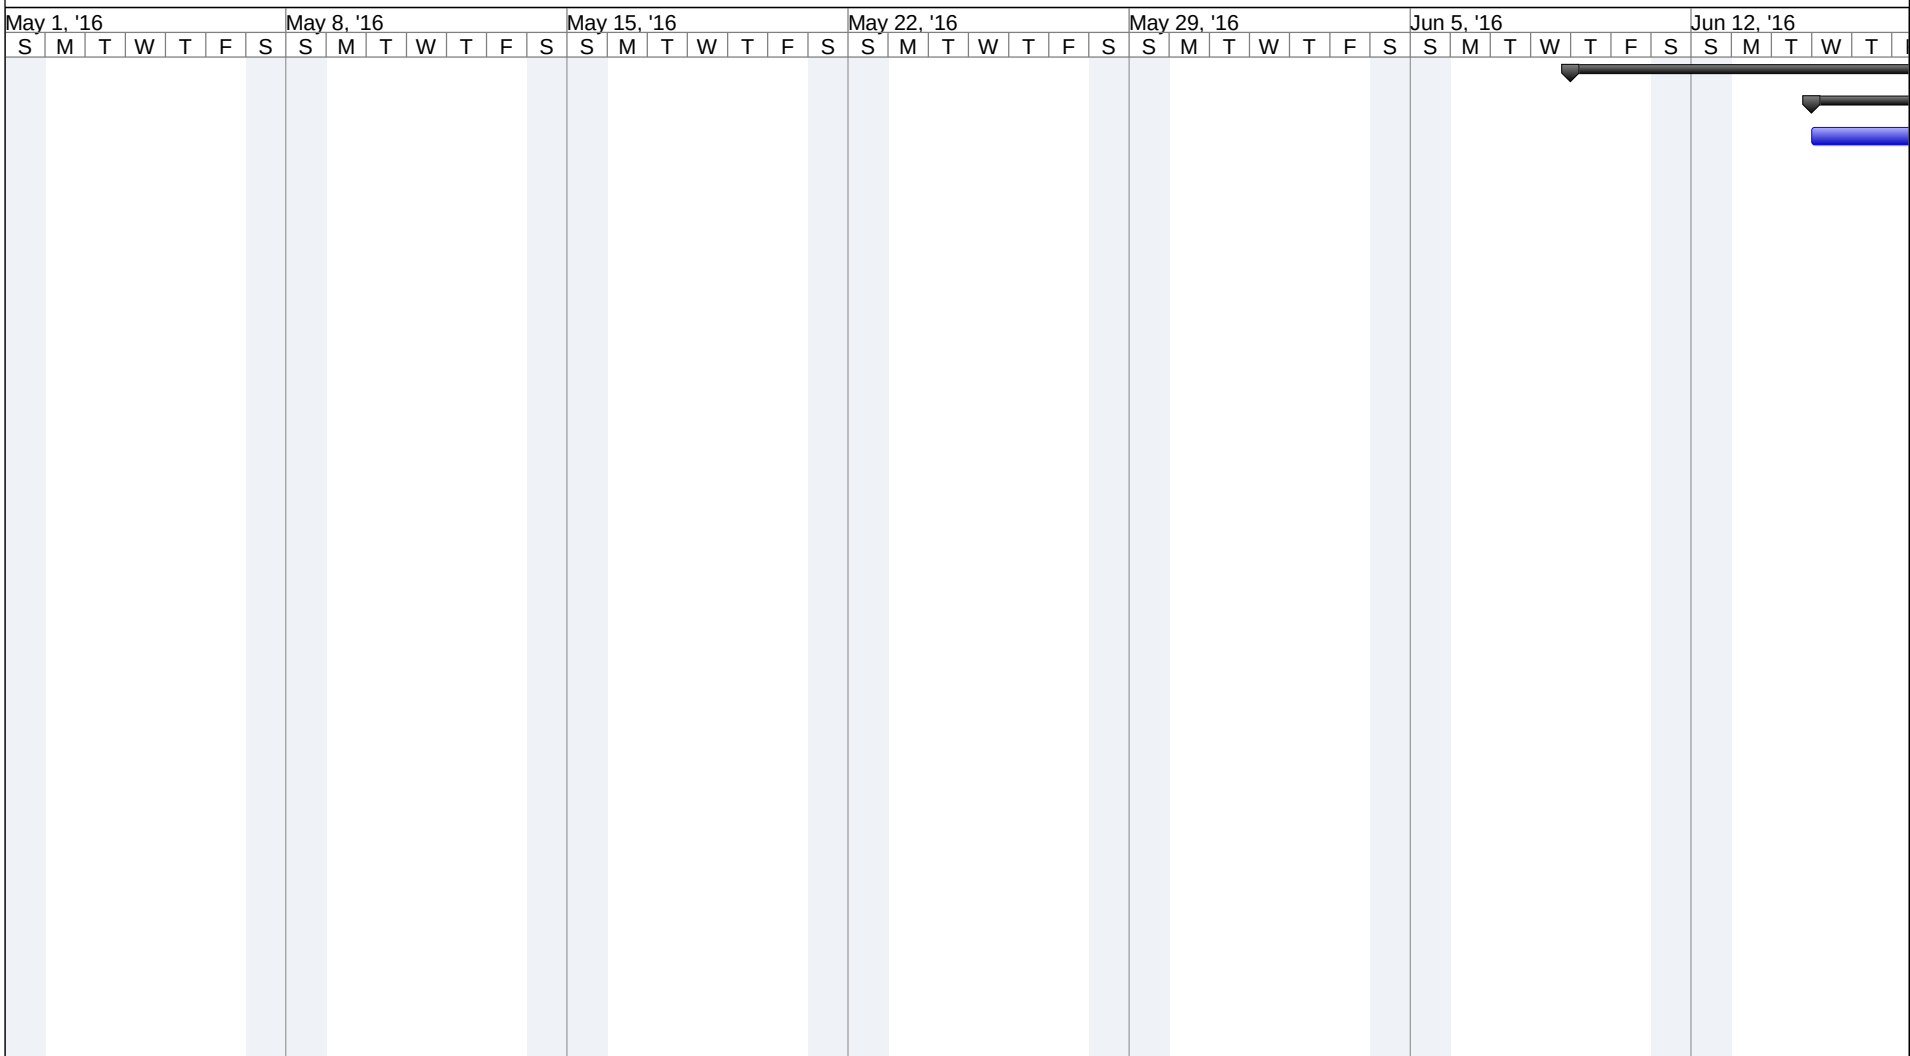

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

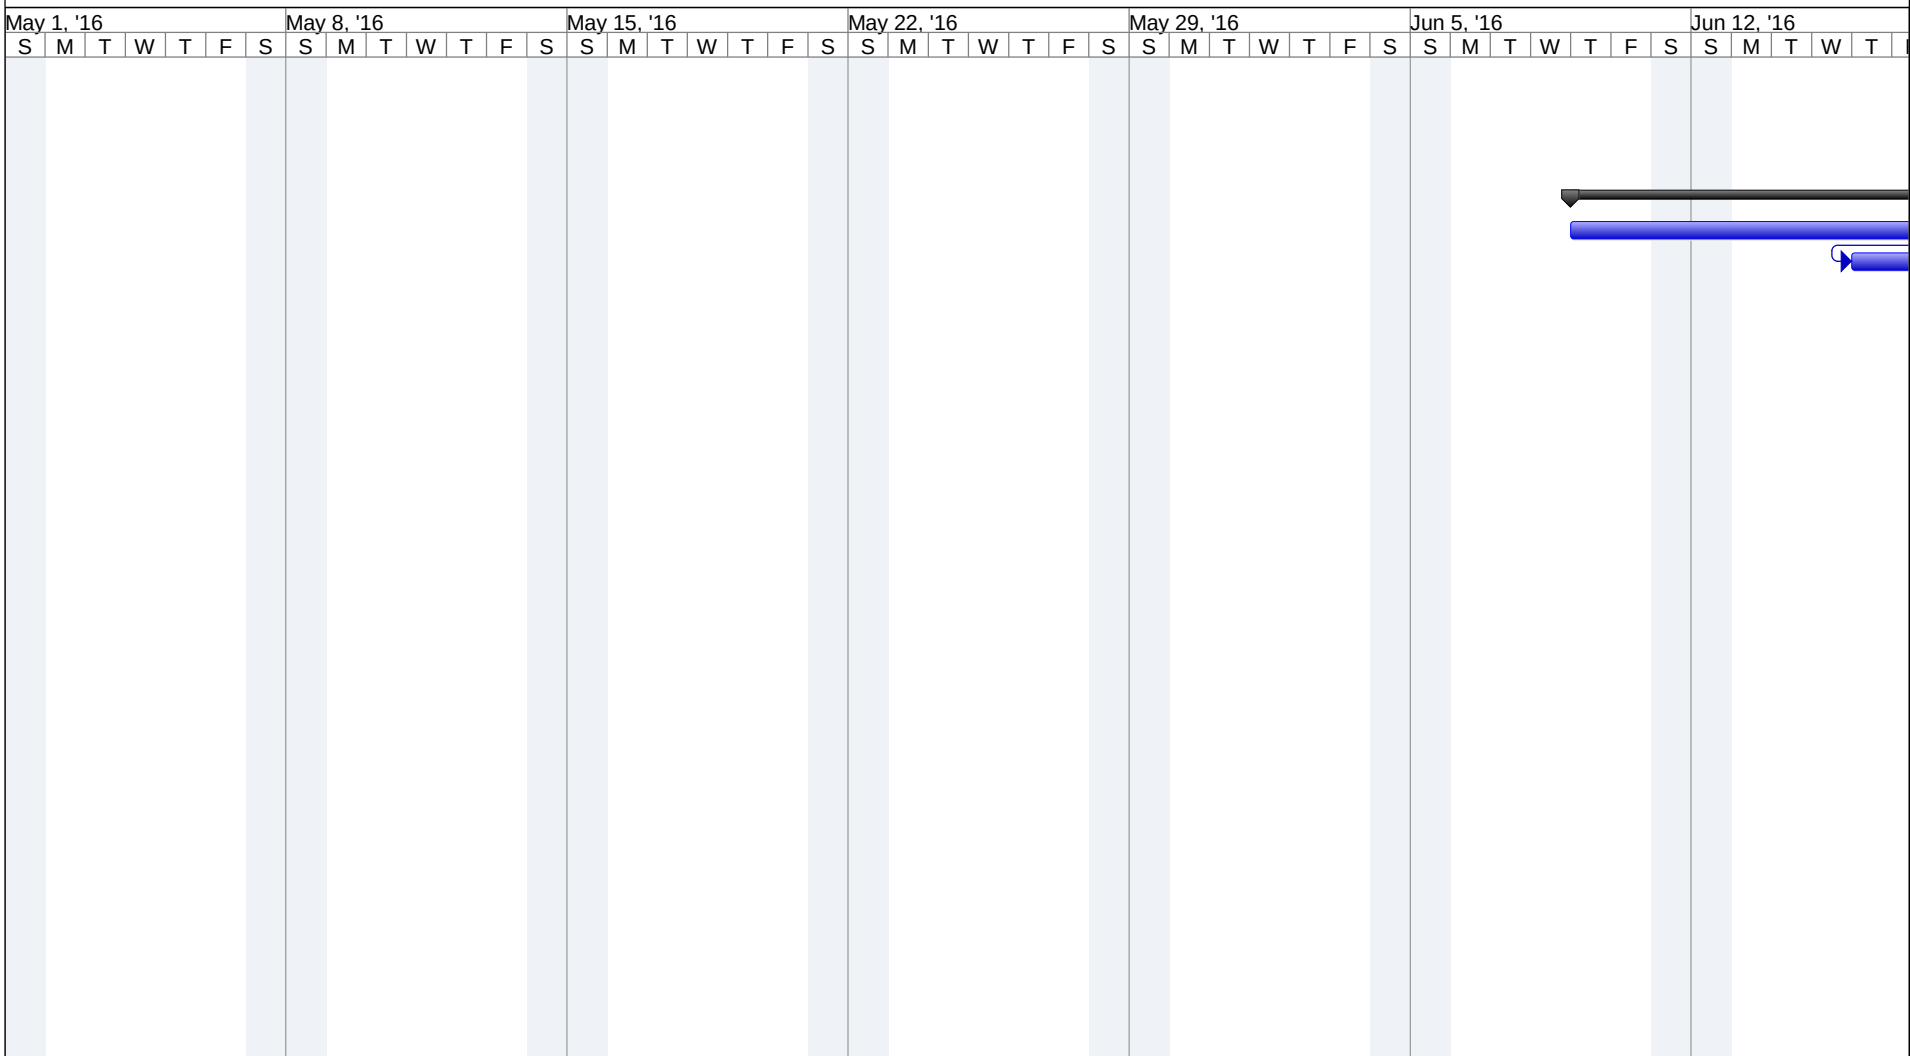

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

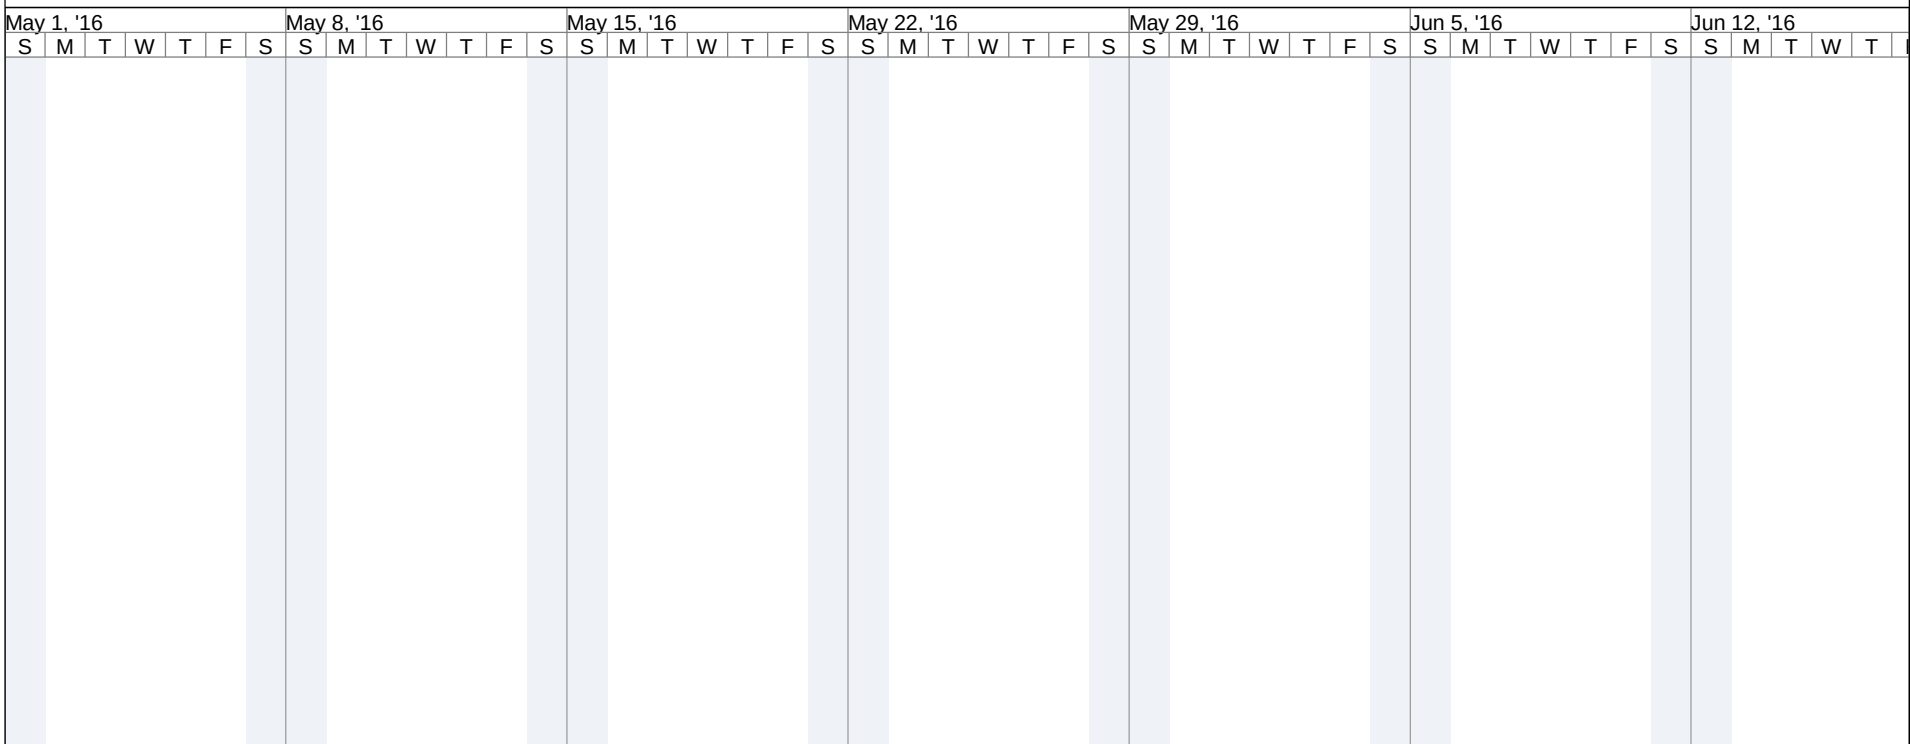

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

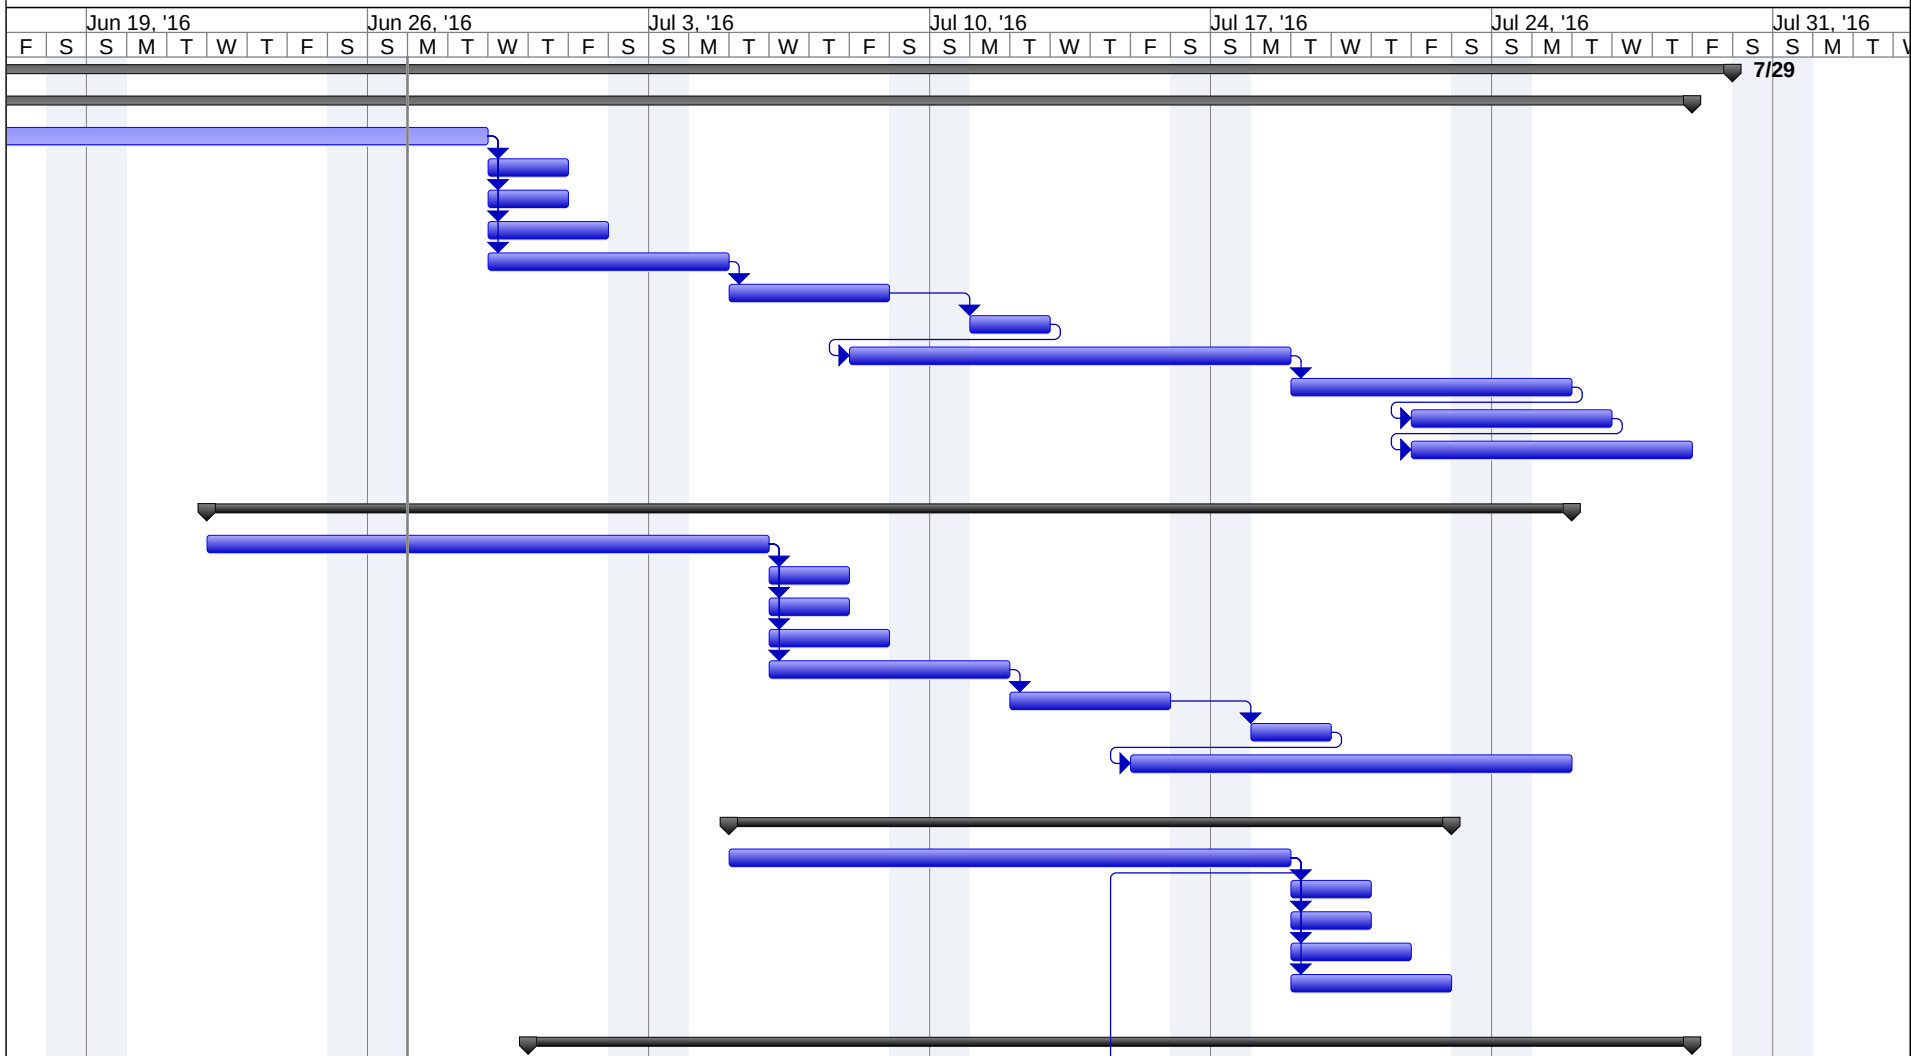

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

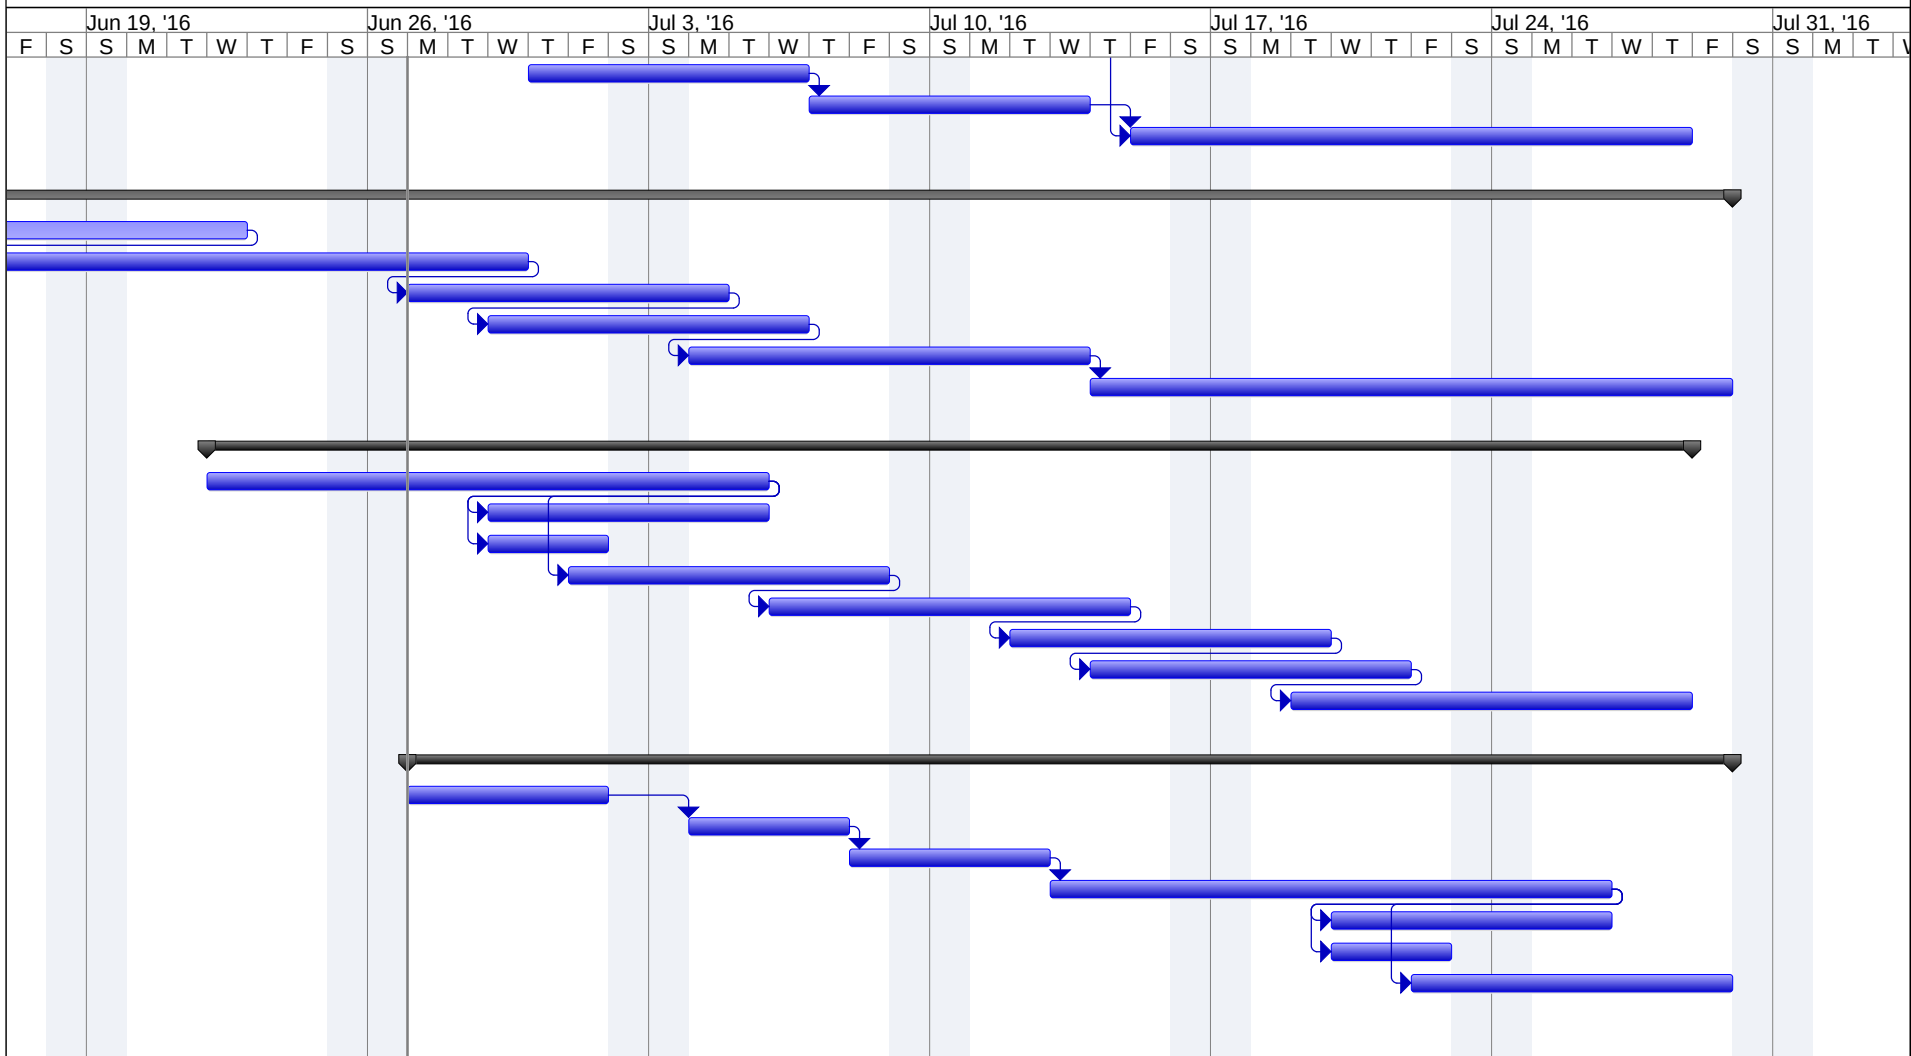

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

Hadley 3 Week Schedule (Interior)
6-27-2016

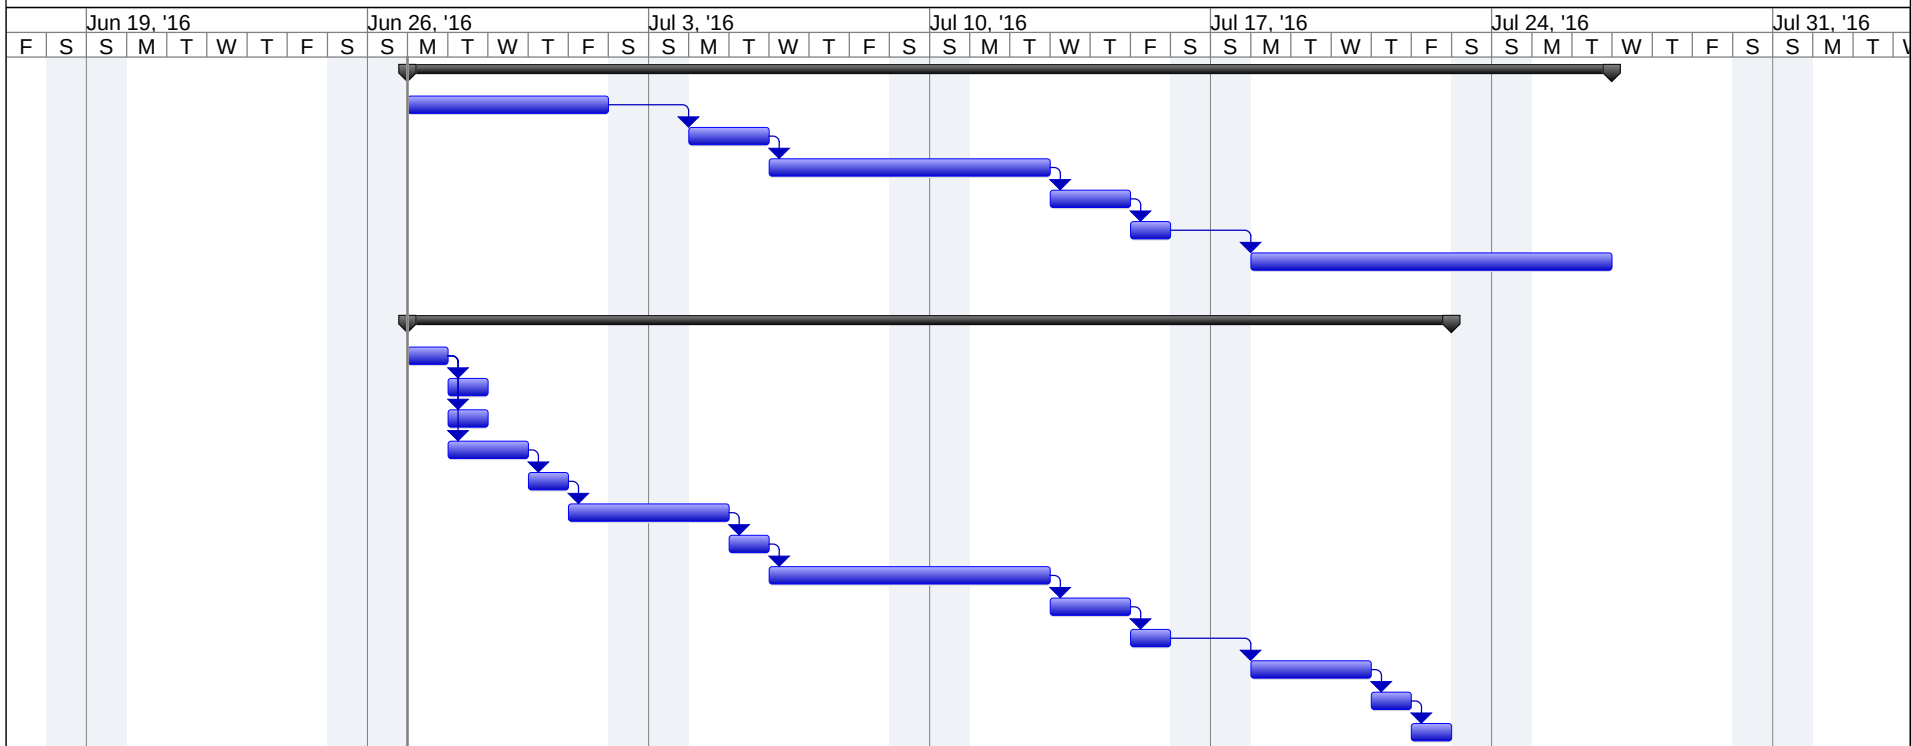

Project: MI Finish 6-27p
Date: Mon 6/27/16

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	
